

**Contractor: Josh King Excavating**

Plant: Beaver Dam



Size: 28" x 96"

Rim to Invert: 5.69'

Floor Height: 6"


Slack: 0.28"

REINFORCING PER ASTM A615 (GRADE 60).  
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.  
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

4) LINTEL BAR SLOT n/n - 7"x1"


0 lb  
10390 lb  
0 lb  
0 lb  
0 lb  
0 lb  
0 lb

Structure Total: 10390 lb

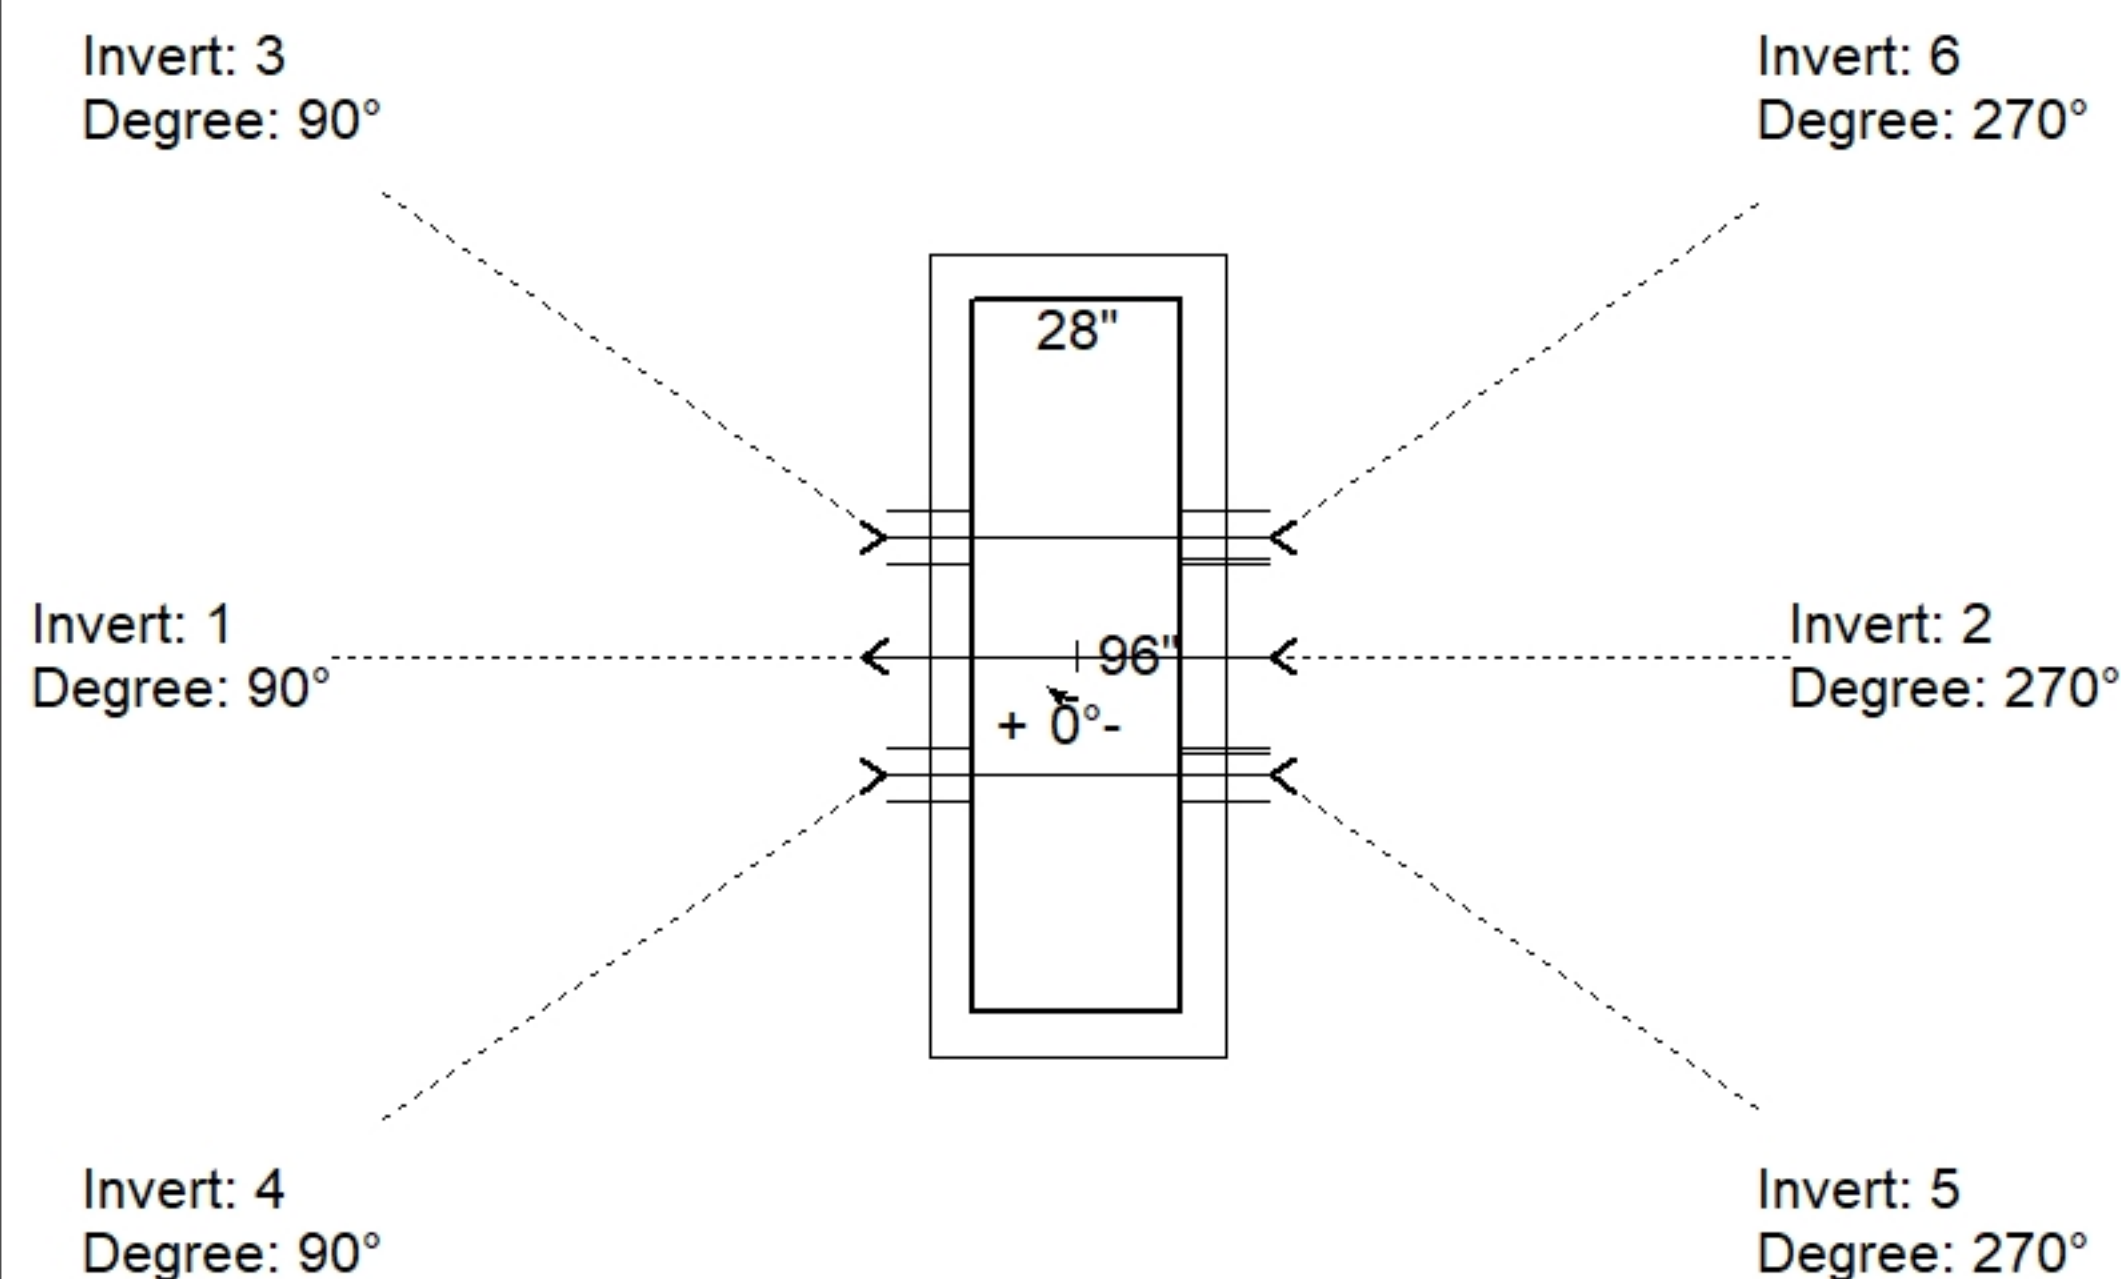

| Position | Elev     | Angle | Pipe                    | Pipe OD | Hole    | Connector             | Up ( _) | Ref |
|----------|----------|-------|-------------------------|---------|---------|-----------------------|---------|-----|
| Rim      | 670.45'  |       |                         |         |         |                       |         |     |
| Reducer  |          |       |                         |         |         |                       |         |     |
| Invert 1 | 664.76'  | 90°   | 24" RCP B WALL          | 30"     | 32"     | Hole 32               | 0"      | P1  |
| Invert 2 | 665.26'  | 270°  | 18" RCP B WALL          | 23"     | 26"     | Hole 26               | 6.5"    | P1  |
| Invert 3 | 669.844' | 90°   | 7" x 1" LINTEL BAR SLOT | 7" x 1" | 7" x 1" | LINTEL BAR SLOT 7"x1" | 64.004" | P1  |
| Invert 4 | 669.844' | 90°   | 7" x 1" LINTEL BAR SLOT | 7" x 1" | 7" x 1" | LINTEL BAR SLOT 7"x1" | 64.004" | P1  |
| Invert 5 | 669.844' | 270°  | 7" x 1" LINTEL BAR SLOT | 7" x 1" | 7" x 1" | LINTEL BAR SLOT 7"x1" | 64.004" | P1  |
| Invert 6 | 669.844' | 270°  | 7" x 1" LINTEL BAR SLOT | 7" x 1" | 7" x 1" | LINTEL BAR SLOT 7"x1" | 64.004" | P1  |
| Invert 7 |          |       |                         |         |         |                       |         |     |
| Invert 8 |          |       |                         |         |         |                       |         |     |

### Default - Interior Dimensions

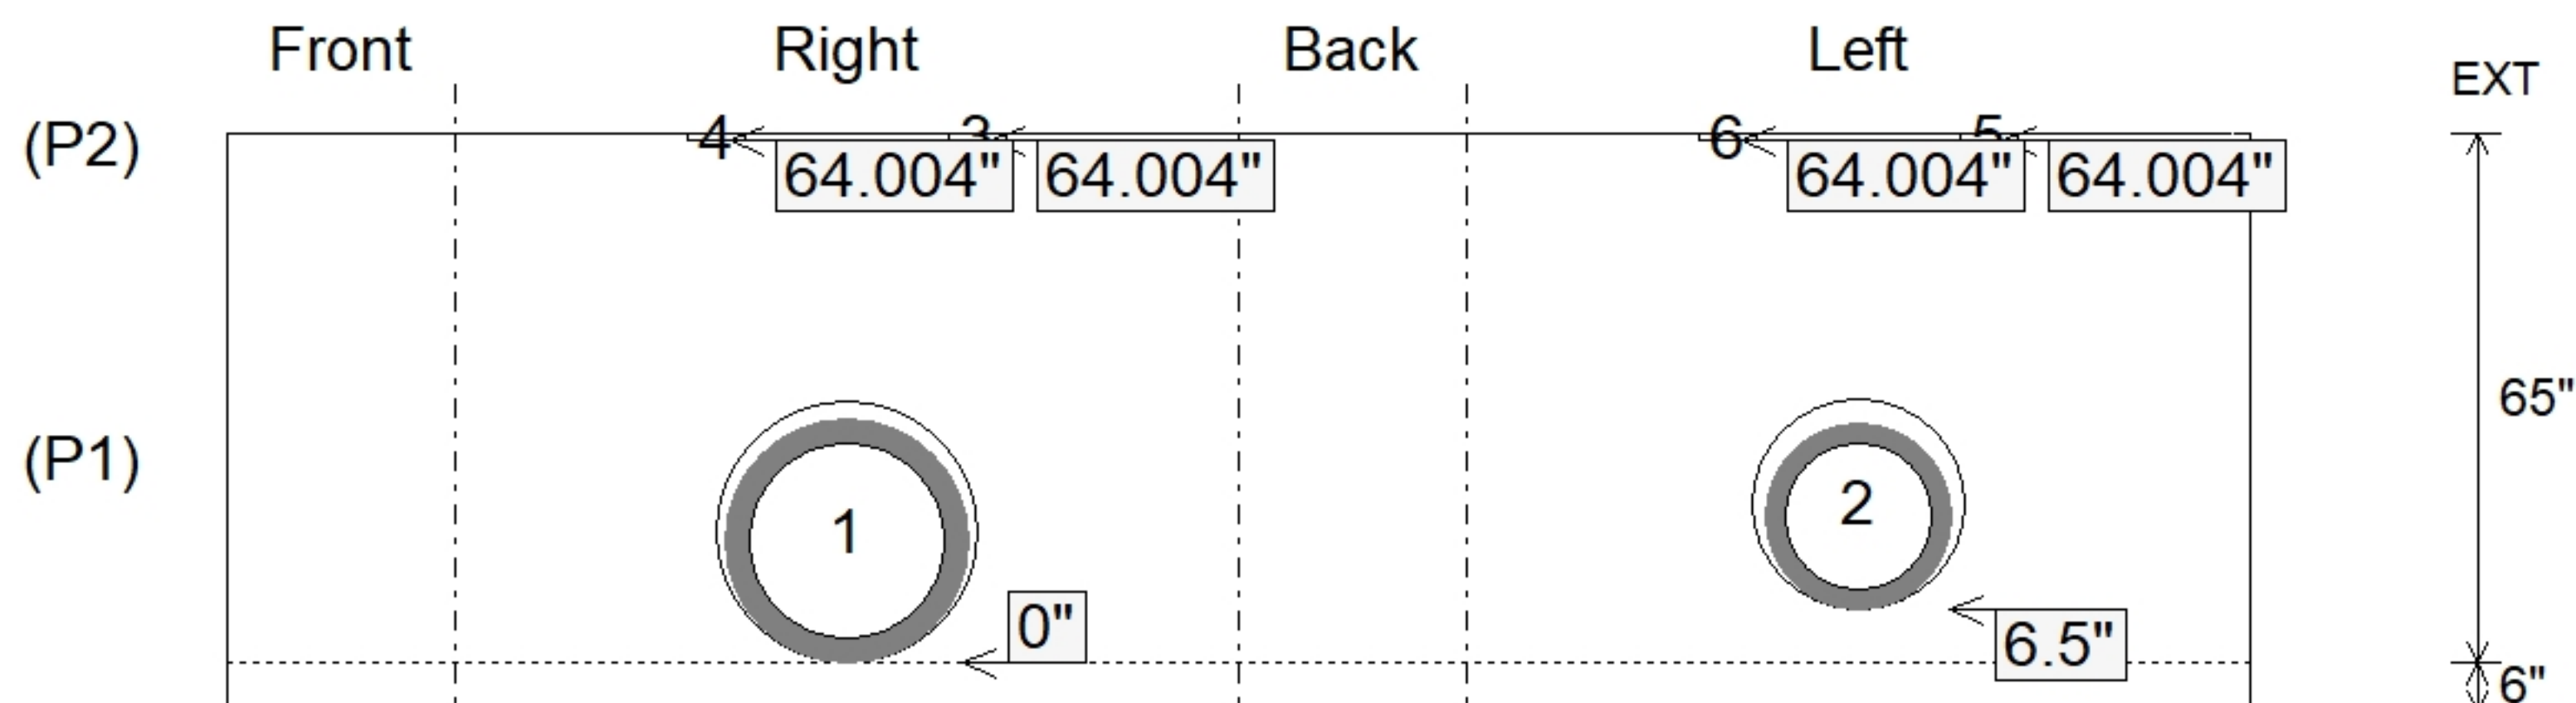

Submittal Drawing  
8/5/2026 8:19:41 AM

SUBMITTAL  
APPROVED BY:
