

Job Name: 25-2397 Sandy Springs Sec. 2
Job Location: Elizabethtown, KY 42701
Contractor: Dirt Works Unlimited, LLC.

Plant: 100

7/9/2026 2:52:15 PM

Tech: Jared - A

PC: Thomas Ryan



Structure ID: S


P2 BX060060-08LD08-S

BX FLAT LID 8inW w/24"x36" HOLE

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 60" x 60" - BX FLAT LID 8inW w/24"x36" HOLE - 8"
P1) 60" x 60" - BOX BASE 8inW, 8inF, Variable Ht - 58"
1) SECONDARY POUR - WALLS
1) CASTING - HOE 525 SET (F/G/H)
1) 60" x 60" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 54
1) Hole - 44
1) Hole - 18
1) Hole - 50

Structure Total:

- 0 lb
3297 lb
10421 lb
0 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
14160 lb
- Structure Notes:**
PLAN LABEL: S
1. HOE 525 SET (F/G/H) PROVIDE BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB
- WALLS (As .31) #5 BARS 12" C.C.E.W.
- WALLS (As .31) #5 BARS 12" C.C.E.W.
5. PLEASE VERIFY THE REQUIRED TOP OF FRAME ELEVATION AS THE STRUCTURE SCHEDULE AND PLAN VIEW VALUES DIFFER. SCHEDULE VALUES WERE USED IN THIS SUBMITTAL.

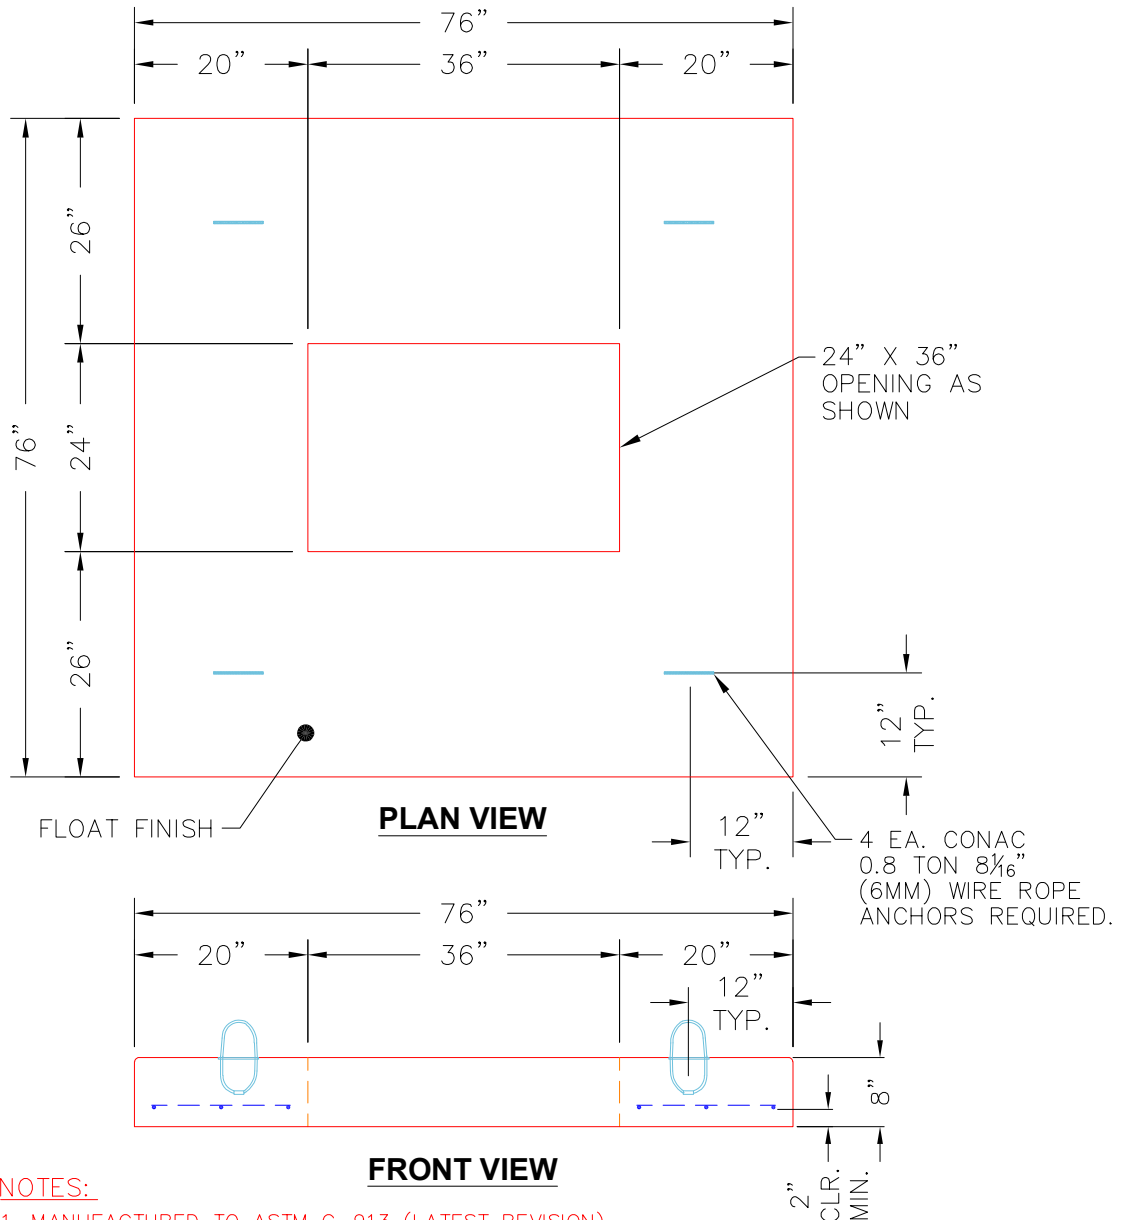

- NOTES:**
1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
 2. CONCRETE: 4,000 PSI AT 28 DAYS.
 3. REINFORCING: #5 BAR @ 8" O.C. E.W. (GRADE 60).
 4. WEIGHT: 3,297 LBS.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 3297 lb
Volume (Net): 0.84cu.yd
