




**Structure Notes:** PLAN LABEL: V

1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
  - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
  - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.


P2) 24" x 36" - CASTING HEIGHT - 6"  
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33"  
1) CASTING - HOE 525 SET (F/G/H)  
1) 24" x 36" - Conseal CS-102 1.00"  
1) Hole - 18

0 lb  
4593 lb  
442 lb  
0 lb  
0 lb


Structure Total: 5035 lb

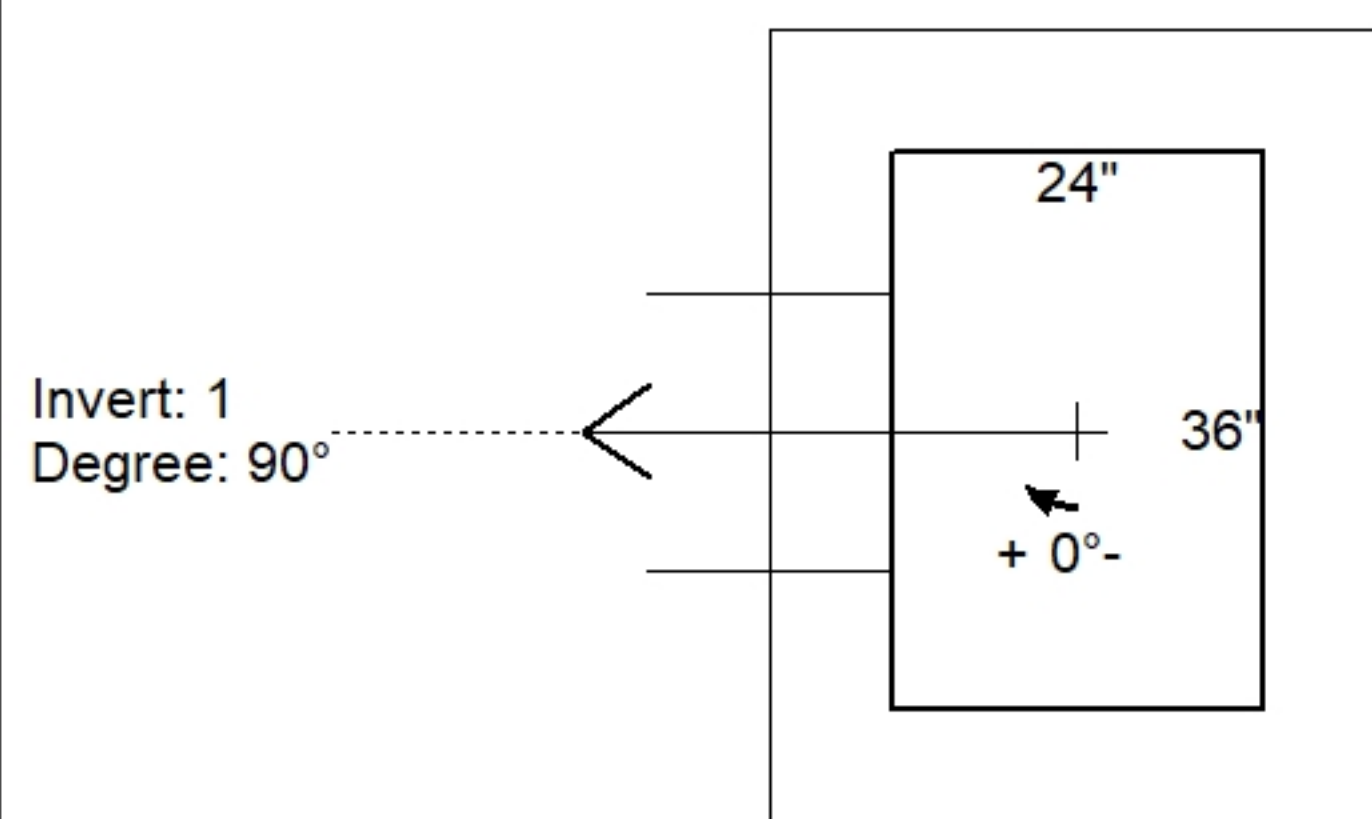

| Position | Elev    | Angle | Pipe           | Pipe OD | Hole | Connector | Up (↓) | Ref |
|----------|---------|-------|----------------|---------|------|-----------|--------|-----|
| Rim      | 691.82' |       |                |         |      |           |        |     |
| Reducer  |         |       |                |         |      |           |        |     |
| Invert 1 | 688.56' | 90°   | 12" RCP B WALL | 16"     | 18"  | Hole 18   | -2"    | P1  |
| Invert 2 |         |       |                |         |      |           |        |     |
| Invert 3 |         |       |                |         |      |           |        |     |
| Invert 4 |         |       |                |         |      |           |        |     |
| Invert 5 |         |       |                |         |      |           |        |     |
| Invert 6 |         |       |                |         |      |           |        |     |
| Invert 7 |         |       |                |         |      |           |        |     |
| Invert 8 |         |       |                |         |      |           |        |     |

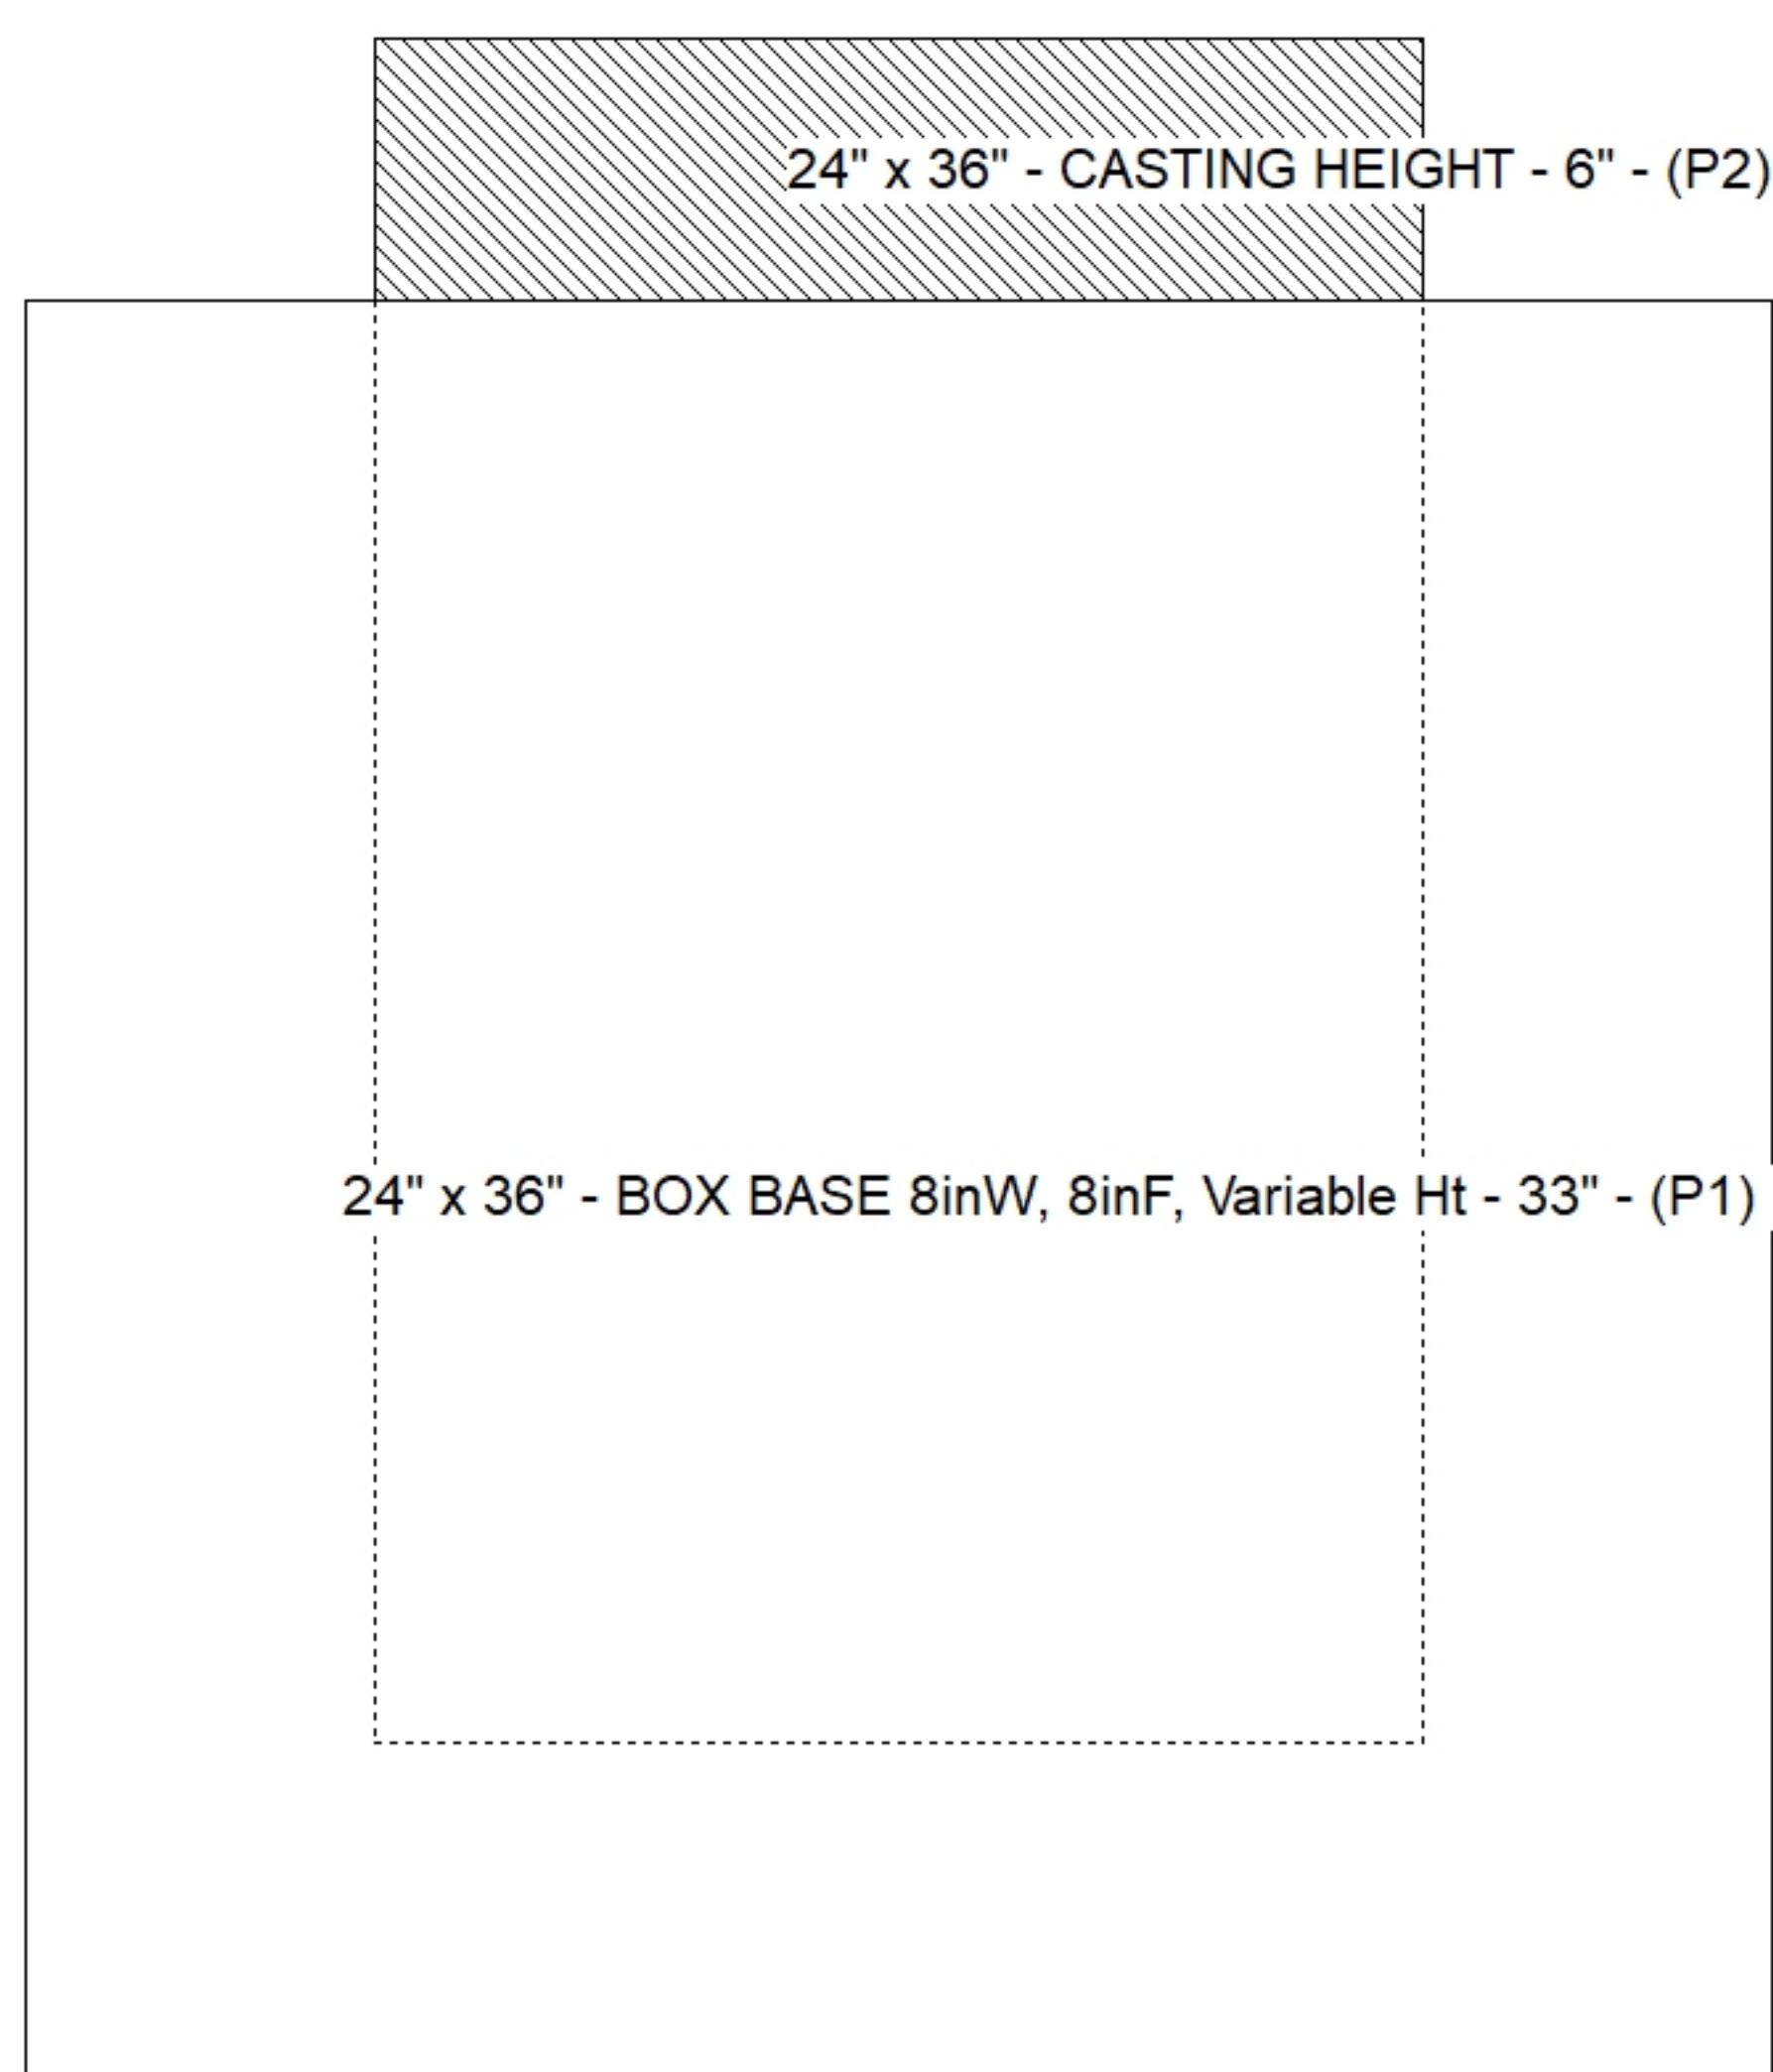

### Default - Interior Dimensions

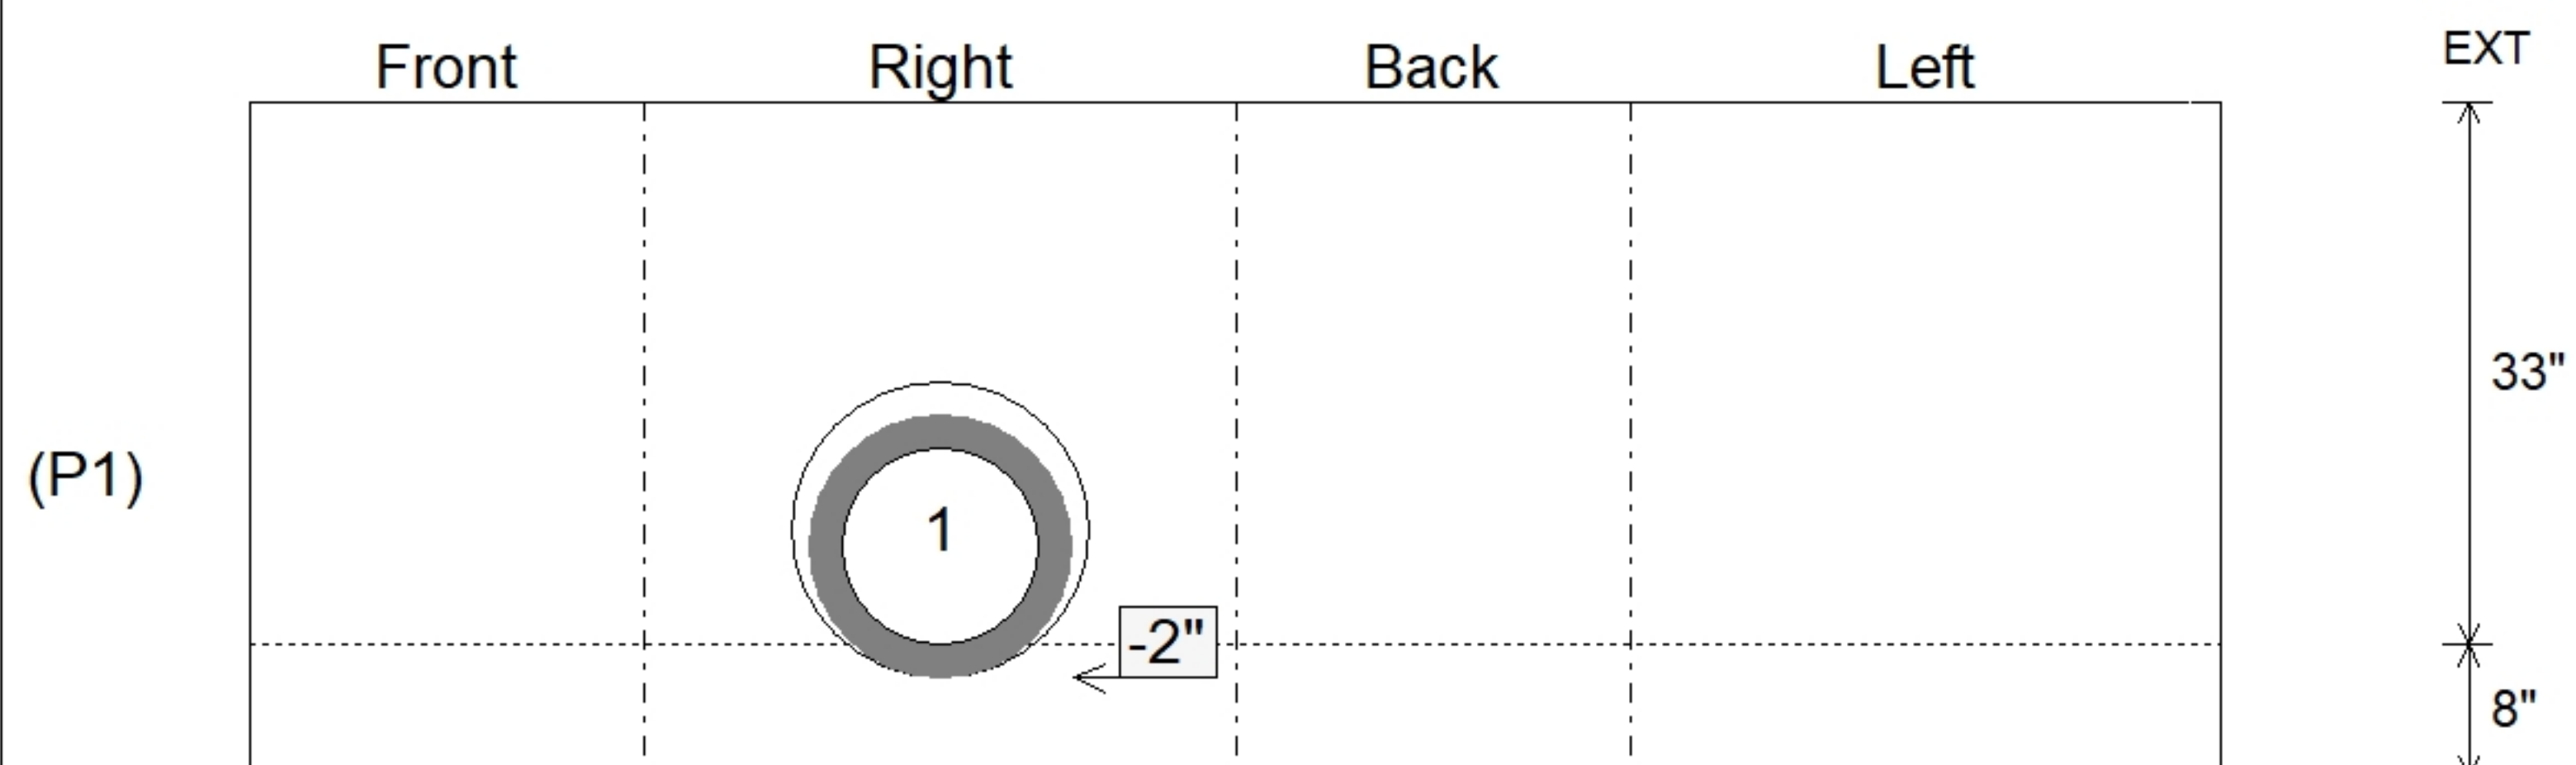

SUBMITTAL  
APPROVED BY:
