


Structure Notes: PLAN LABEL: X

1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.


P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33"
1) CASTING - HOE 525 SET (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 18

0 lb
4593 lb
442 lb
0 lb
0 lb


Structure Total: 5035 lb

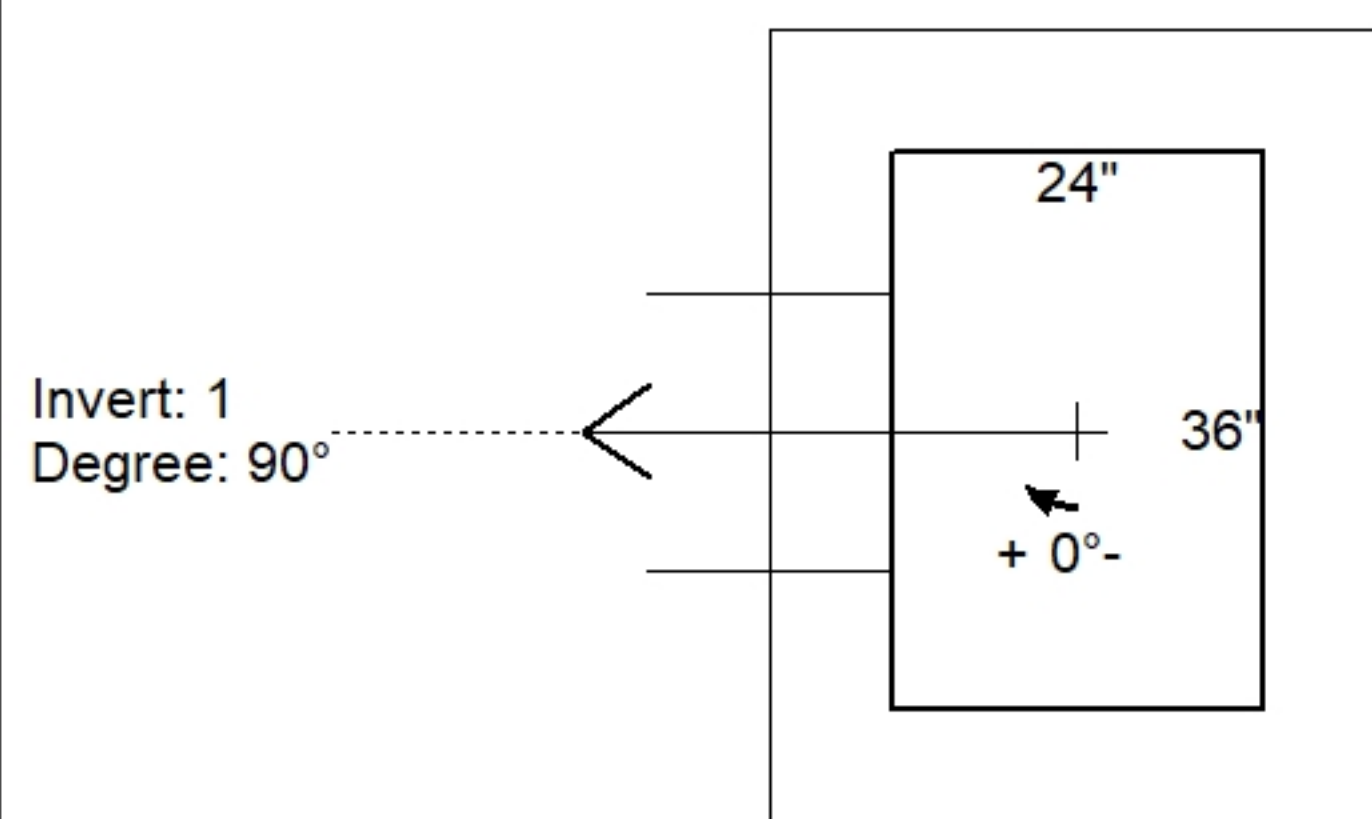

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	690.82'							
Reducer								
Invert 1	687.56'	90°	12" RCP B WALL	16"	18"	Hole 18	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

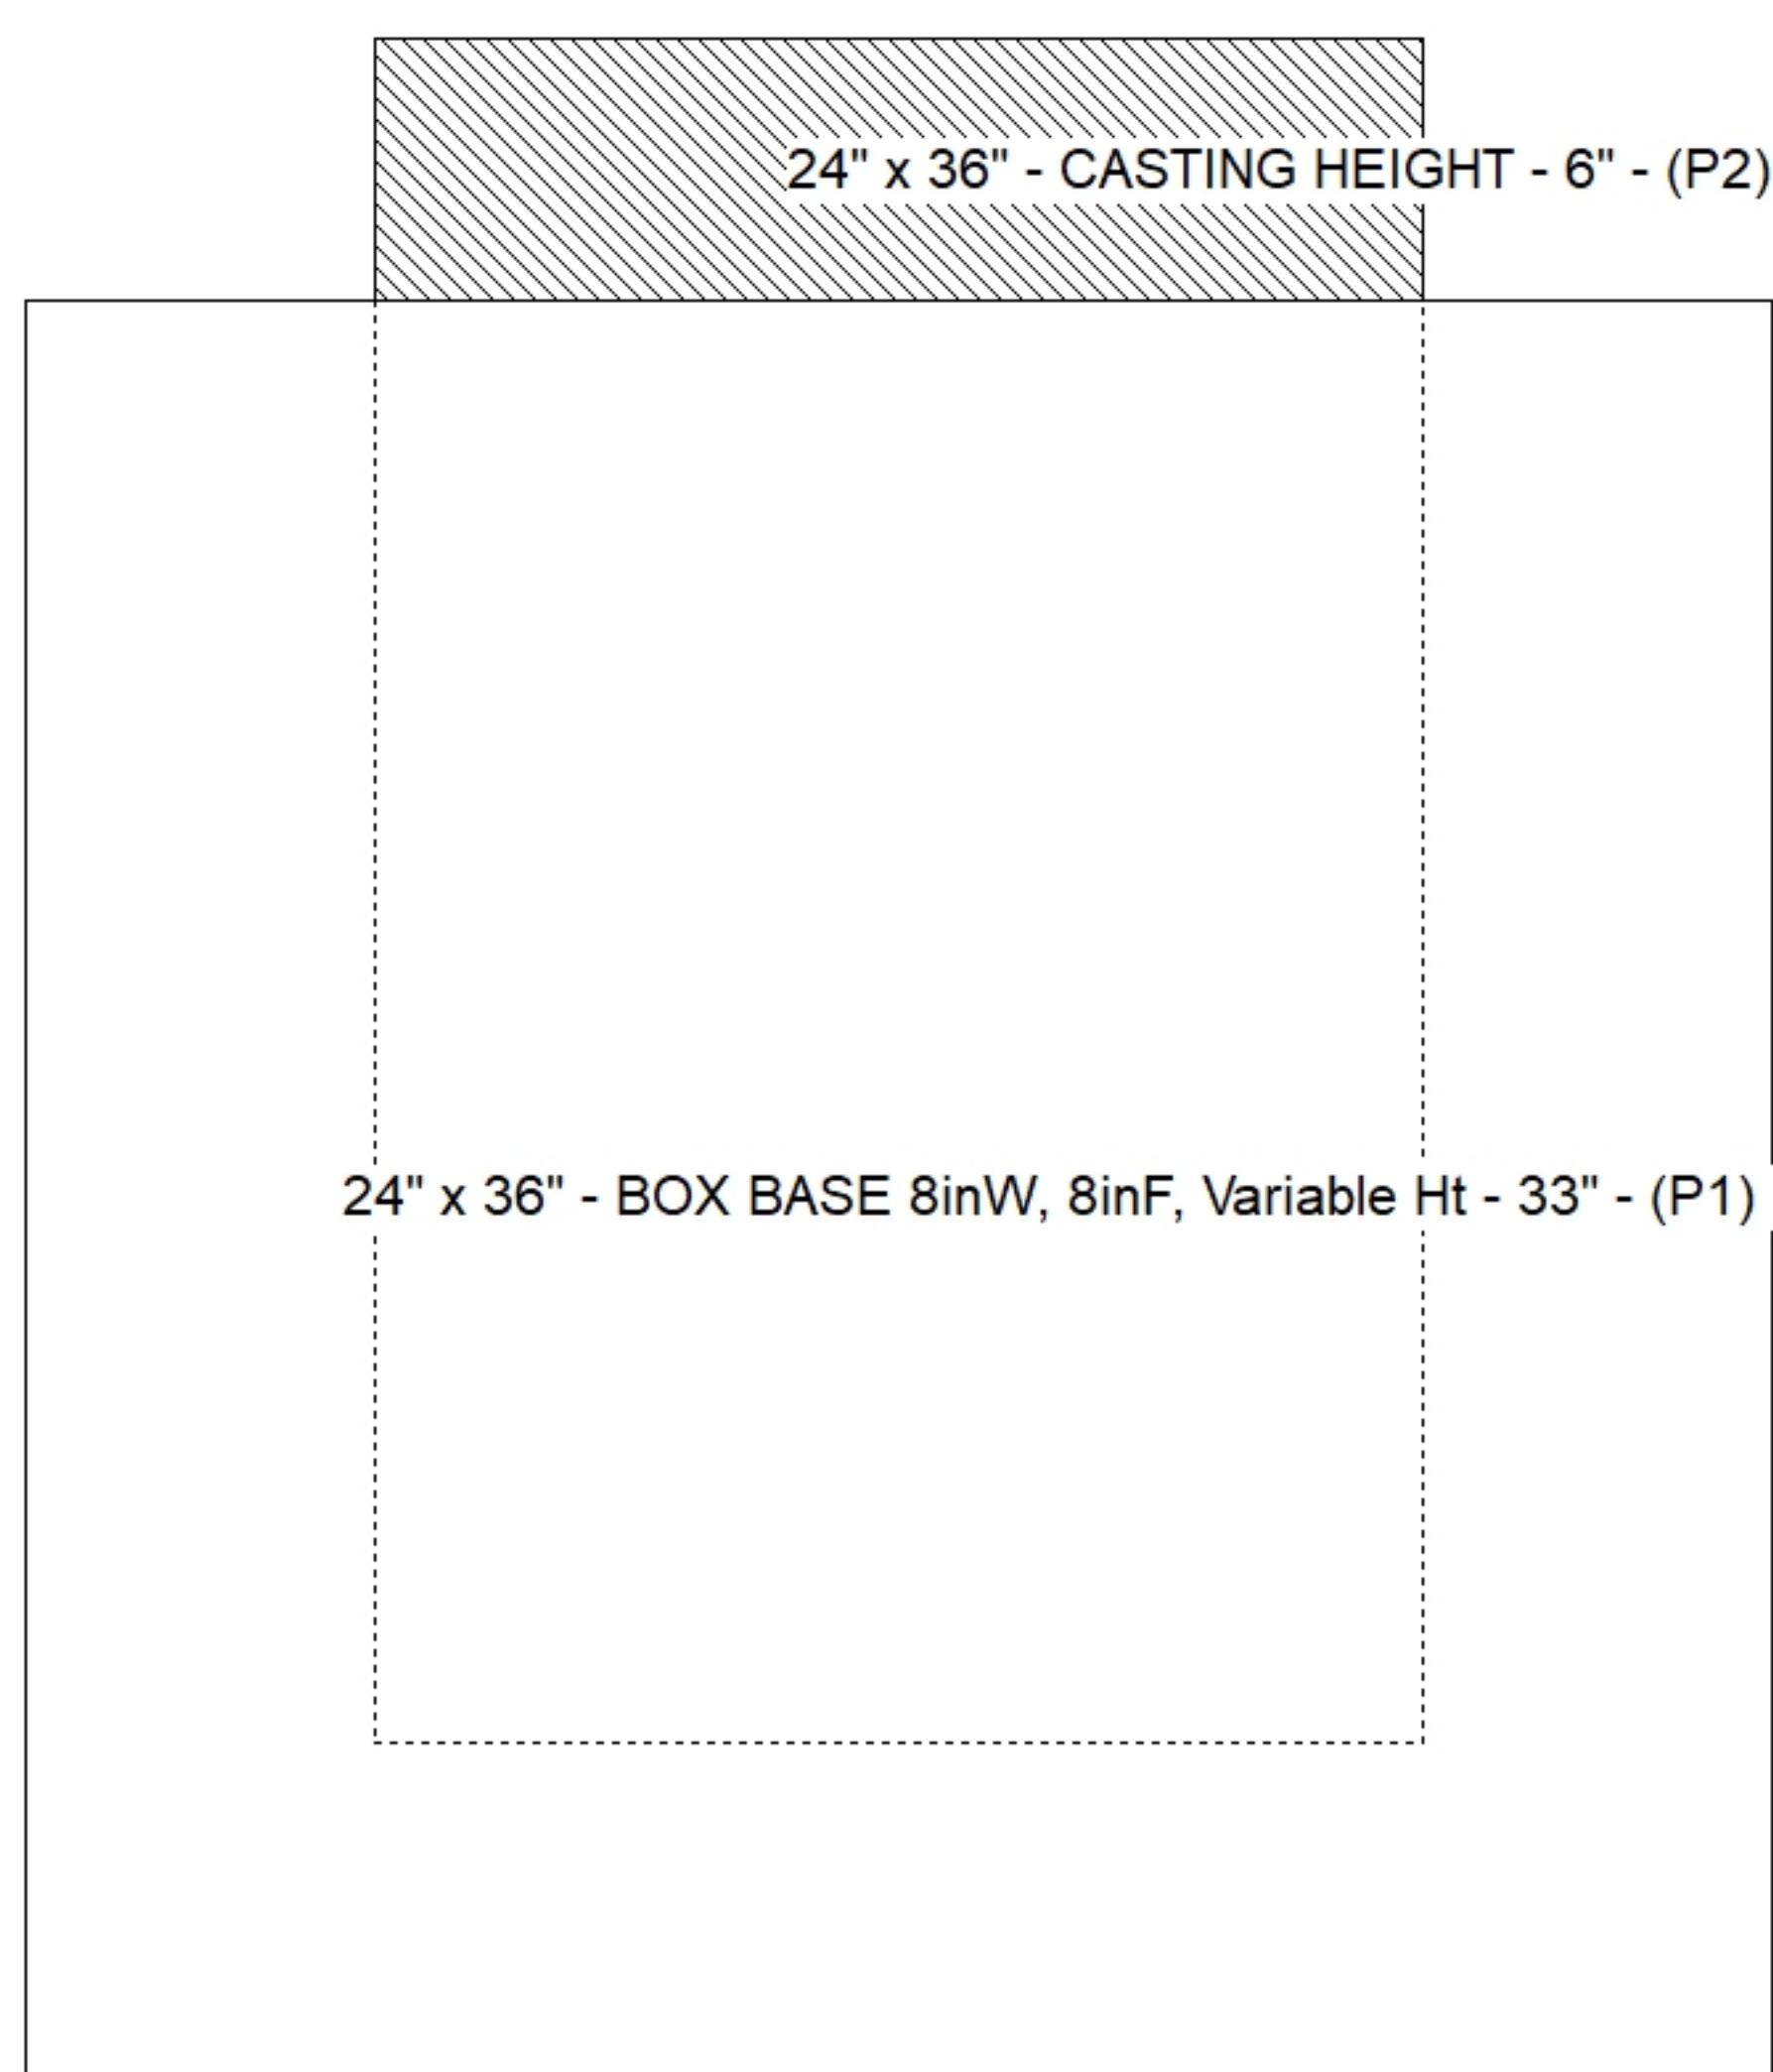

Default - Interior Dimensions

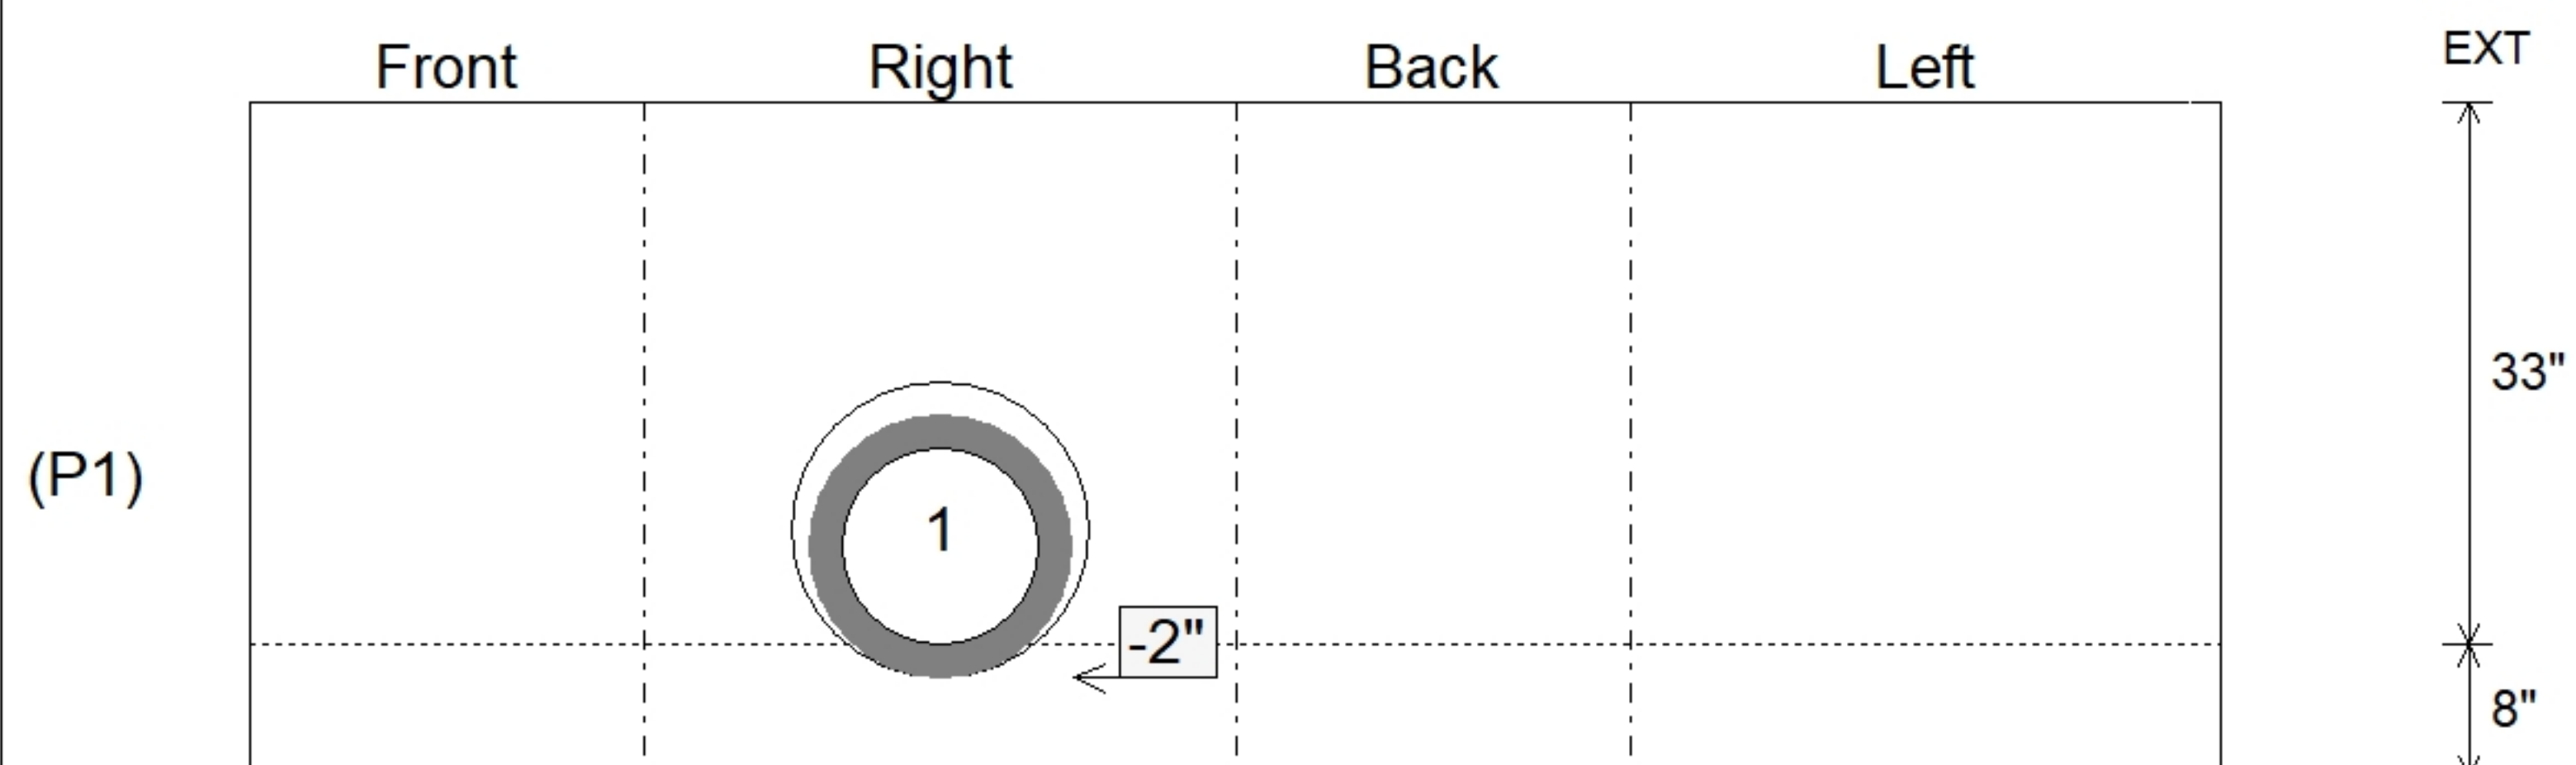

SUBMITTAL
APPROVED BY:
