

Contractor: Byard Construction, LLC

Plant: 100



Floor (Bot): 414.863'
Overall Height: 15.5'
Slack: 0.92"


0 lb
3116 lb
4192 lb
3353 lb
2911 lb
1440 lb
0 lb
0 lb
0 lb
250 lb
0 lb
0 lb
16 lb
0 lb

Invert: 2
Degree: 151°

Invert: 1
Degree: 0°

Step: 255.5°

+ 0° -

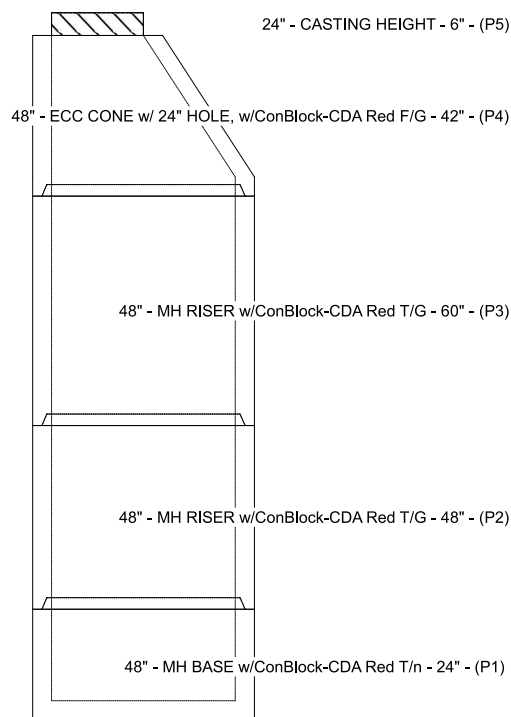

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	430.44'							
Reducer								
Invert 1	415.53'	0°	8" PVC SDR26	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	415.63'	151°	8" PVC SDR26	8.5"	12"	PSX 12-08 NYLO	1.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:
