


Job Name: 25-2422 - Woodland Springs Section 3 (Sanitary) Job Location: Clarksville, TN Contractor: Byard Construction, LLC					Plant: 100 5/14/2026 2:16:57 PM		Tech: Jared - A PC: A. Chambers						
Structure ID: A-9													
P2 MH048RS36CDARED				MH RISER w/ConBlock-CDA Red T/G									
P4) 24" - CASTING HEIGHT - 6" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 9) MH Step ML-10-TDS-NCR - 10"						0 lb 3116 lb 2515 lb 3330 lb 1440 lb 0 lb 0 lb 0 lb 250 lb 0 lb 0 lb 16 lb 0 lb ----- 10667 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CONBLOCK CDA RED ADMIXTURE REQUIRED 5. STEPS AT 269 DEGREES 6. JBS 1155 FRAME & COVER "SANITARY" SUPPLIED BY ICAST					
Rim: 462.12' Rim to Invert: 9.49' Slack: 1.88" Sump: 2" Step Position: 269°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

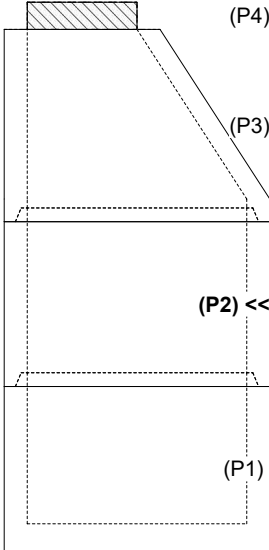


(P4)

(P3)

(P2) <<

(P1)


RIGHT-SIDE UP VIEW (int. dimensions)



Step: 269°
Horz: 112.625"

+ 0°-

INSIDE WALL DIMENSIONS



(P2)

0° 90° 180° 270° 360°

EXT

36"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 36" Height (Ext): 36"	Weight (Net): 2515 lb Volume (Net): 0.64cu.yd
----------------------------------	------------------------------------	--	--	--
