

Contractor: Byard Construction, LLC

TECH: Jared - A

Plant: 100



Size: 24" x 108"

Rim to Invert: 3.5'


Floor Height: 6"

Slack: 0"

1. (3)JBS 3080 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

0 lb

Structure Total: 8704 lb

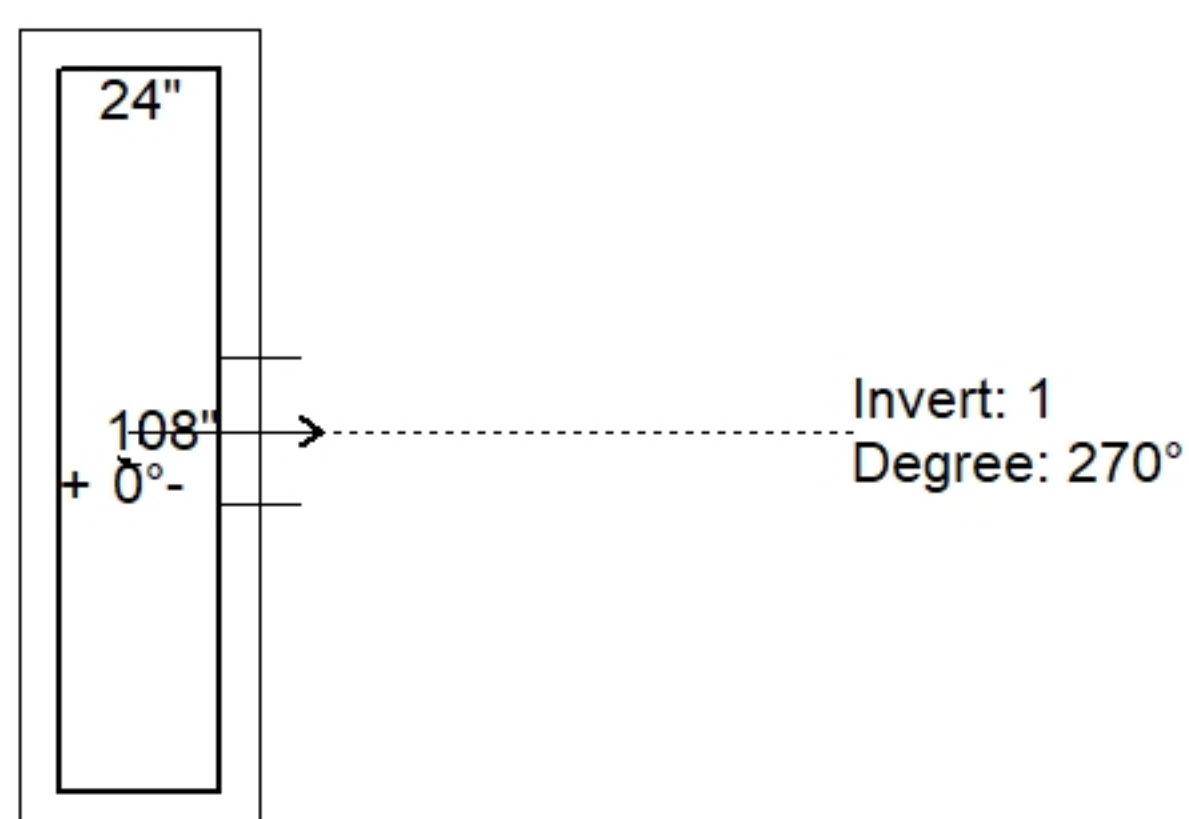


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	427.02'							
Reducer								
Invert 1	423.52'	270°	18" CMP	19"	22"	Hole 22	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 108" - CASTING HEIGHT - 6.5" - (P2)

24" x 108" - BOX BASE 6inW, 6inF, Variable Ht - 36" - (P1)

Default - Interior Dimensions

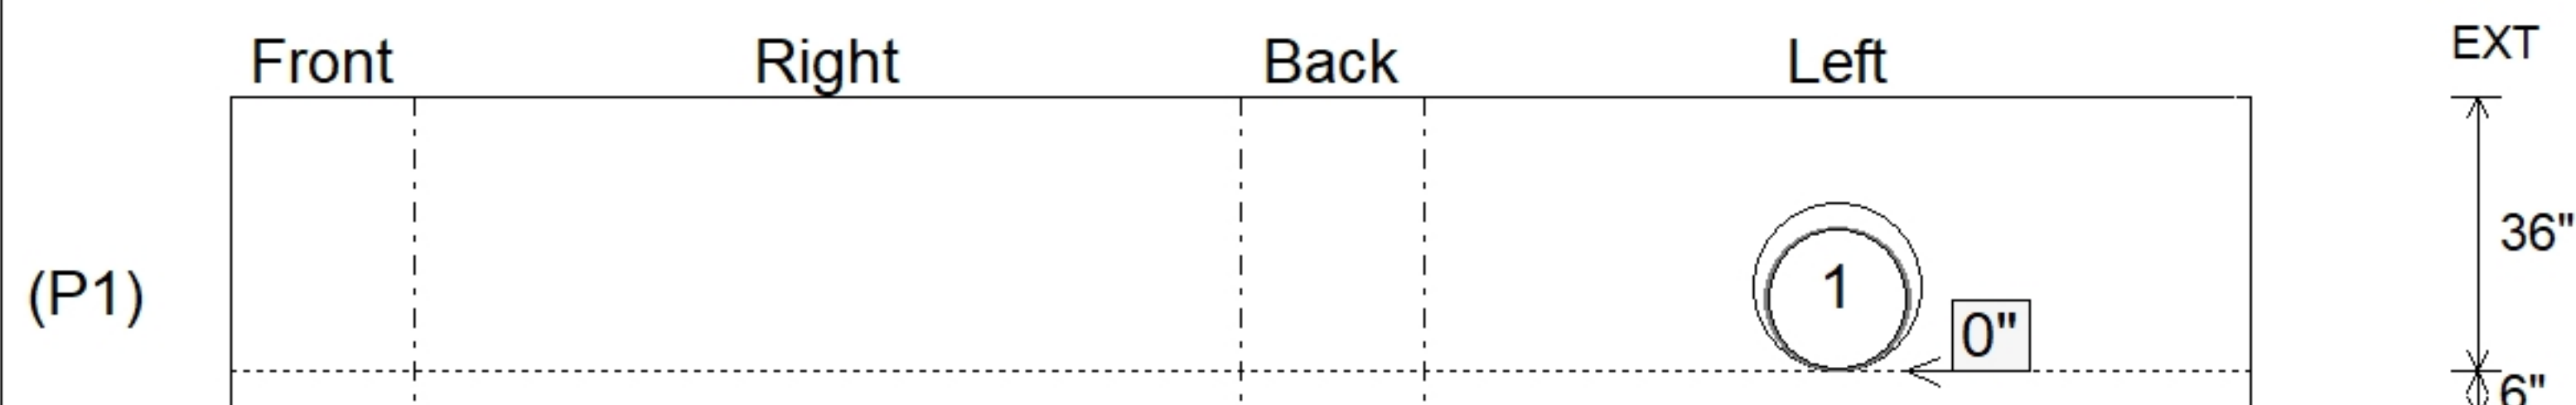

Submittal Drawing
9/9/2026 3:27:55 PM

SUBMITTAL
APPROVED BY:
