

Contractor: Byard Construction, LLC

TECH: Jared - A

Plant: 100



Slack: 0.24"


1. JBS 1155 F/C STORM PROVIDED BY ICST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole - 7"
P1) 48" - MH BASE Custom Ht - 33"
1) CASTING - JBS 1155 F/C STORM
1) 48" - Conseal CS-102 1.00"
2) Hole - 24



0 lb
1286 lb
3241 lb
250 lb
0 lb
0 lb

Structure Total: 4777 lb

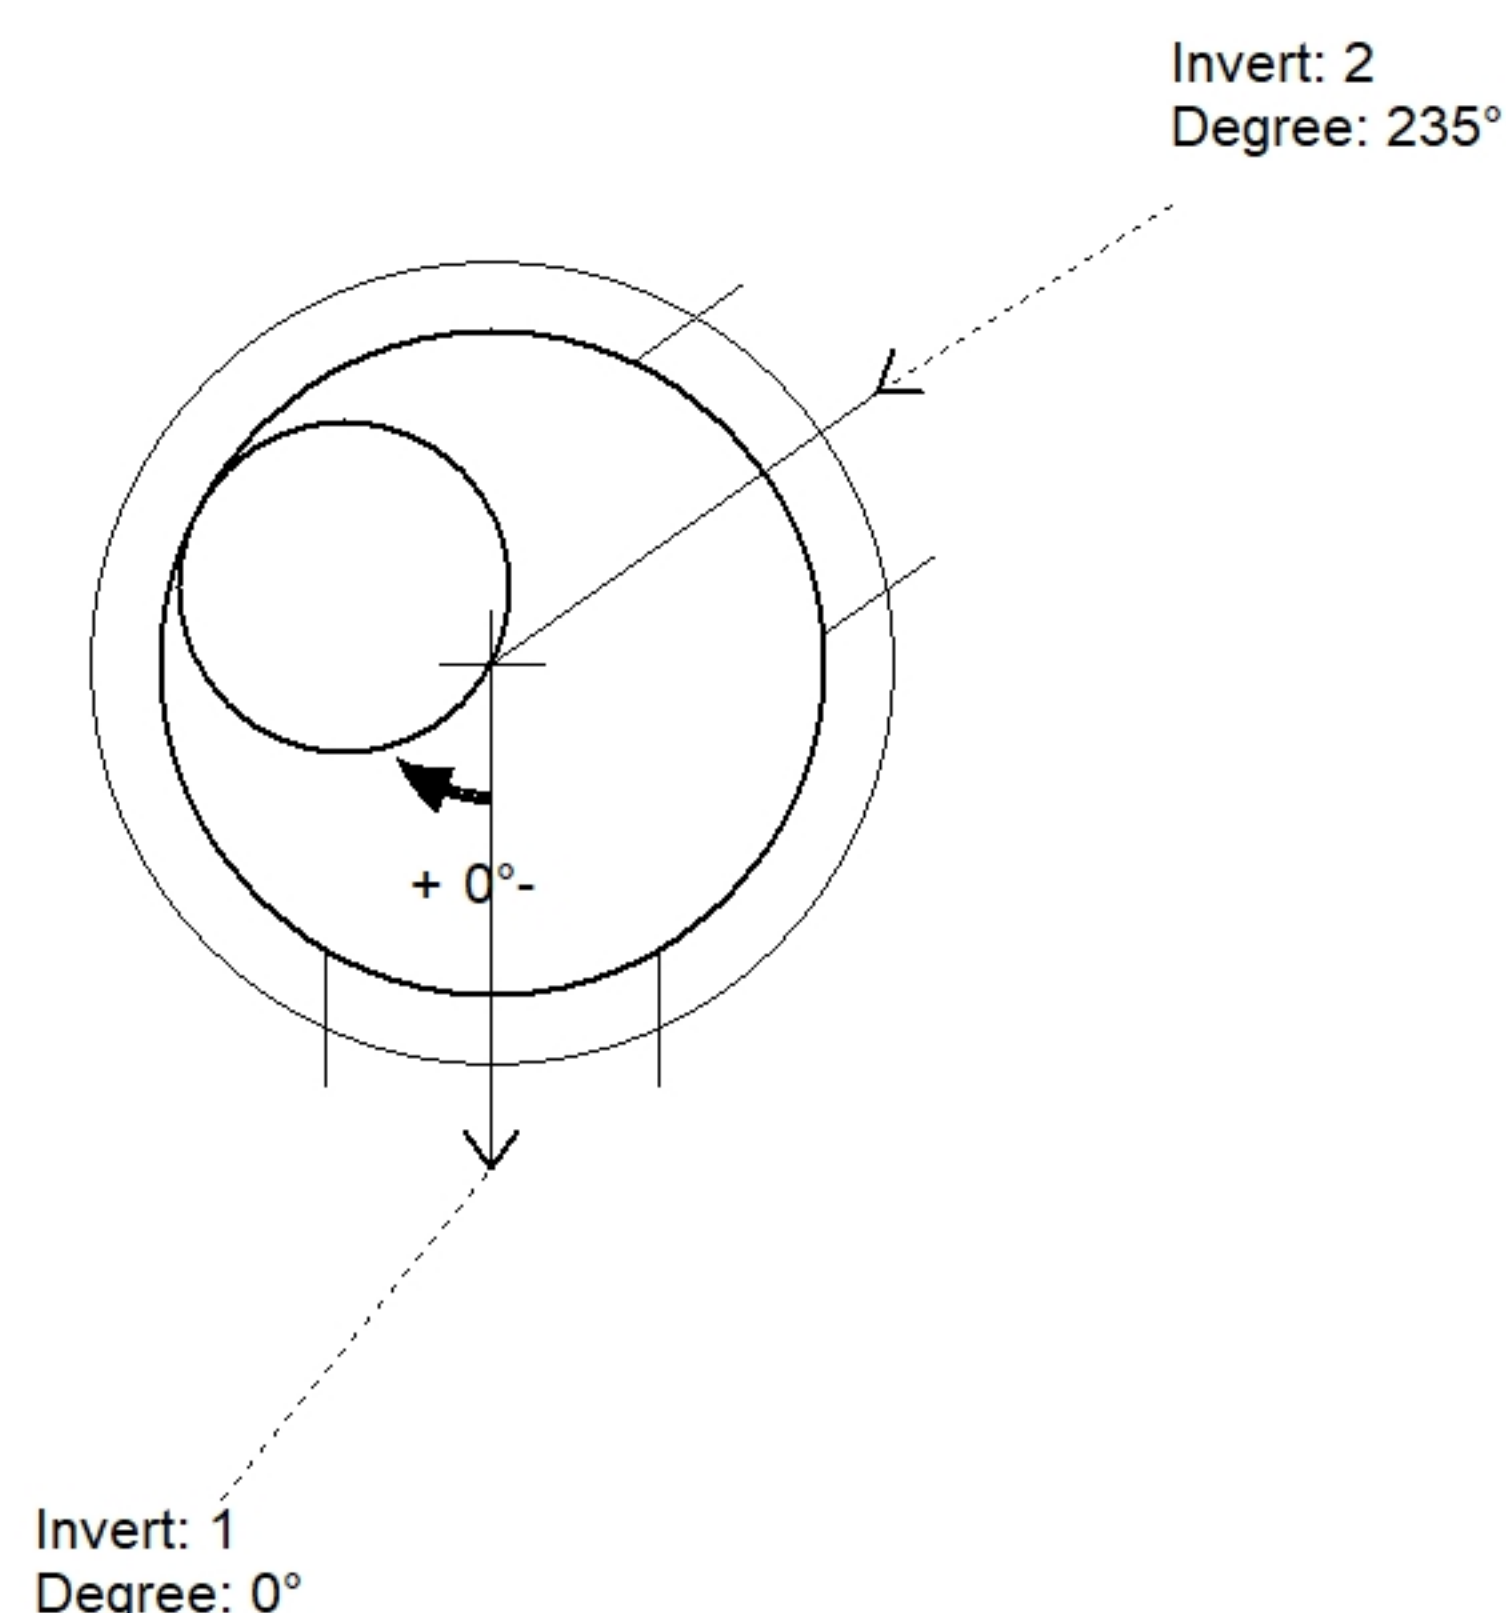

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	428.7'							
Reducer								
Invert 1	424.98'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2	425.08'	235°	18" HDPE	21.2"	24"	Hole 24	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

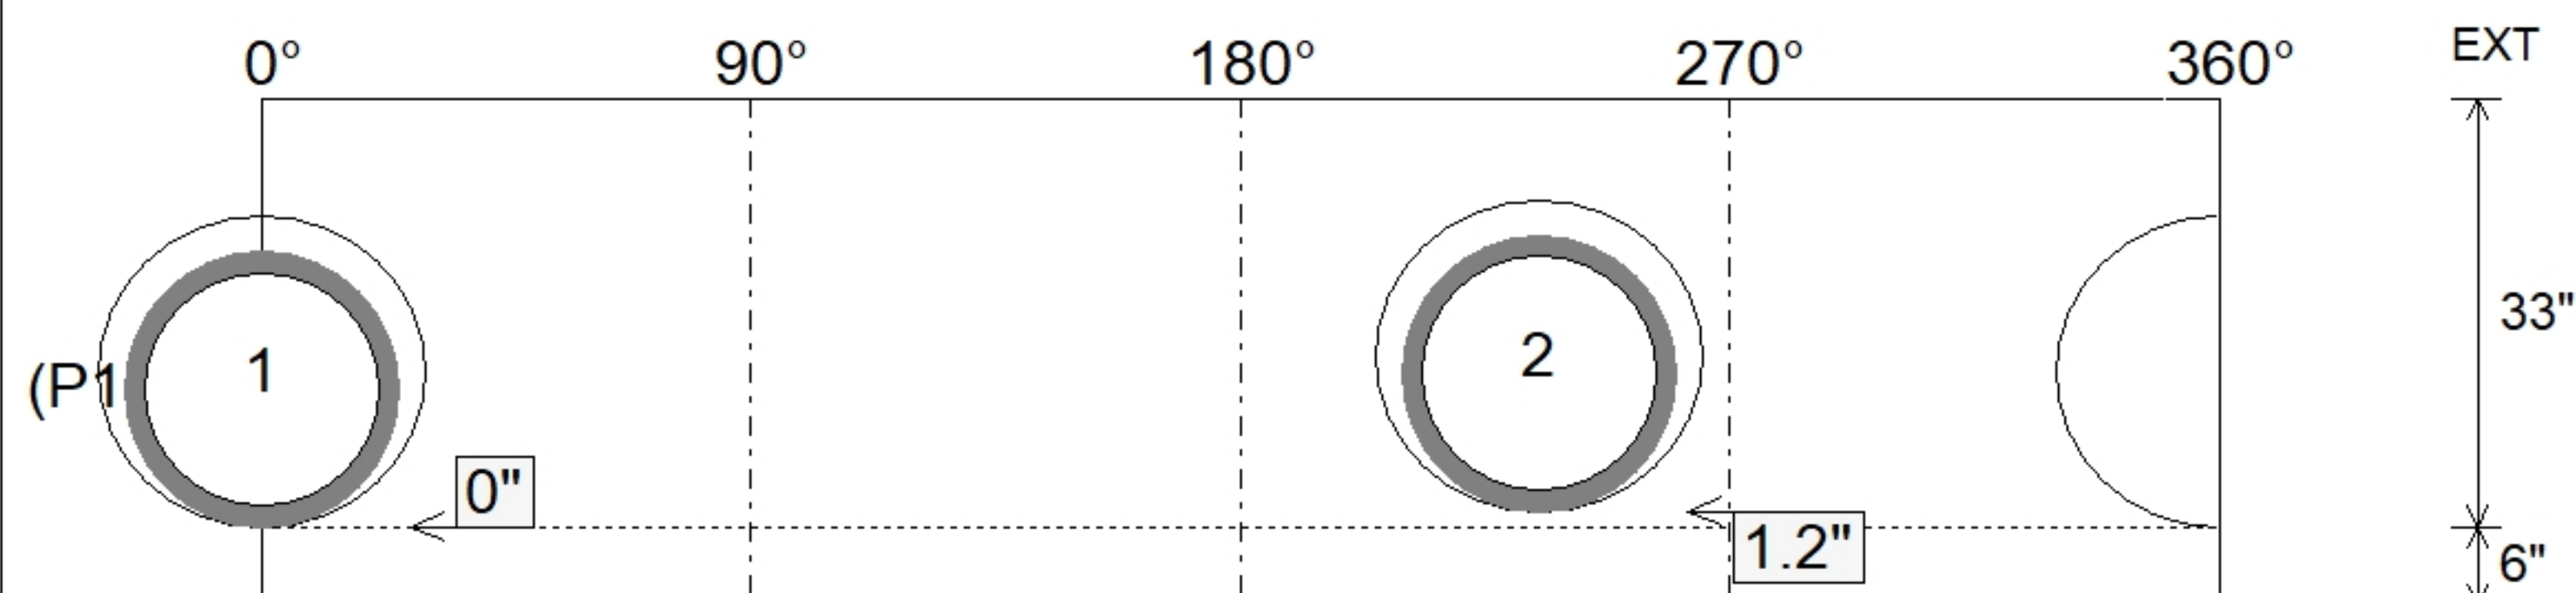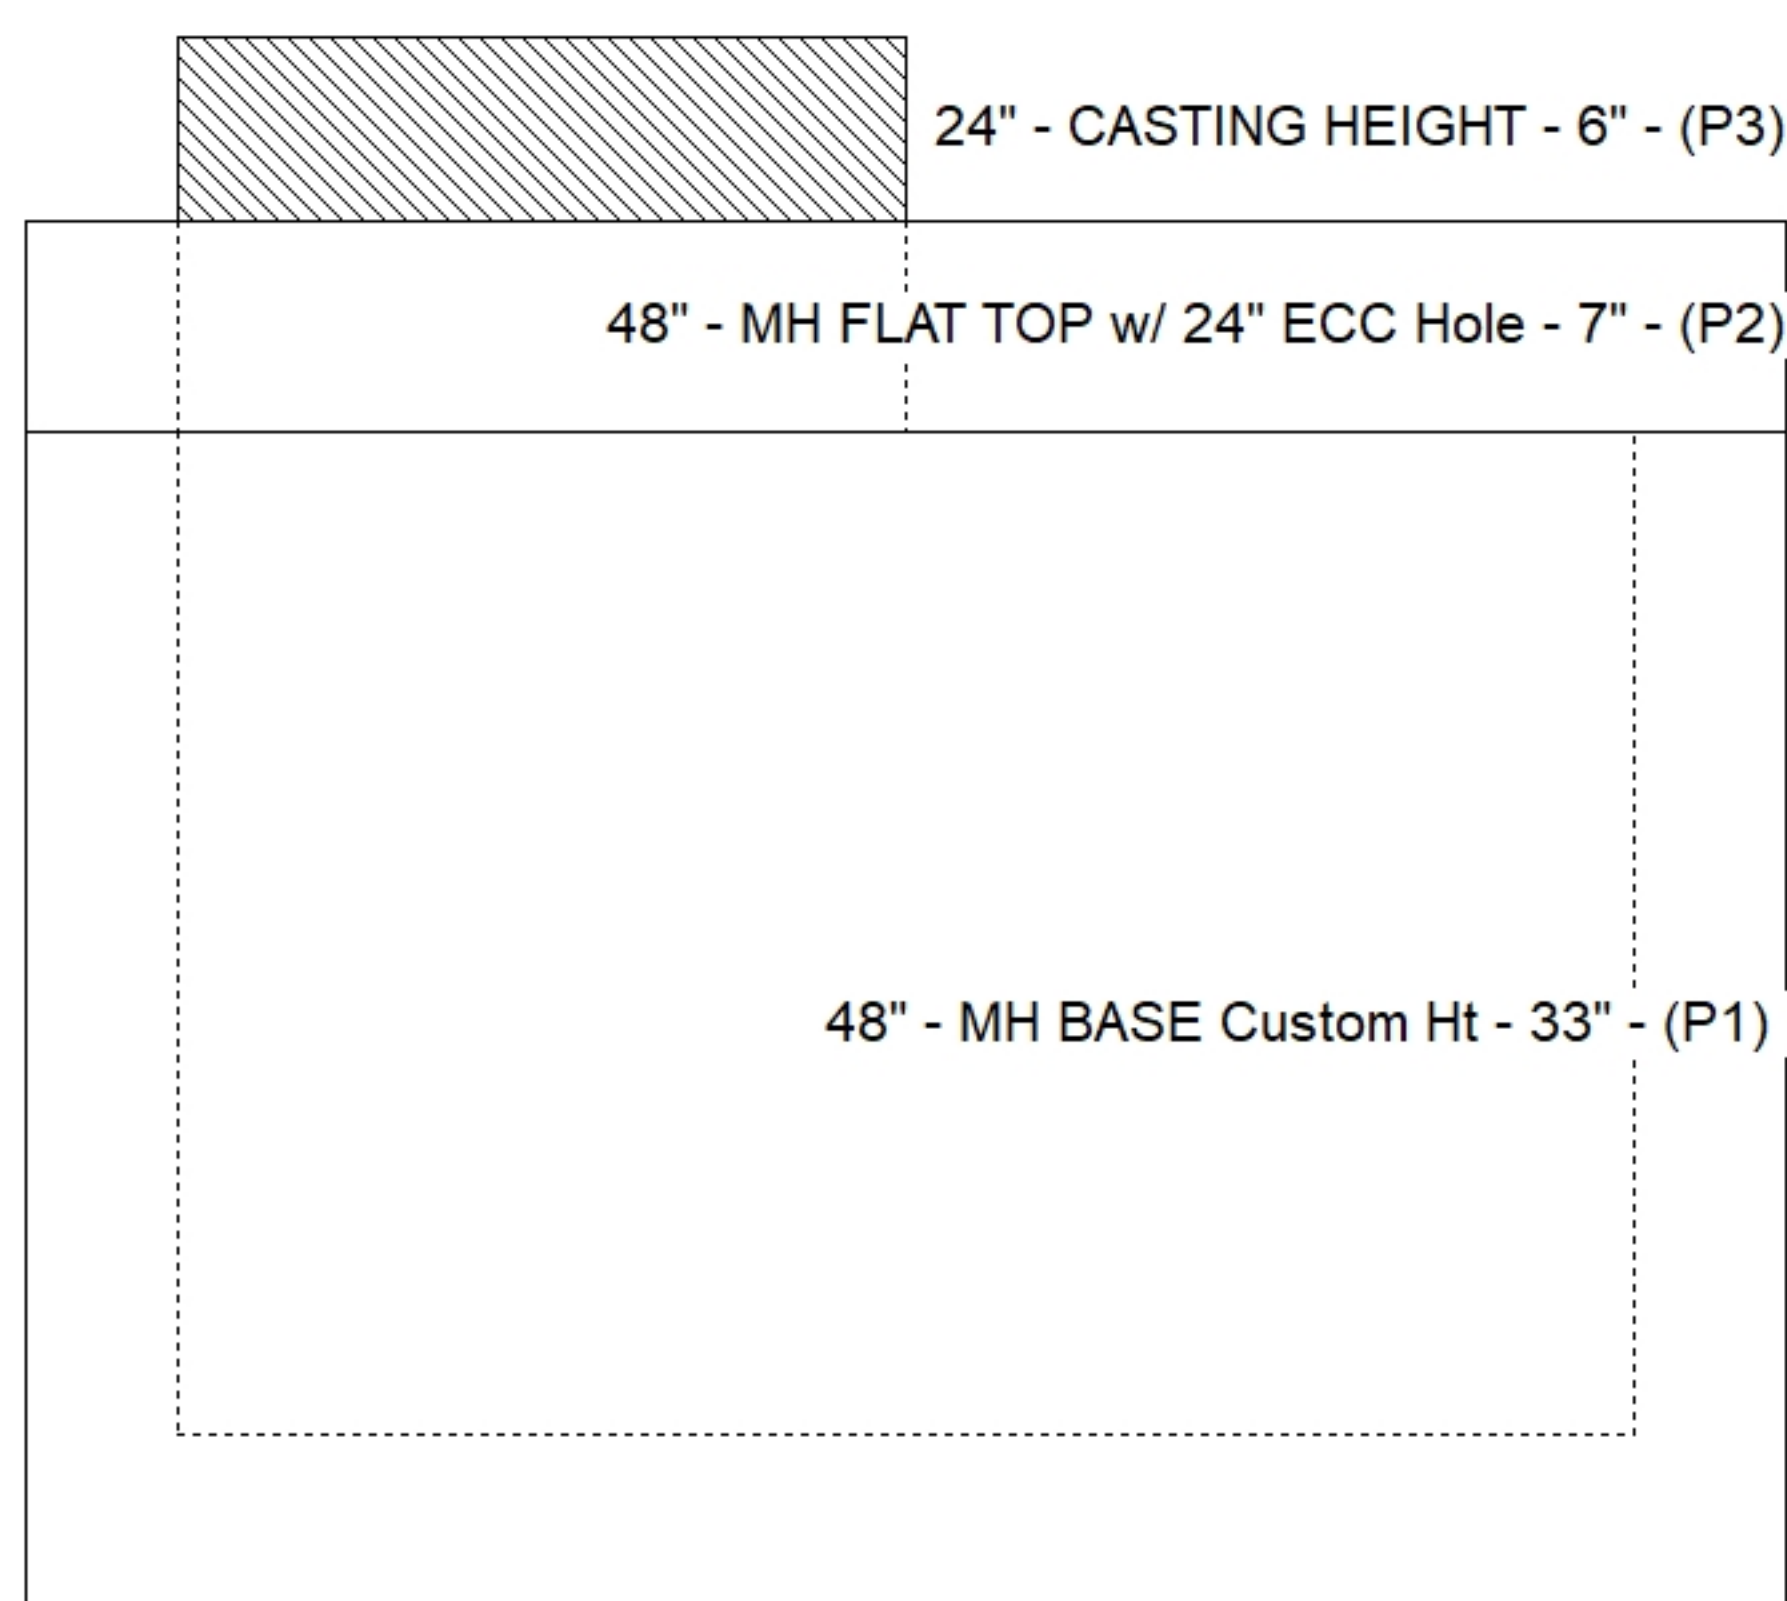

Submittal Drawing
9/9/2026 3:27:57 PM

SUBMITTAL
APPROVED BY:
