

Contractor: Byard Construction, LLC

TECH: Jared - A

Plant: 100




Slack: 0.96"

1. (3)JBS 3080 SETS (F/G/H) PROVIDED BY ICAT.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 108" - CASTING HEIGHT - 6.5"
P1) 24" x 108" - BOX BASE 6inW, 6inF, Variable Ht - 48"
3) CASTING - JBS 3080 SET (F/G/H)
1) Hole - 22
1) Hole - 24

0 lb
8621 lb
1500 lb
0 lb
0 lb

Structure Total: 10121 lb

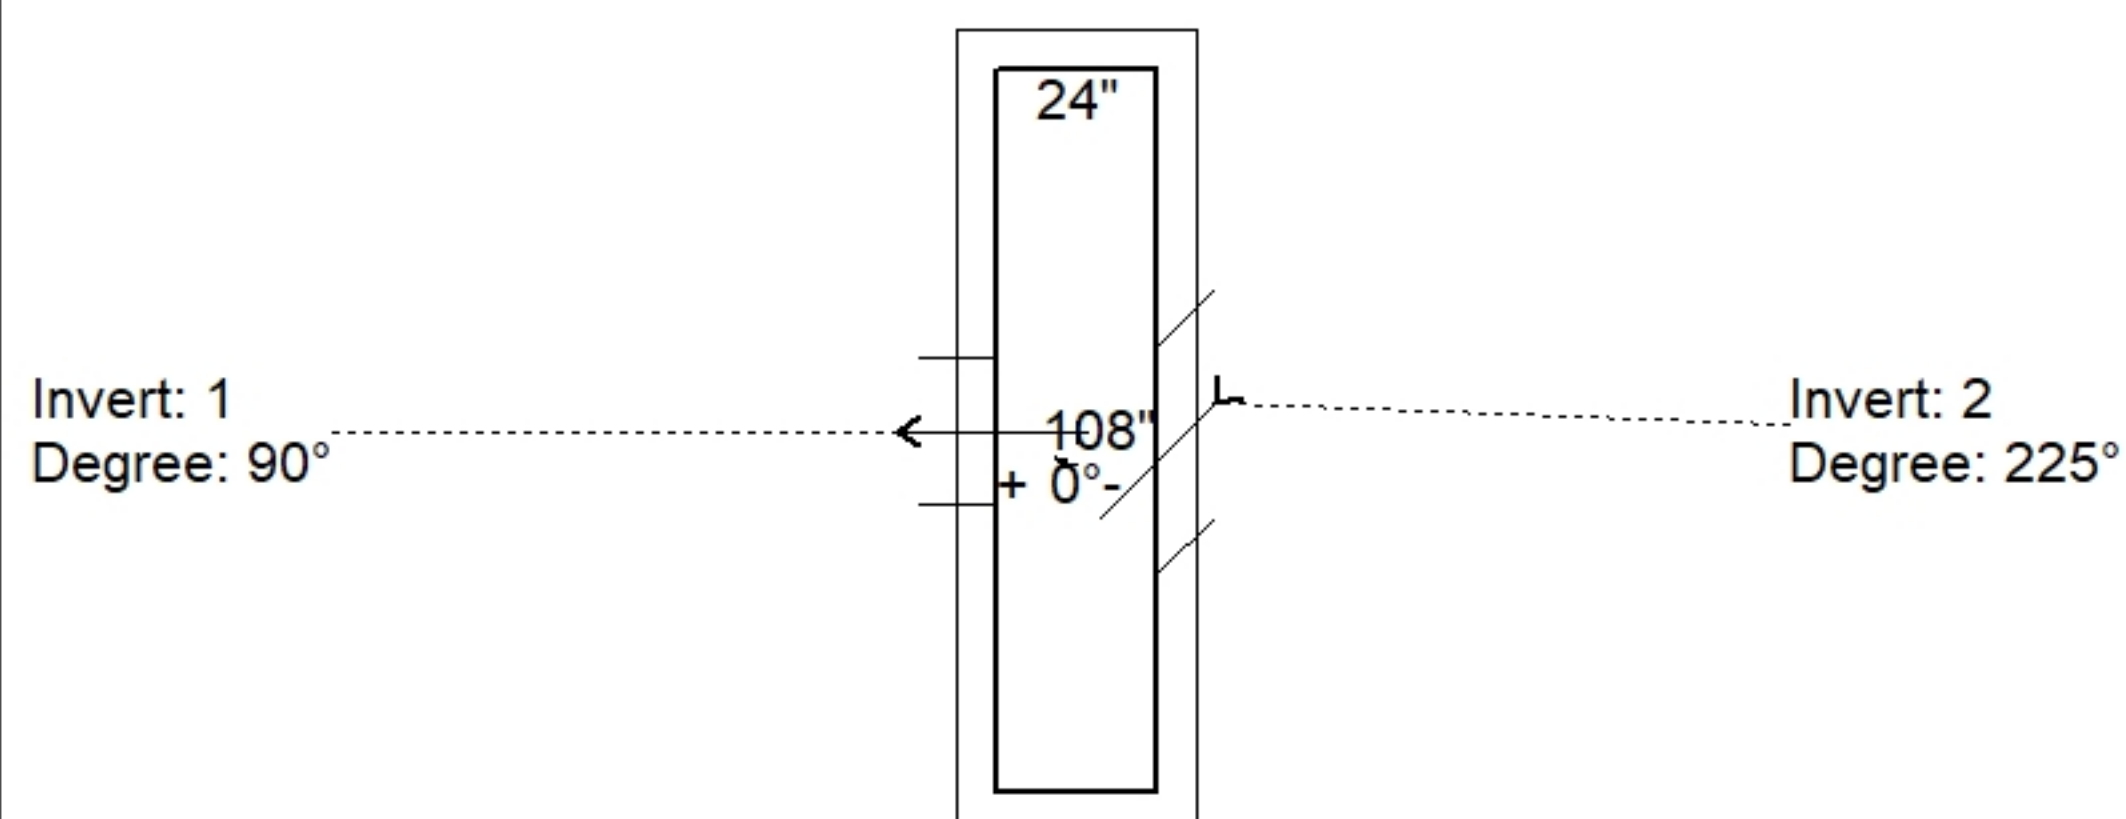


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	429.1'							
Reducer								
Invert 1	424.52'	90°	18" CMP	19"	22"	Hole 22	0"	P1
Invert 2	424.62'	225°	18" HDPE	21.2"	24"	Hole 24	0.1"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 108" - CASTING HEIGHT - 6.5" - (P2)

24" x 108" - BOX BASE 6inW, 6inF, Variable Ht - 48" - (P1)

Default - Interior Dimensions

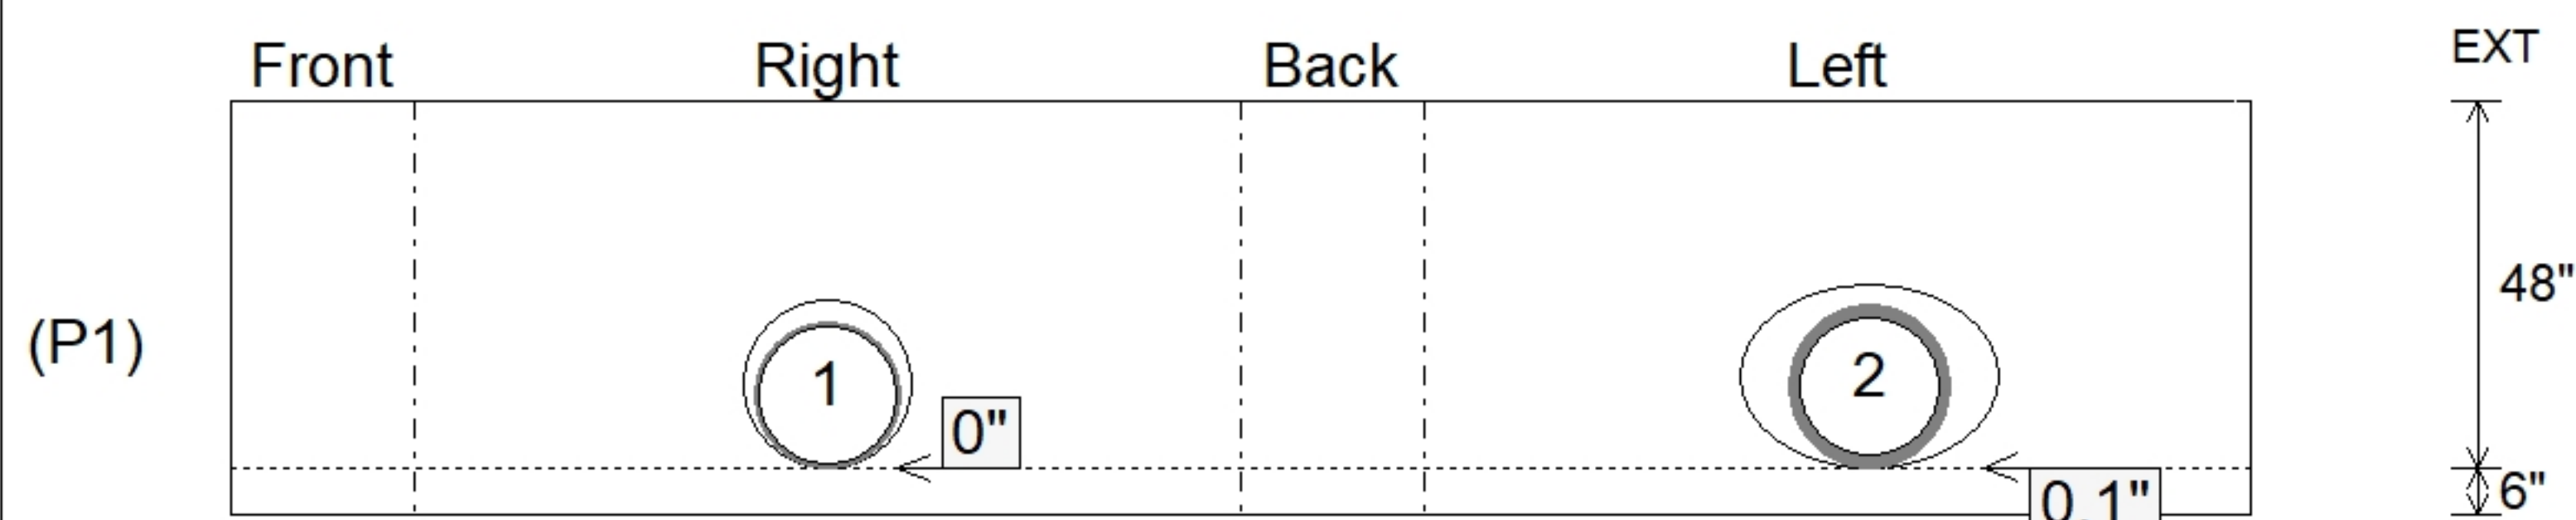

Submittal Drawing
9/9/2026 3:27:58 PM

SUBMITTAL
APPROVED BY:
