

Job Name: 25-2471 - Texas Roadhouse
Job Location: Danville, KY
Contractor: McCain Bros Excavating LLC

Plant: 100

6/11/2026 11:35:51 AM

Tech: Jared - F
PC: M. Sullivan



Structure ID: 3

P3 MH060LD13

MH FLAT TOP w/ 24" ECC Hole F/G

- P4) 24" - CASTING HEIGHT - 7"
P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13"
P2) 60" - MH RISER Custom Ht T/G - 31"
P1) 60" - MH BASE T/n - 72"
2) 60" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 30
1) DOGHOUSE INVRTD - 30"x29"
4) MH Step ML-10-TDS-NCR - 10"



Structure Total:

0 lb
2869 lb
3236 lb
9101 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
15206 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. (7" TALL CASTING BY OTHERS)

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

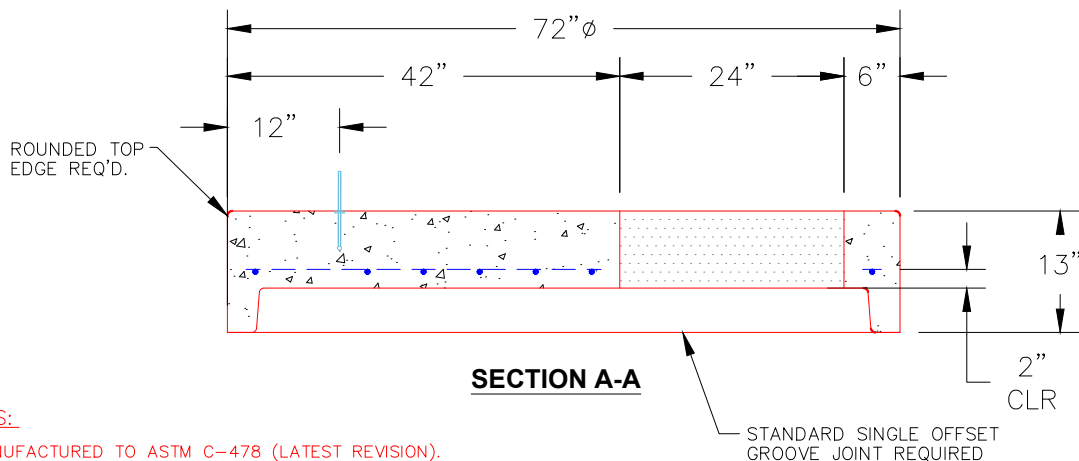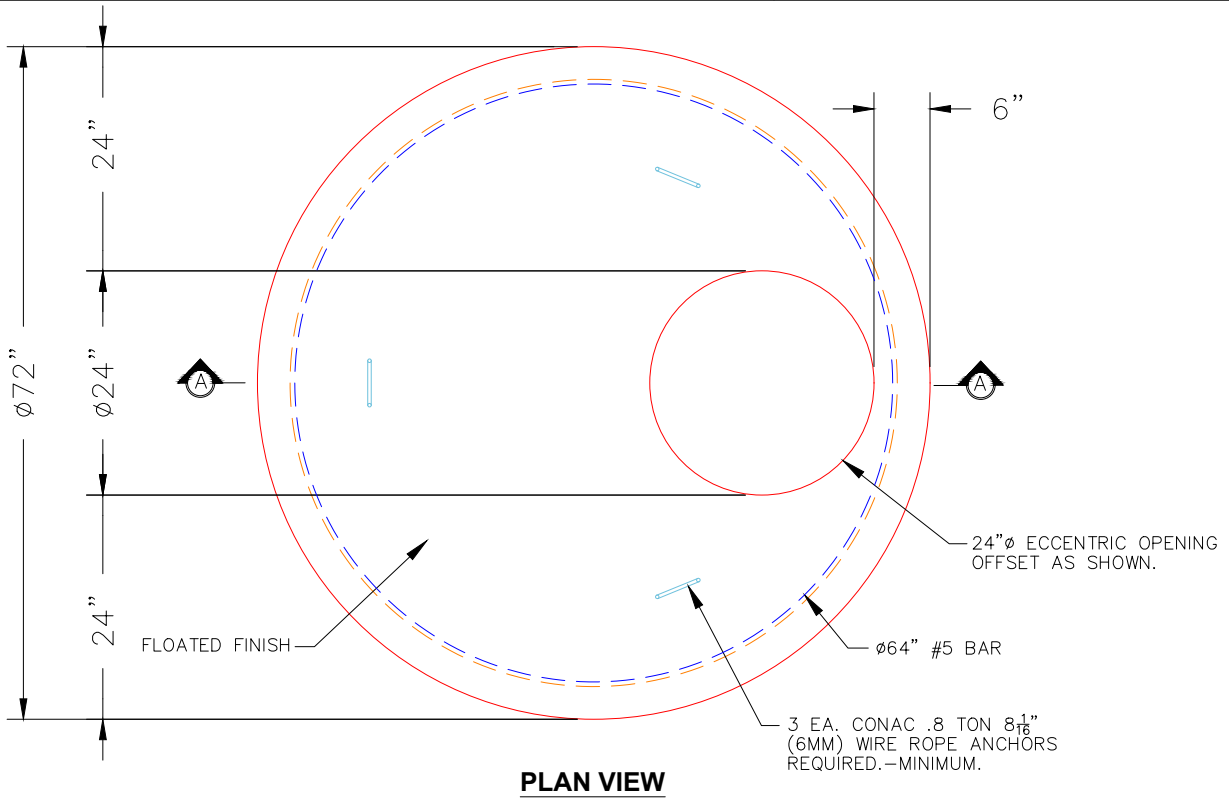

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2869 lb
Volume (Net): 0.73cu.yd
