

Job Name: 25-2471 - Texas Roadhouse
Job Location: Danville, KY
Contractor: McCain Bros Excavating LLC

Plant: 100
6/16/2026 8:14:24 AM

Tech: Jared - F
PC: M. Sullivan



Structure ID: SSMH 1

P3 GR3


GRADE RING

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING - 3"
P2) 48" - ECC CONE w/ 24" HOLE - 36"
P1) 48" - MH BASE - 30"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
3) PSX - 12-06 NYLO
5) MH Step ML-10-TDS-NCR - 10"

0 lb
202 lb
3000 lb
3282 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
24 lb
0 lb

Structure Total: 7949 lb


Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING SUPPLIED BY OTHERS.
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

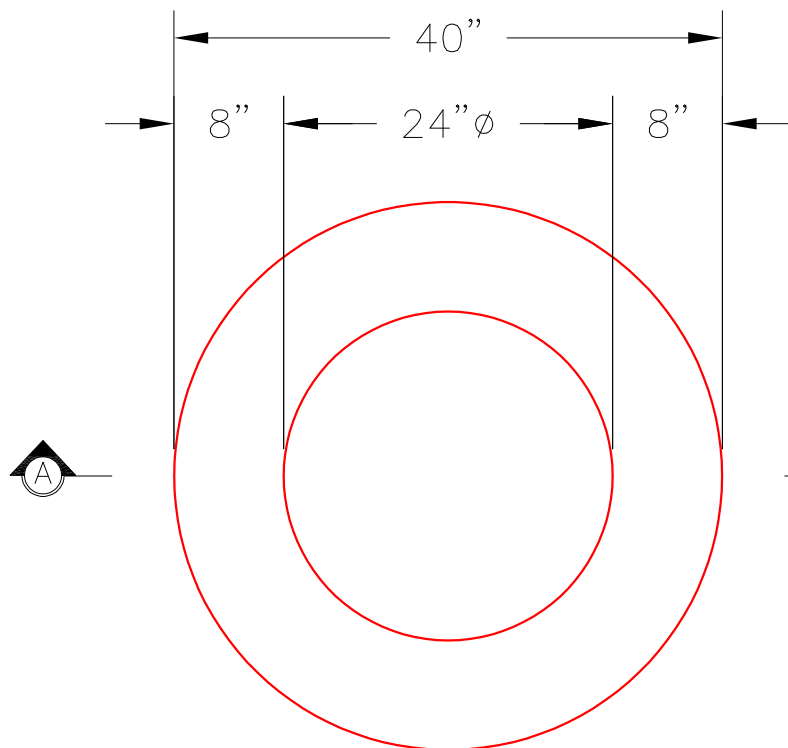


PLAN VIEW

NOTES:

1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
-CONCRETE: 4,000 PSI @ 28 DAYS.
-REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)

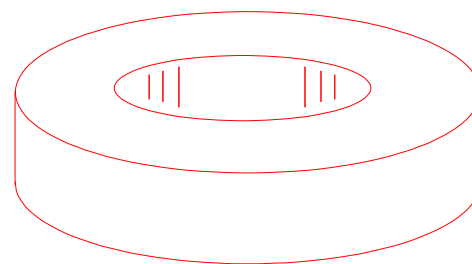

ISOMETRIC VIEW



SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
