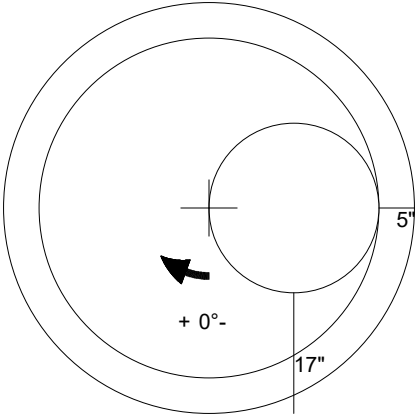



Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC		Plant: Beaver Dam 8/7/2025 12:54:23 PM	Tech: C. Russ PC: E.Bradley	
Structure ID: SF-106A R EMAKE				
P3 MH048CN24X		ECC XYPEX CONE w/ 24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 6" P3) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P2) 48" - MH RISER w/XYPEX T/G - 60" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 44" 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 2) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820 1) PSX - 12-08 NYLO		0 lb 1738 lb 4144 lb 3899 lb 1440 lb 0 lb 0 lb 0 lb 0 lb 2 lb 8 lb ----- 11231 lb Structure Total:	<u>Structure Notes:</u> 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1155 "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1738 lb Volume (Net): 0.44cu.yd
