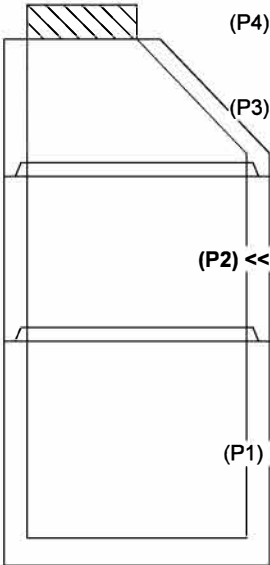





Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC					Plant: Beaver Dam 8/7/2025 12:59:53 PM		Tech: C. Russ PC: E.Bradley				
Structure ID: SF-110											
P2 MH048RS36XS			MH RISER w/XYPEX T/G								
P4) 24" - CASTING HEIGHT - 7.50" P3) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER w/XYPEX T/G - 36" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 43" 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 2) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820						0 lb 1981 lb 2515 lb 3829 lb 1440 lb 0 lb 0 lb 0 lb 0 lb 2 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1123 WT "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 604.28' Rim to Invert: 9.61' Slack: 0.82" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd	
