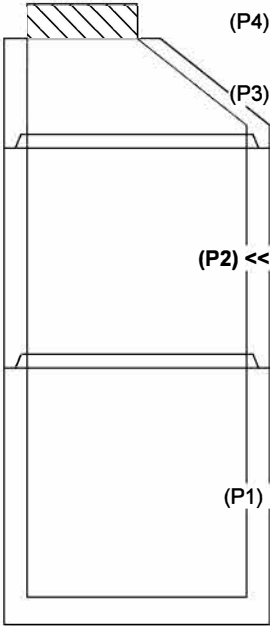

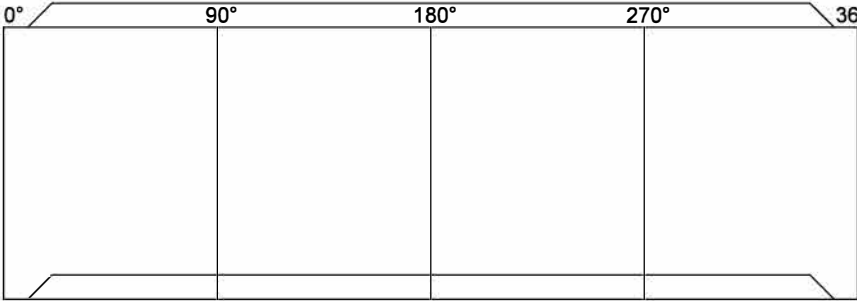


Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC					Plant: Beaver Dam 8/7/2025 1:01:20 PM		Tech: C. Russ PC: E.Bradley				
Structure ID: SF-110A											
P2 MH048RS48XS			MH RISER w/XYPEX T/G								
P4) 24" - CASTING HEIGHT - 7.50" P3) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P2) 48" - MH RISER w/XYPEX T/G - 48" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 50" 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 2) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820					0 lb 1738 lb 3353 lb 4318 lb 1440 lb 0 lb 0 lb 0 lb 2 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1123 WT "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total: 10852 lb											
Rim: 606.67' Rim to Invert: 10.66' Slack: 0.42" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
		EXT 48"									
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd	
