

Job Name: 25-2666 Residential Subdivision  
 Job Location: Hawesville, Ky  
 Contractor: Winwater Hartford KY Co.

Plant: 100

12/15/2025 8:26:07 AM

Tech: C.Russ

PC: A.Chambers



**Structure ID: CBI AA2**

**P2 MH048LD07-24X36RECT**


**MH FLAT TOP w/24"x36" Hole F/F**

- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 48" - MH FLAT TOP w/24"x36" Hole F/F - 7"
- P1) 48" - MH BASE Custom Ht F/n - 38"
- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 48" - SGL 1"x14.5' Butyl (2x)
- 2) Hole - 30"
- 3) MH Step ML-10-TDS-NCR - 10"


	0 lb
	1044 lb
	3353 lb
	442 lb
	0 lb
	0 lb
	0 lb
Structure Total:	4839 lb

**Structure Notes:**

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
  - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
  - RISER/WALLS (As .12)
  - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
4. HOE 525 PROVIDED BY ICAST

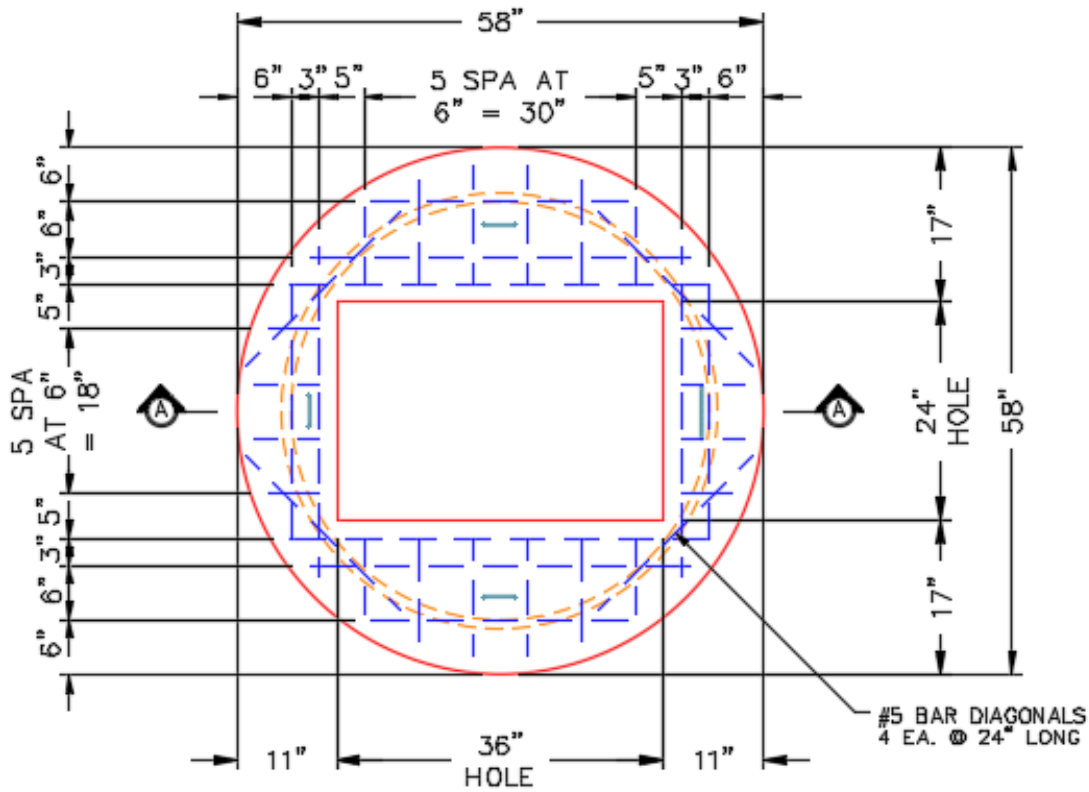

**PLAN VIEW**

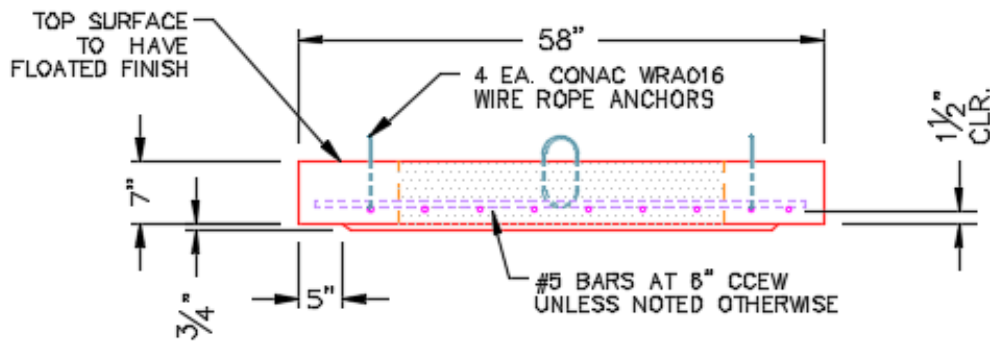

**SECTION AA**

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 1044 lb  
 Volume (Net): 0.27cu.yd
