





Structure ID: A-2 (1)

P1 HWSF24 24" - SLOPED & FLARED HEADWALL F/F

DIMENSIONS									
PIPE Ø	A	B	C	D	E	F	G	H	I
24"	3'-8"	4'-4"	2'-10"	1'-8"	5'-0"	4"	3 1/2"	2'-10"	6'-0"
									WEIGHT 4,956 LBS.

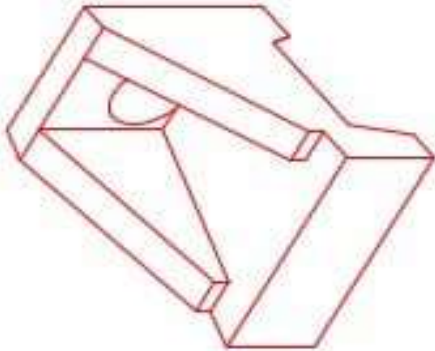


ISOMETRIC VIEW
24" HEADWALL

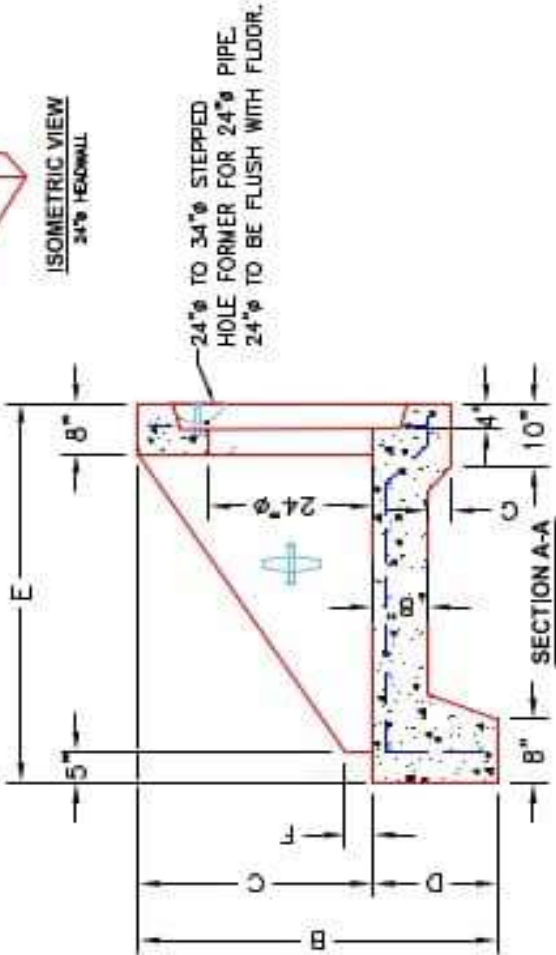


SECTION A-A

"A-ANCHOR" LIFTING SYSTEM
FOR PLANT & FIELD HANDLING.

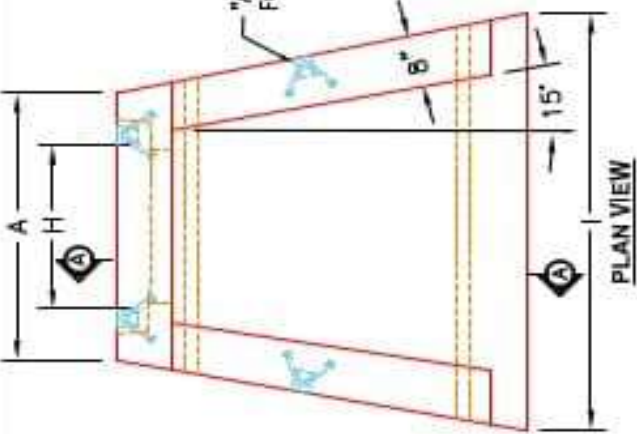

PLAN VIEW

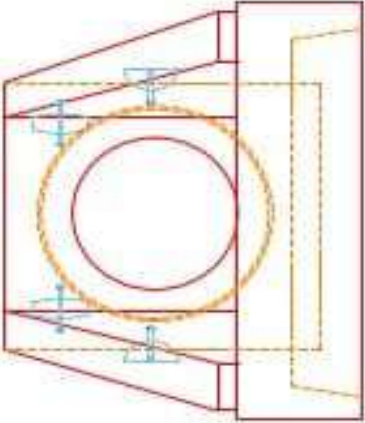

FRONT ELEVATION

- NOTES:
1. CONCRETE 4000 PSI @ 28 DAYS.
 2. REINFORCING #4 BAR @ 12" O.C. E.W. - GRADE 60, (WITH 3" CONCRETE COVER MINIMUM)
 3. REINFORCING BARS TO BE TACK WELDED OR TIED.
 4. DRAWING TO BE USED IN CONJUNCTION WITH KYTC STD. DRAWING RCH-020-03 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
 5. CHAMFER ON ALL EXPOSED EDGES.

PRODUCTION WORK ORDER

QUALITY CONTROL CHECKLIST	
☐ ALL DIMENSIONS CORRECT.	
☐ LIFTERS INSTALLED.	
☐ STEPPED HF CORRECT SIZE.	
☐ REINFORCING CORRECT.	
☐ DISSIPATOR BLOCK INSTALLED.	
☐ EDGES CHAMFERED.	
☐ ALL PATCHWORK ACCEPTABLE.	



DESCRIPTION: KYTC 24" Ø SLOPED & FLARED HEADWALL
CUSTOMER: STOK
PROJECT: STOCK INVENTORY
STRUCTURE ID.: N/A
QUOTE/SALES ORDER NO: N/A
CHECK: J.H. ROSS, PE
DRAWING: N. RICHARDS
DATE: REV. 4/22/24
SCALE: NTS
PG. 1 of 1
