



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction	Plant: 100	Tech:	J. Horsley - A	
	5/12/2026 1:01:40 PM	PC:	J. Jarvis	
Structure ID: 121 P2 MH048LD12ECC MH FLAT LID w/24in ECC Hole F/G				

P3) 24" - CASTING HEIGHT - 8" P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 28" 1) 48" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 18 1) Hole - 16 2) MH Step ML-10-TDS-NCR - 10"	0 lb 1561 lb 2956 lb 0 lb 0 lb 0 lb 0 lb 0 lb 4517 lb Structure Total:	Structure Notes: **KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE A / ASTM C-478 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-510 FRAME & COVER "STORM" SUPPLIED BY OTHERS 5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING 6. TOP SURFACE TO RECEIVE FLOATED FINISH
--	---	--

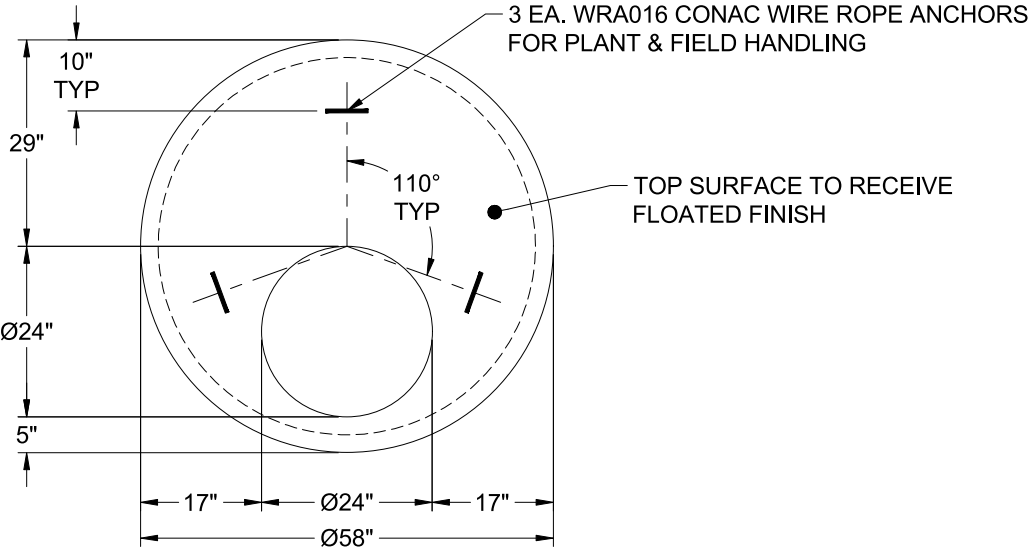

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 12"	Weight (Net): 1561 lb Volume (Net): 0.4cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	---
