


Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)
Job Location: Indiana, KY
Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:12:29 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 146

P2 MH048LD12ECC

MH FLAT LID w/24in ECC Hole F/G



- P3) 24" - CASTING HEIGHT - 8"
P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 40"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
1) Hole - 22
2) Hole - 20
3) MH Step ML-10-TDS-NCR - 10"

0 lb
1561 lb
3689 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 5250 lb

Structure Notes:

- ** KYTC STATE PROJECT **
1. PER KYTC MANHOLE TYPE A / ASTM C-478 SPECS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
 4. HOE KY-510 FRAME & COVER "STORM" SUPPLIED BY OTHERS
 5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
 6. TOP SURFACE TO RECEIVE FLOATED FINISH

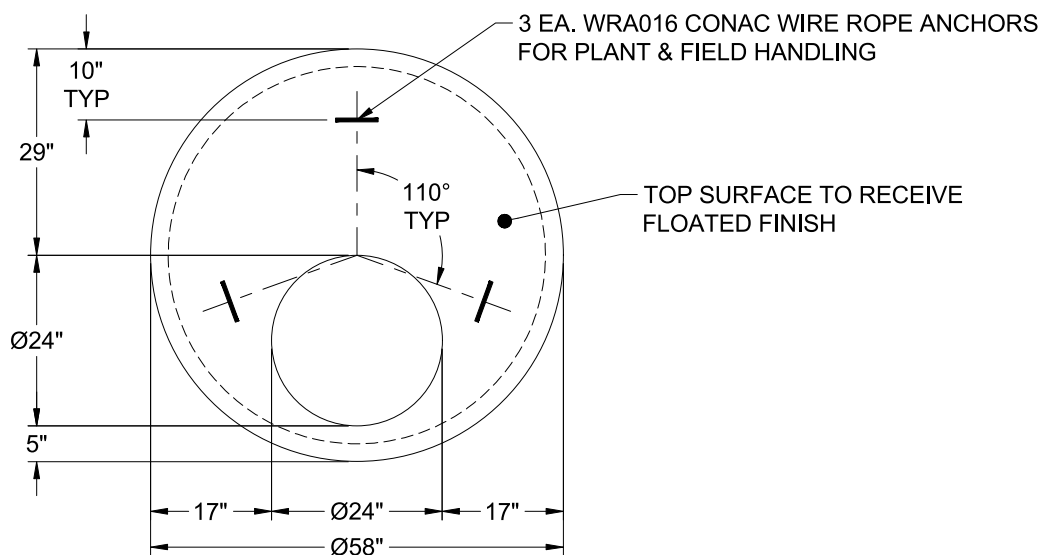

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.4cu.yd
