

Contractor: Louisville Paving and Construction


Plant: 100



Slack: 0"


4. HOE KY-210 FRAME & GRATE SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID

Structure Total: 4259 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	563.4'							
Reducer								
Invert 1	560.15'	90°	15" HDPE	17.6"	20"	Hole 20	-2.5"	P1
Invert 2	560.15'	270°	15" HDPE	17.6"	20"	Hole 20	-2.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								


24" x 24" - BOX BASE 8inW. 8inE. Variable Ht F/n - 31" - (P1)

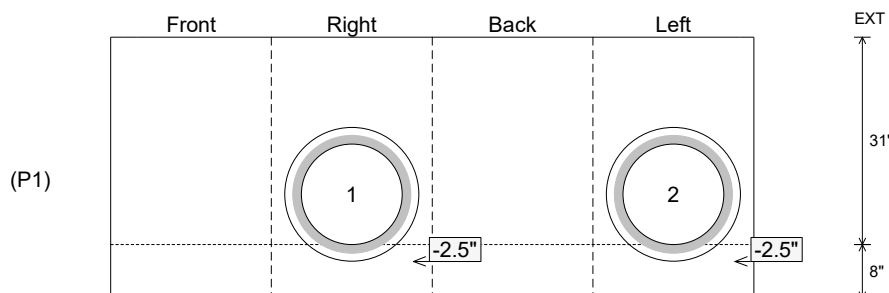


SUBMITTAL
APPROVED BY:

GENERAL NOTES:

1. MANUFACTURE TO ASTM C-913 (LATEST REVISION)
2. CONCRETE: 5,000 PSI AT 28 DAYS
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60)
4. WEIGHT: 943 LBS
5. HOE KY-210 FRAME & GRATE SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID

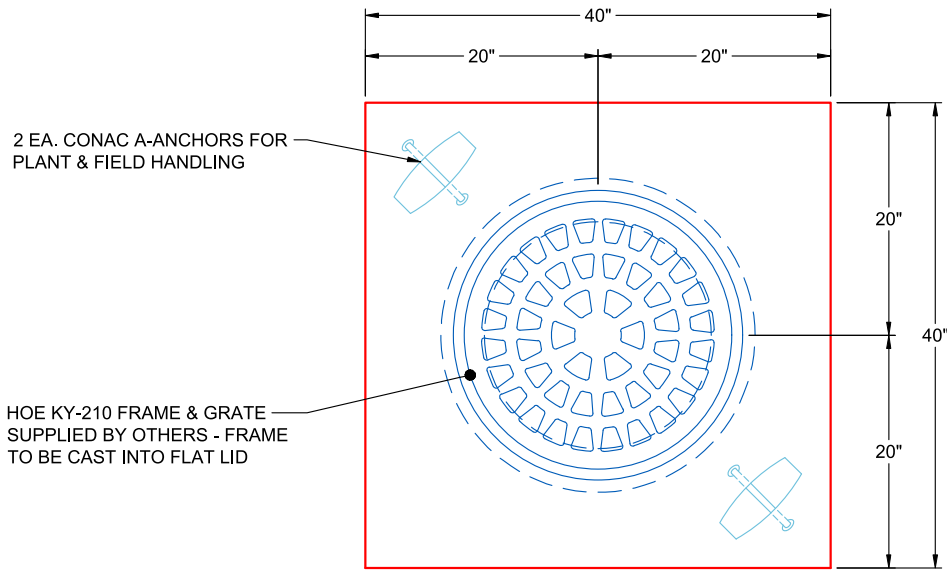

PLAN VIEW



FRONT VIEW

REVISIONS

REV. 0 DATE: NO REVISIONS TO DATE



SUBMITTAL DRAWING: 40" X 40" X 8" FLAT LID SPECIAL		
CUSTOMER: LOUISVILLE PAVING & CONSTRUCTION		
PROJECT: KYTC JEFFERSON CO CALL 106 (251315)		
STRUCTURE: 20		
SALES ORDER NO: 25-2952		
CHECKED BY: B. SMITH	DRAWN BY: K. CARDWELL	
DATE: 06/12/26	SCALE: NTS	PG. 1 OF 1
