

Contractor: Louisville Paving and Construction

Plant: 100



Slack: 2"


1. PER MSD YARD DRAIN / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #4 BAR @ 12" C.C. E.W. (GRADE 60)
4. HOE 165-A FRAME & GRATE SUPPLIED BY OTHERS

P2) 18" x 18" - CASTING HEIGHT - 4"
P1) 18" x 18" - BOX BASE 6inW, 6inF F/n - 24"
1) 18" x 18" - Conseal CS-102 1.00"
1) Hole - 16

0 lb
1508 lb
0 lb
0 lb



Structure Total: 1508 lb

Invert: 1
Degree: 165°



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	562.8'							
Reducer								
Invert 1	560.3'	165°	12" HDPE	14.5"	16"	Hole 16	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

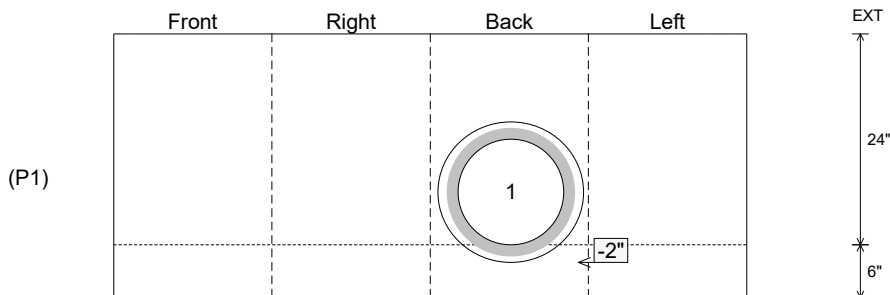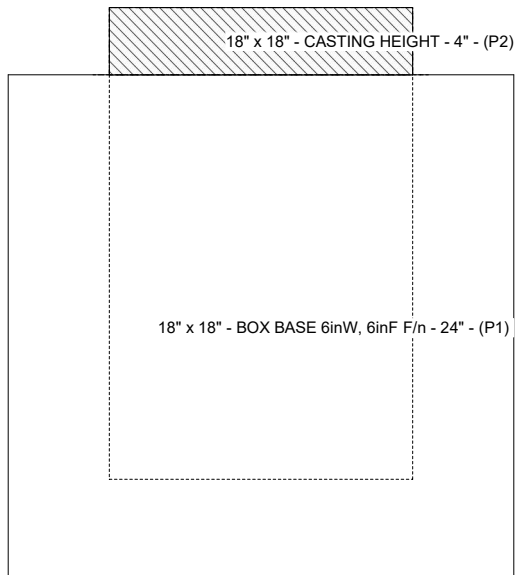

Submittal Drawing
6/17/2026 5:40:15 PM

SUBMITTAL
APPROVED BY:
