

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)
Job Location: Indiana, KY
Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:12:28 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 44

P2 MH048LD12ECC

MH FLAT LID w/24in ECC Hole F/G

- P3) 24" - CASTING HEIGHT - 4"
P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 29"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
1) Hole - 20
1) Hole - 18
2) MH Step ML-10-TDS-NCR - 10"



0 lb
1561 lb
3112 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 4673 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC MANHOLE TYPE A / ASTM C-478 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY OTHERS
5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
6. TOP SURFACE TO RECEIVE FLOATED FINISH

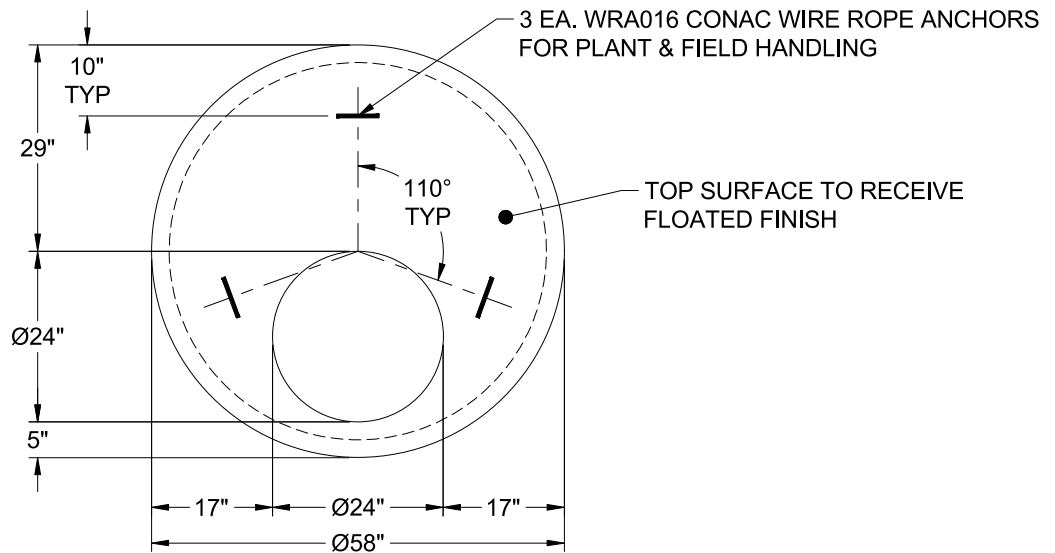

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.4cu.yd
