



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction	Plant: 100	Tech:	J. Horsley - A	
	6/12/2026 3:12:28 PM	PC:	J. Jarvis	
Structure ID: 50 P2 MH048LD12ECC MH FLAT LID w/24in ECC Hole F/G				

- P3) 24" - CASTING HEIGHT - 4"
 P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12"
 P1) 48" - MH BASE Custom Ht T/n - 38"
 1) 48" - Conseal CS-102 1.00"
 1) 24" - Conseal CS-102 1.00"
 2) Hole - 20
 1) Hole - 18
 3) MH Step ML-10-TDS-NCR - 10"

	0 lb
	1561 lb
	3605 lb
	0 lb
	0 lb
	0 lb
	0 lb
	0 lb
Structure Total:	5166 lb

- Structure Notes:
 ** KYTC STATE PROJECT **
 1. PER KYTC MANHOLE TYPE A / ASTM C-478 SPECS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
 4. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY OTHERS
 5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
 6. TOP SURFACE TO RECEIVE FLOATED FINISH

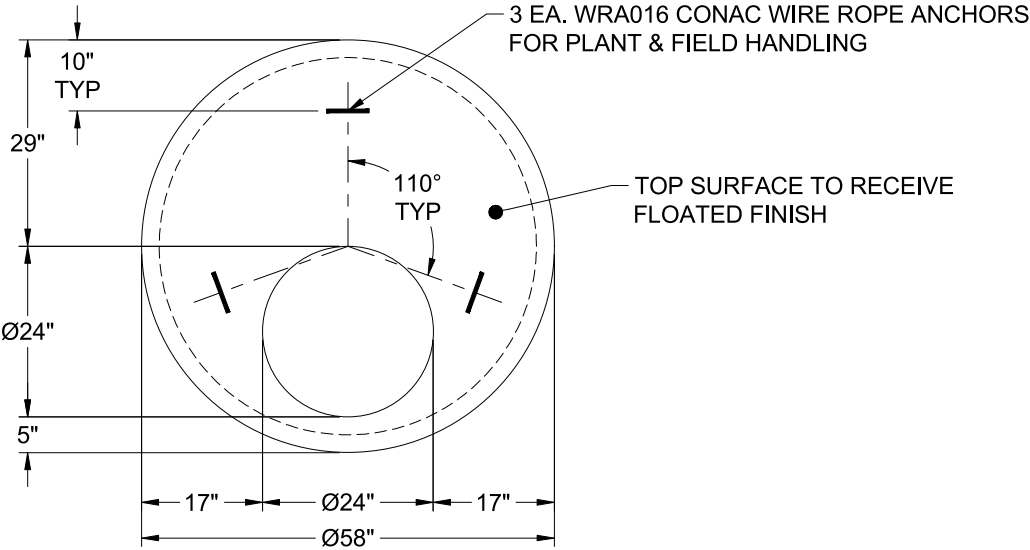

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 12"	Weight (Net): 1561 lb Volume (Net): 0.4cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	---
