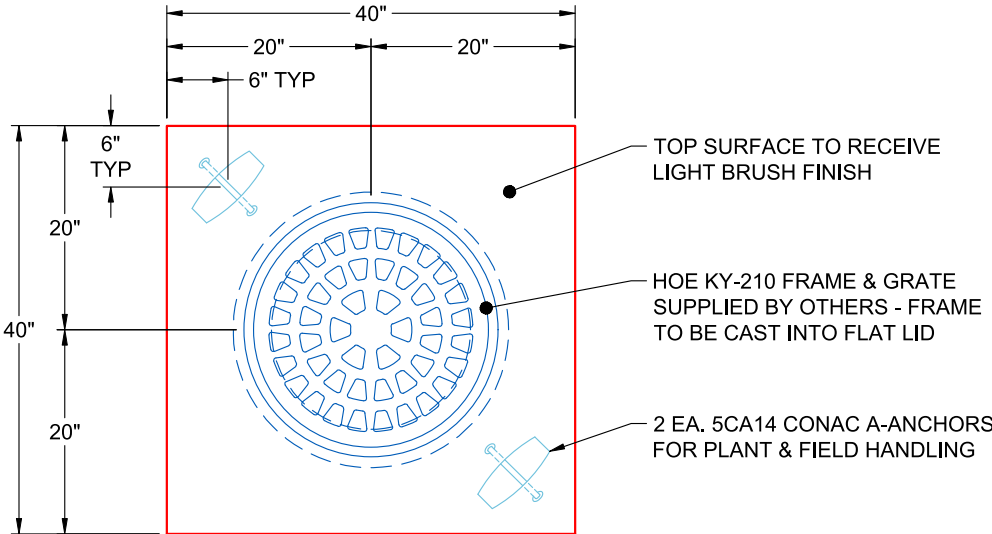



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)		Plant: 100	Tech: J. Horsley - A	
Job Location: Indiana, KY Contractor: Louisville Paving and Construction		5/12/2026 1:01:38 PM	PC: J. Jarvis	
Structure ID: 79				
P2 BX024024-08LD08-14		CB FLAT TOP 8"W (HOE KY-210) F/F		
P2) 24" x 24" - CB FLAT TOP 8"W (HOE KY-210) F/F - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40" 1) This Structure Includes a Cast-in Item - HOE KY-210 Frame (Supplied By Others) 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 18		943 lb 4314 lb 0 lb 0 lb 0 lb ----- Structure Total: 5257 lb	Structure Notes: **KYTC STATE PROJECT** 1. PER KYTC DBI TYPE 14 / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-210 FRAME & GRATE SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID 5. LIFTERS: 2 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN 6. TOP SURFACE TO RECEIVE LIGHT BRUSH FINISH	
 PLAN VIEW (RIGHT SIDE UP)  FRONT VIEW (RIGHT SIDE UP)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 943 lb Volume (Net): 0.24cu.yd

Job Number:

25-2952

Job Name:

KYTC Jefferson Co Call 106
(251315)

Structure:

79

Note:

HOE KY-210 Frame Supplied By
Others To Be Cast Into Flat Lid
