

Job Name: 25-3040B - Stonedale Farms
Job Location: Nicholasville, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/24/2026 8:44:03 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: MH21

P3 GR3

GRADE RING

P4) 24" - CASTING HEIGHT - 7"

P3) 24" - GRADE RING - 3"

P2) 48" - ECC CONE w/ 24" HOLE - 30"

P1) 48" - MH BASE - 30"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) 48" - Conseal CS-102 1.00" (Double)

2) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 16M NYLO

4) MH Step ML-10-TDS-NCR - 10"

0 lb

202 lb

2050 lb

3255 lb

0 lb

0 lb

1440 lb

0 lb

0 lb

16 lb

0 lb

Structure Total:

6963 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY).

REINFORCING PER ASTM A615 (GRADE 60).


- CONE (As .12)

- RISER/WALLS (As .12)


- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
2. WEIGHT: 3" 202 LBS.

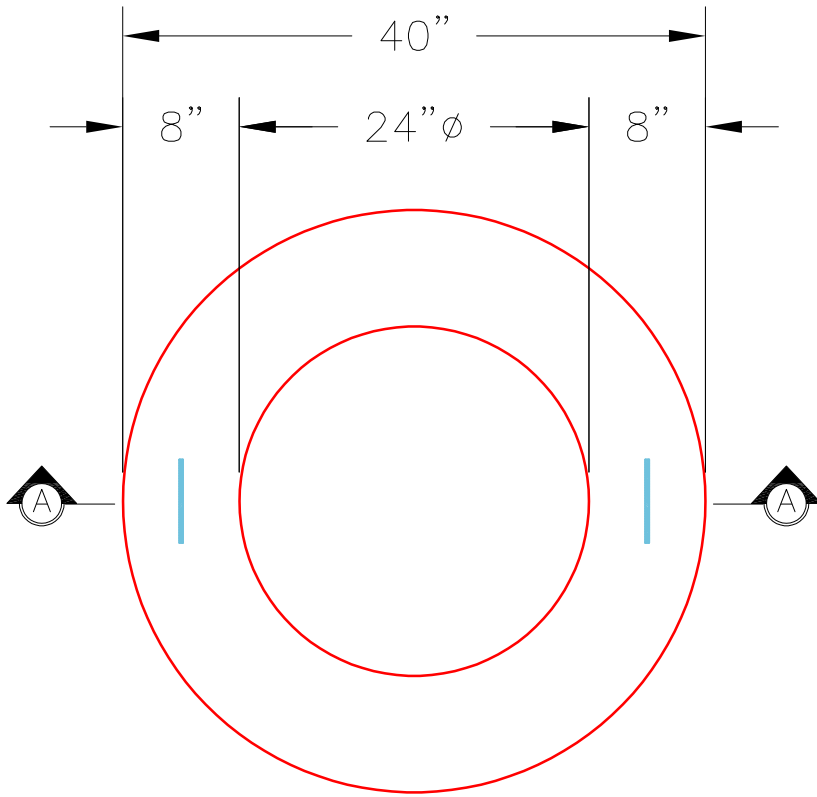

PLAN VIEW

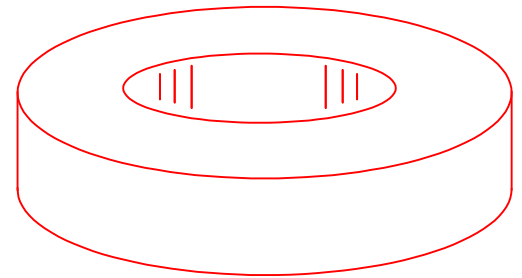

ISOMETRIC VIEW

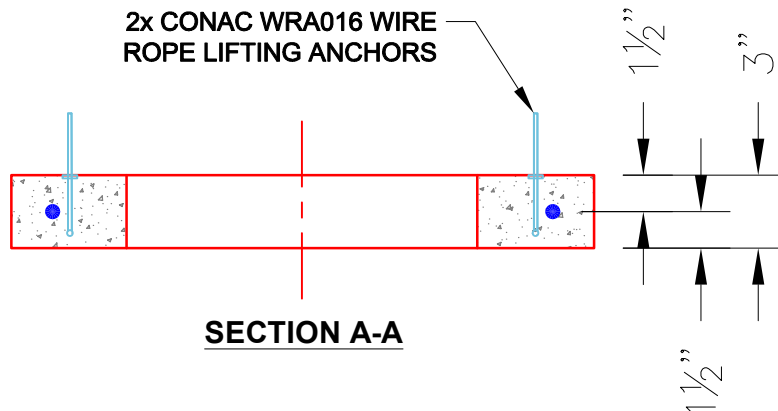

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
