


**Contractor: Weddle Enterprises, Inc**

Plant: 100




Slack: 1"

Structure Total: 7508 lb

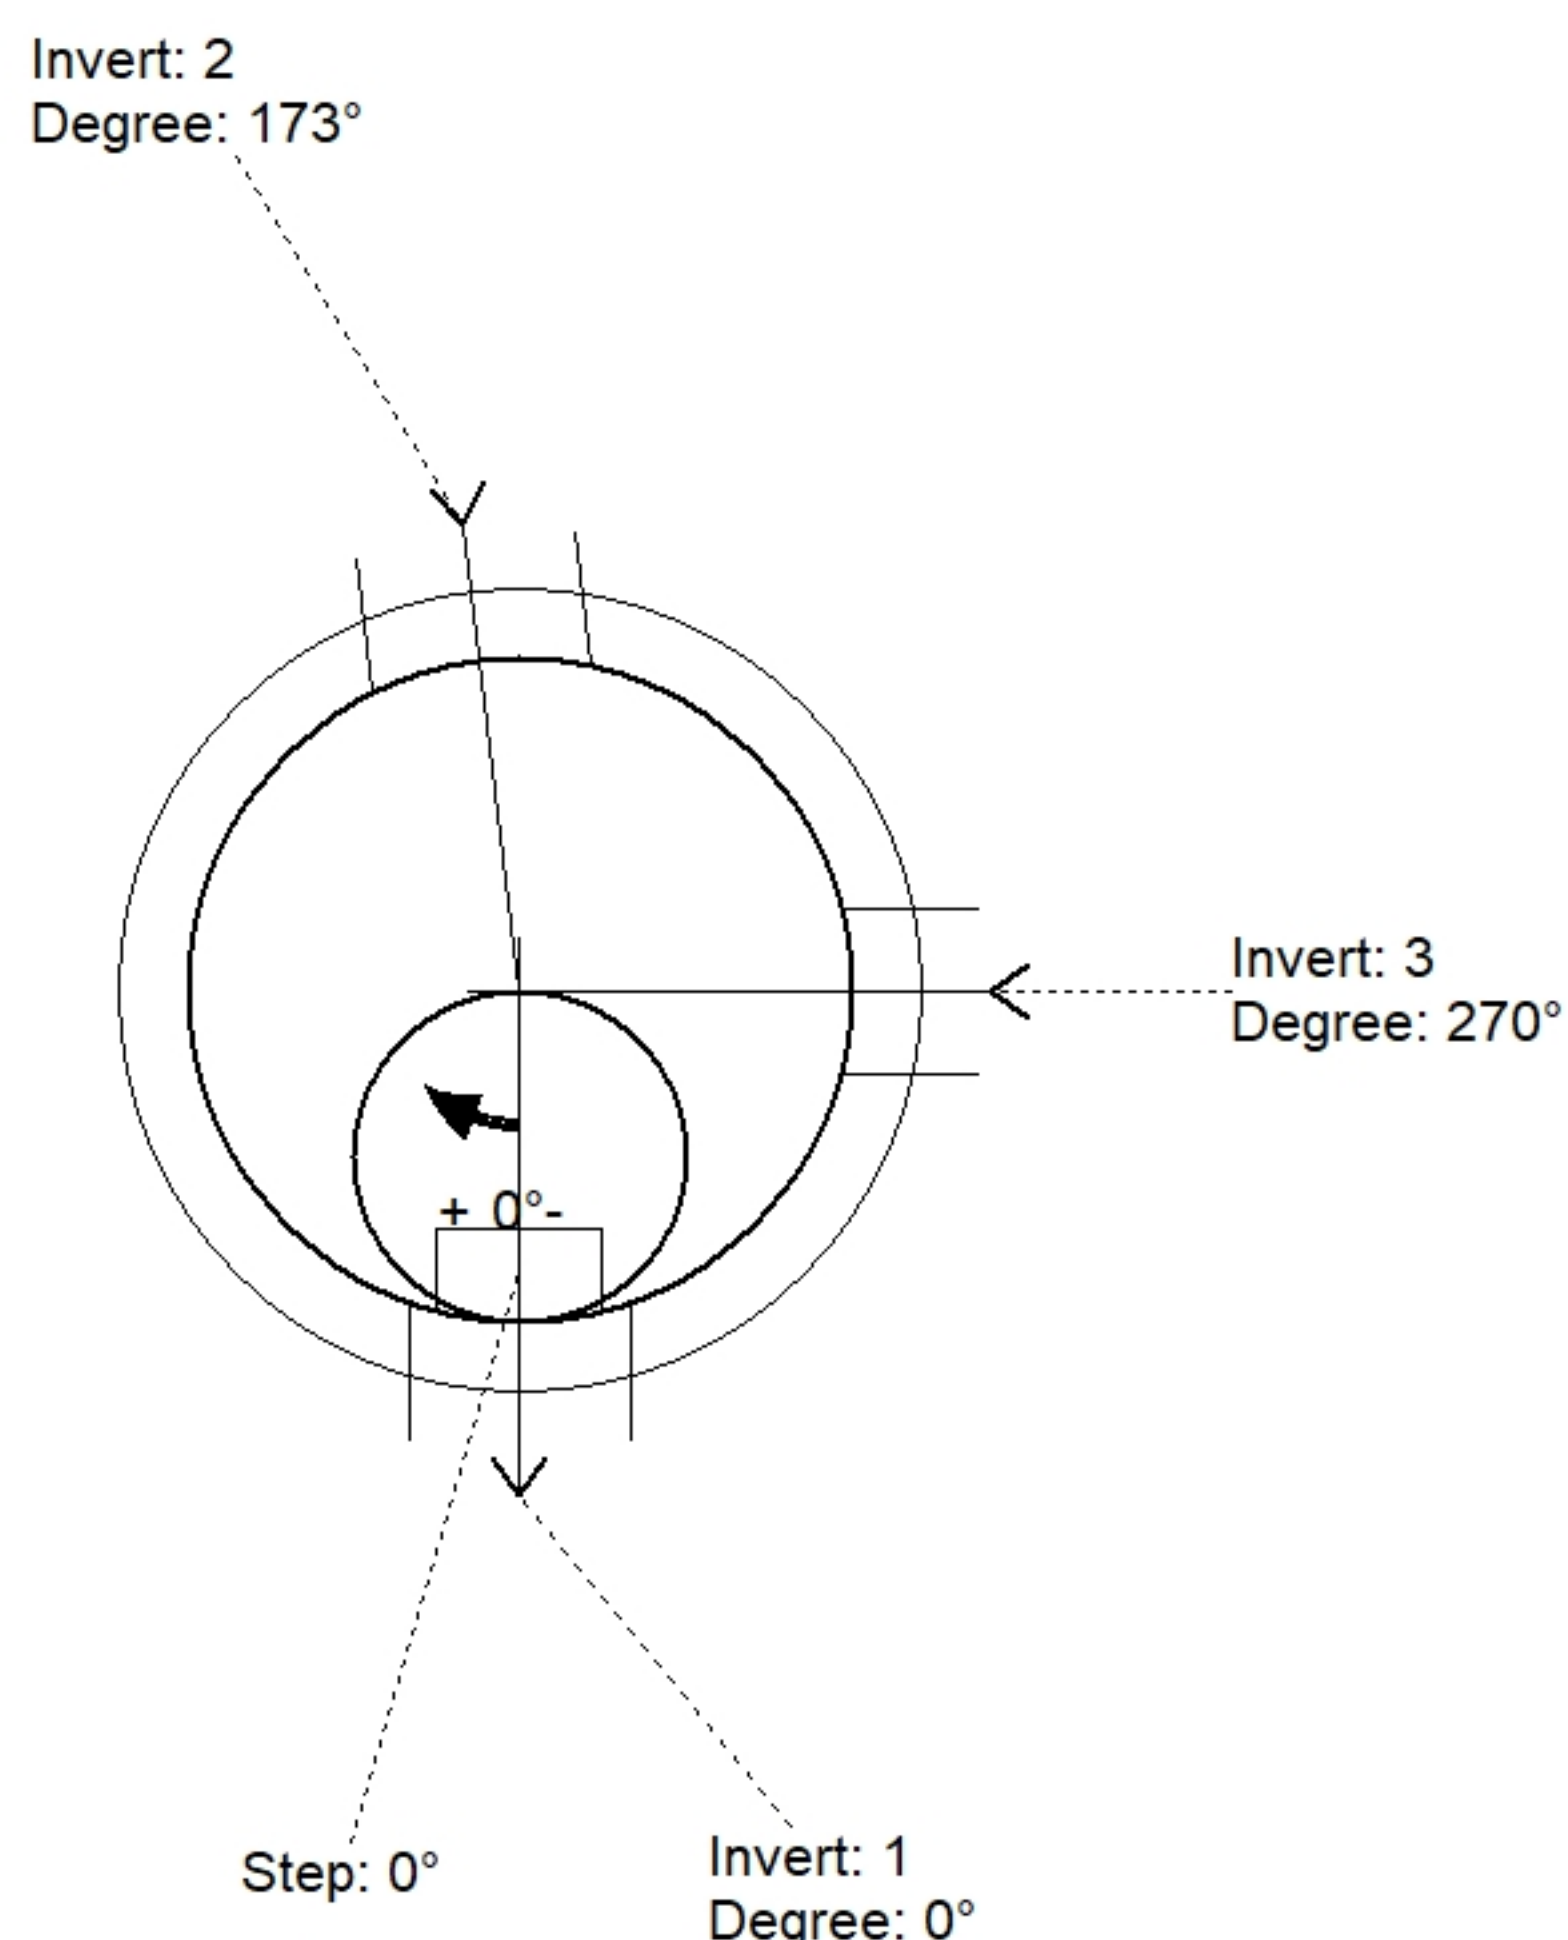

| Position | Elev     | Angle | Pipe          | Pipe OD | Hole | Connector      | Up (') | Ref |
|----------|----------|-------|---------------|---------|------|----------------|--------|-----|
| Rim      | 1008.75' |       |               |         |      |                |        |     |
| Reducer  |          |       |               |         |      |                |        |     |
| Invert 1 | 1003.25' | 0°    | 12" PVC SDR35 | 12.5"   | 16"  | PSX 16M NYLO   | 0"     | P1  |
| Invert 2 | 1003.35' | 173°  | 12" PVC SDR35 | 12.5"   | 16"  | PSX 16M NYLO   | 1.2"   | P1  |
| Invert 3 | 1005'    | 270°  | 8" PVC SDR35  | 8.5"    | 12"  | PSX 12-08 NYLO | 21"    | P1  |
| Invert 4 |          |       |               |         |      |                |        |     |
| Invert 5 |          |       |               |         |      |                |        |     |
| Invert 6 |          |       |               |         |      |                |        |     |
| Invert 7 |          |       |               |         |      |                |        |     |
| Invert 8 |          |       |               |         |      |                |        |     |

### Default - Interior Dimensions

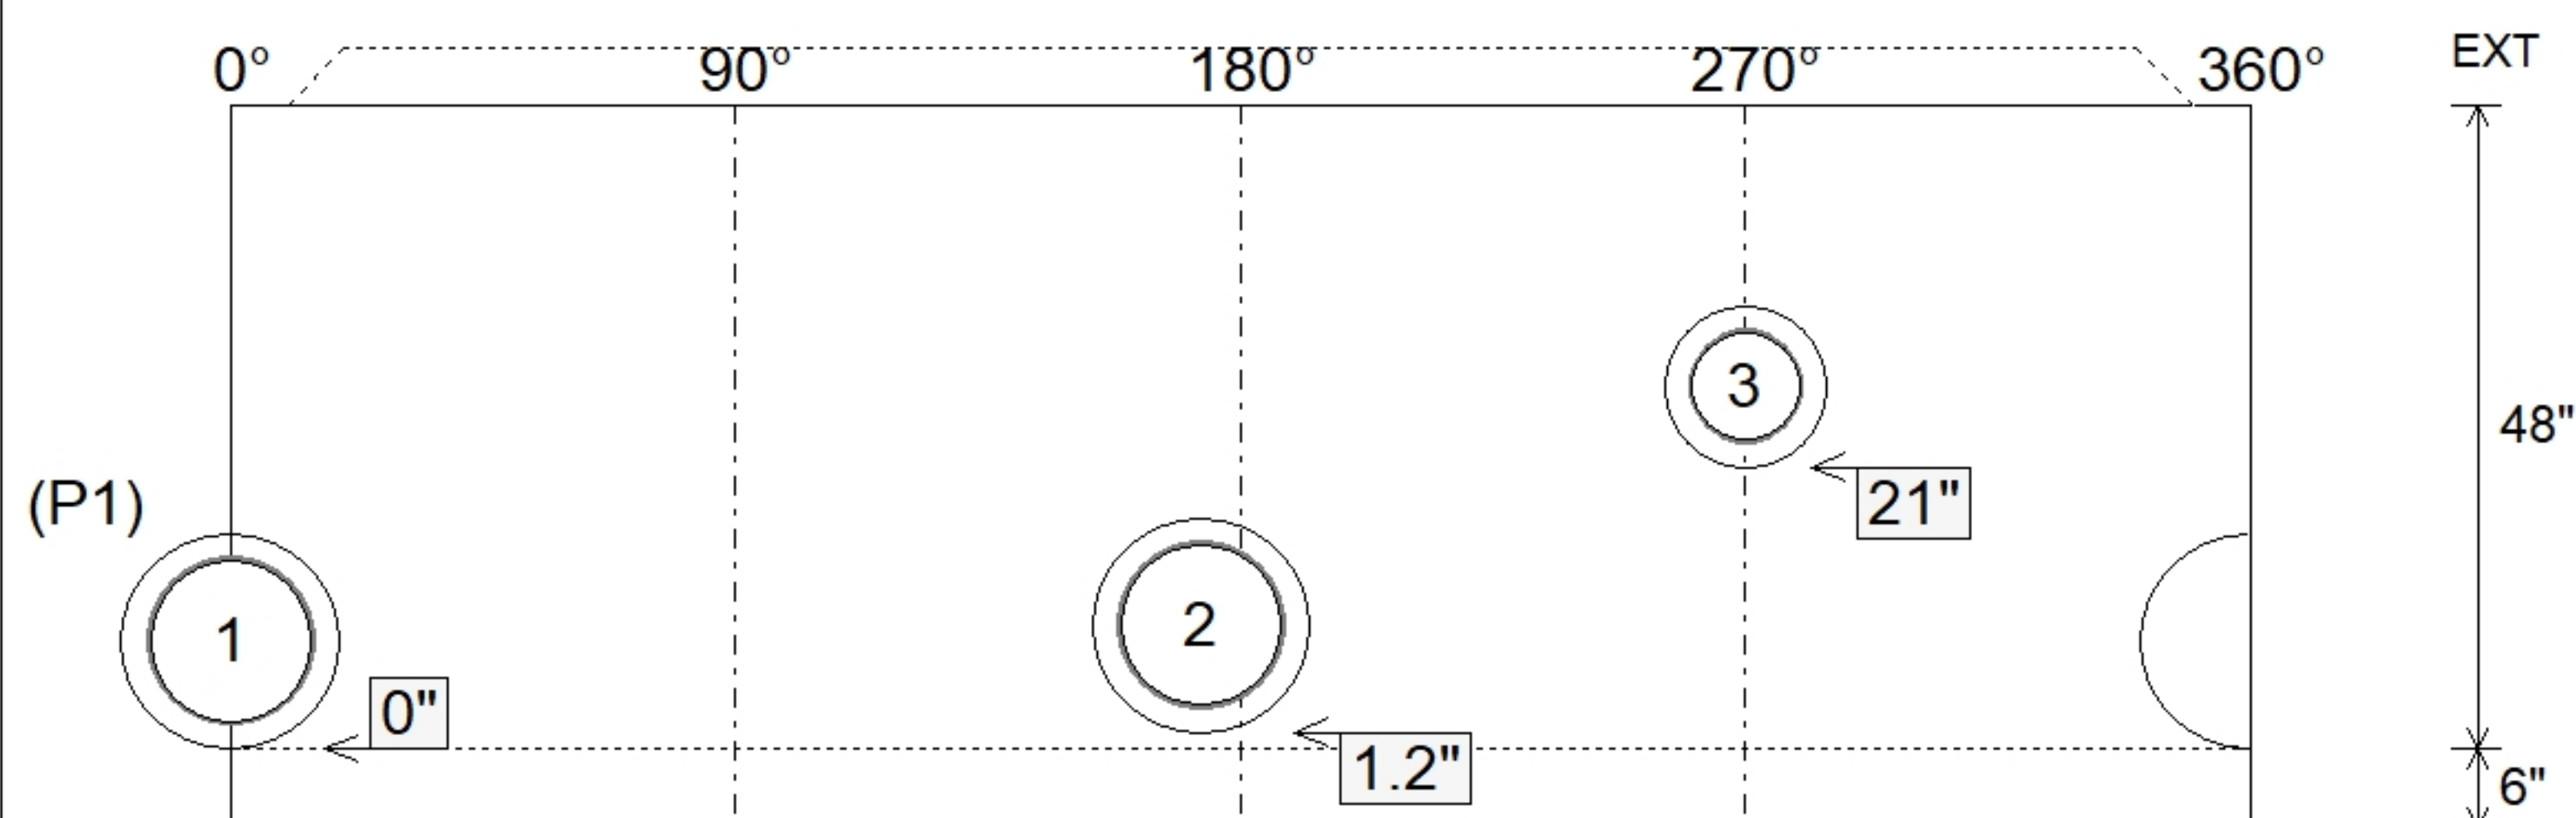

SUBMITTAL  
APPROVED BY:
