

Job Name: 25-3182 - Silverstone Subdivision  
 Job Location: Bowling Green, KY  
 Contractor: R.A. Alexander & Sons, Inc.

Plant: 100

3/10/2026 9:41:51 AM

Tech: Jared - F

PC: T. Lewis



**Structure ID: A4**



**P2 MH048CN36**

**ECC CONE w/ 24" HOLE**

- P4) 24" - CASTING HEIGHT - 7"
- P3) 24" - GRADE RING - 3"
- P2) 48" - ECC CONE w/ 24" HOLE - 36"
- P1) 48" - MH BASE - 36"
- 1) JOINT WRAP - 12" WD x 048" MAC WRAP
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) CASTING - HOE MC-375 F/C Sanitary
- 1) 48" - Conseal CS-102 1.00" (Double)
- 3) A-Lok - 0285
- 5) MH Step ML-10-TDS-NCR - 10"

- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
  2. CONCRETE = 4,000 PSI AT 28 DAYS.
  3. CASTING BY ICAST (HOE MC-375 F/C SANITARY).
- REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
  - RISER/WALLS (As .12)
  - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

0 lb  
 202 lb  
 3000 lb  
 3751 lb  
 0 lb  
 1440 lb  
 271 lb  
 0 lb  
 3 lb  
 0 lb  
 -----  
 Structure Total: 8667 lb

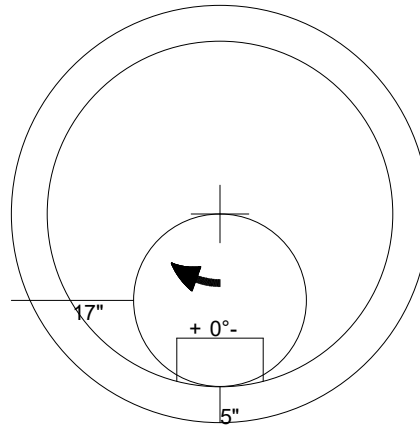

48" - ECC CONE w/ 24" HOLE - 36" - (P2)

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 36"

Weight (Net): 3000 lb  
 Volume (Net): 0.5cu.yd
