

Contractor: Eaton Asphalt

TECH: Jared - A

Plant: 100



Size: 24" x 30"

Rim to Invert: 4.67'

Floor Height: 8"


Slack: 0.04"

1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST.
2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W..
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB (SPACED AT 12" CC) AROUND THE 15" X 27" HOLE


P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 40"
1) CASTING - HOE KY-230-G F/G (GRADE)
1) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
1) Hole - 20
2) Hole - 4

0 lb
963 lb
4767 lb
237 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 5967 lb

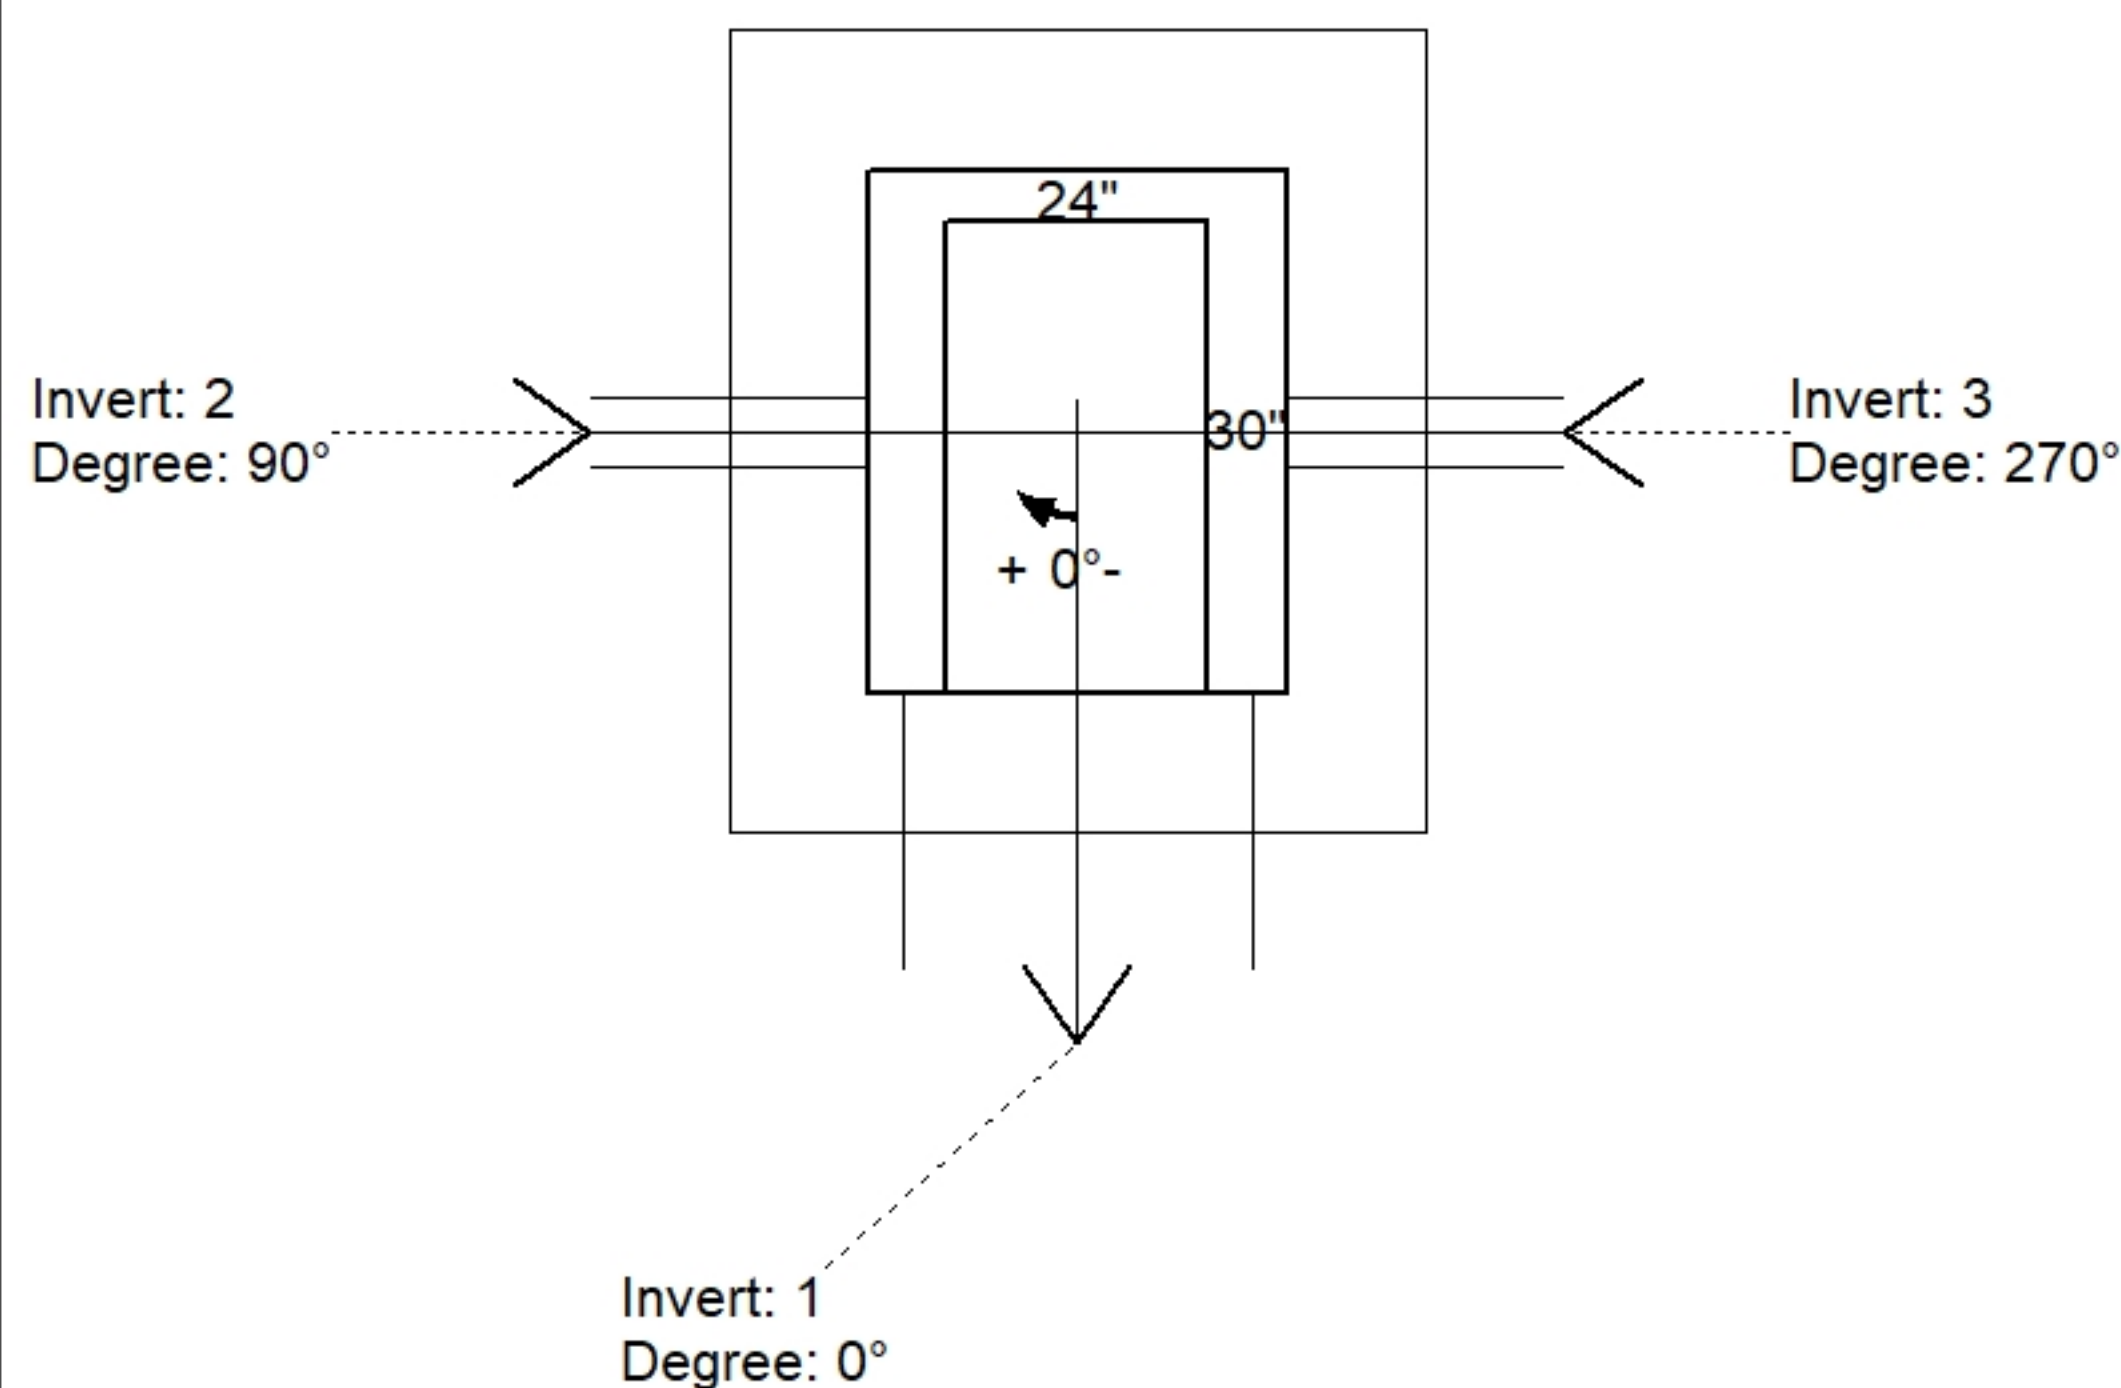

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	891.63'							
Reducer								
Invert 1	886.96'	0°	15" ADS N-12	18"	20"	Hole 20	-2.5"	P1
Invert 2	889.62'	90°	4" WEEP HOLE	4"	4"	Hole 4	31.92"	P1
Invert 3	889.62'	270°	4" WEEP HOLE	4"	4"	Hole 4	31.92"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

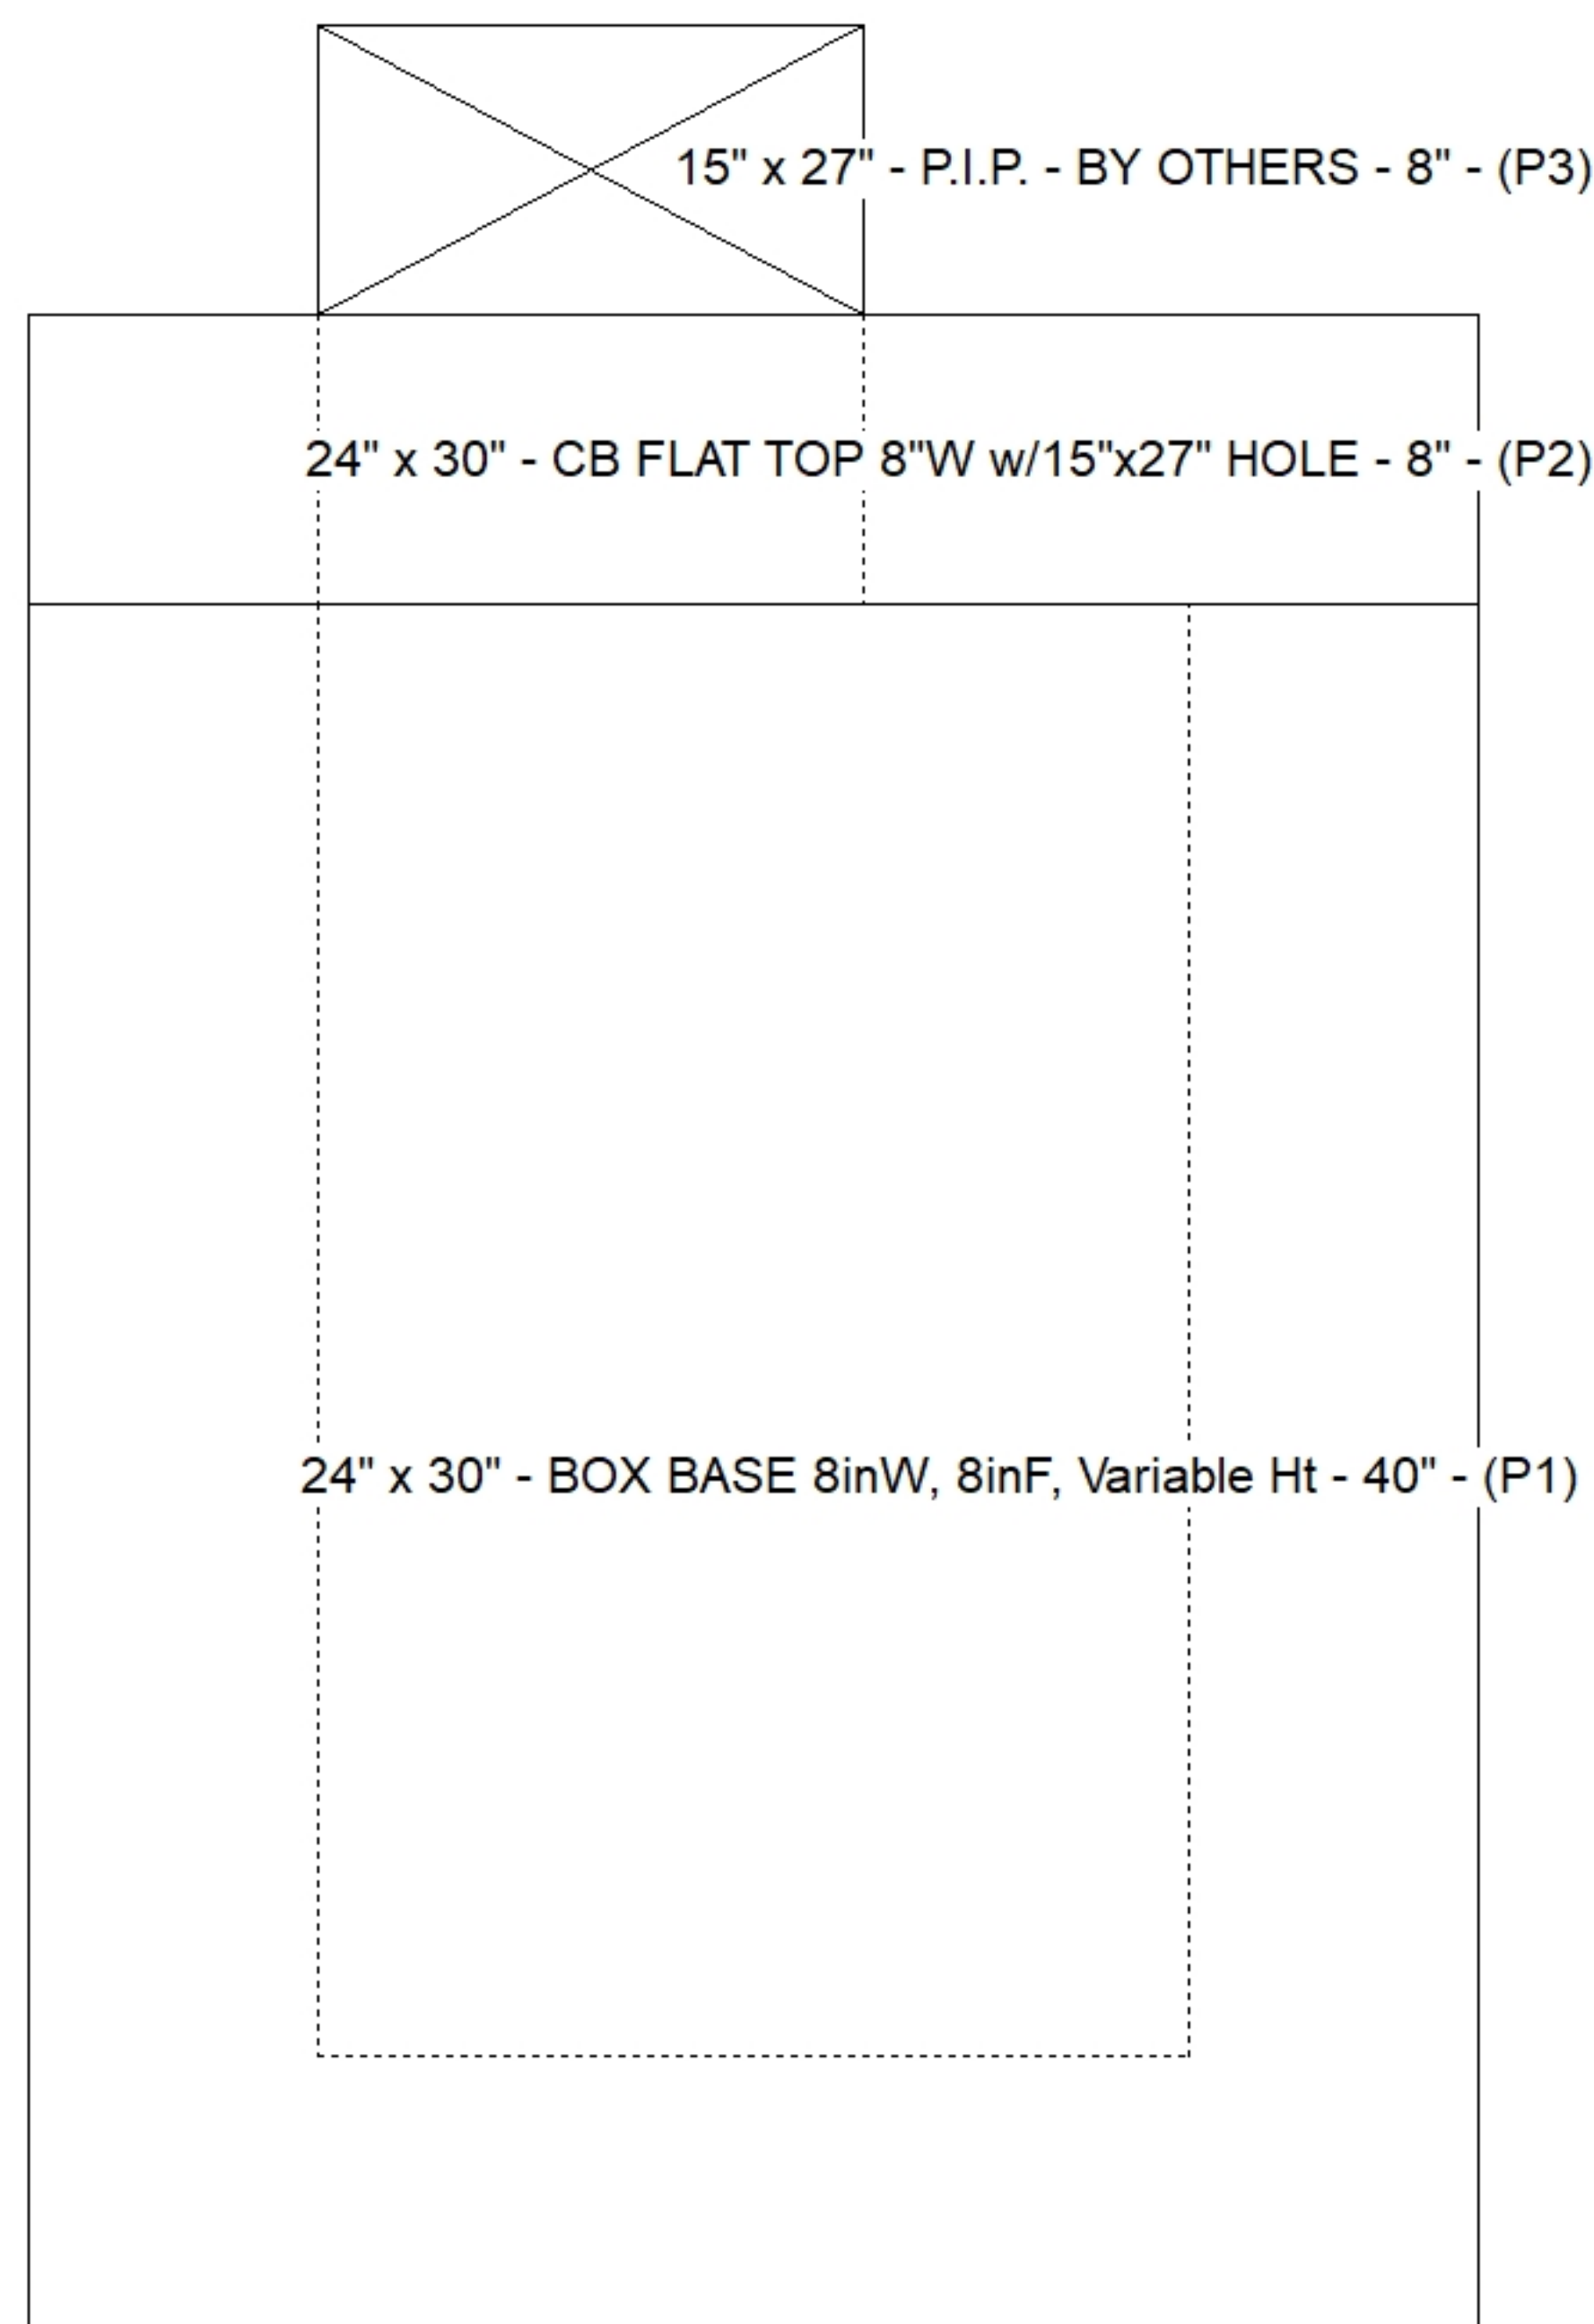

Default - Interior Dimensions

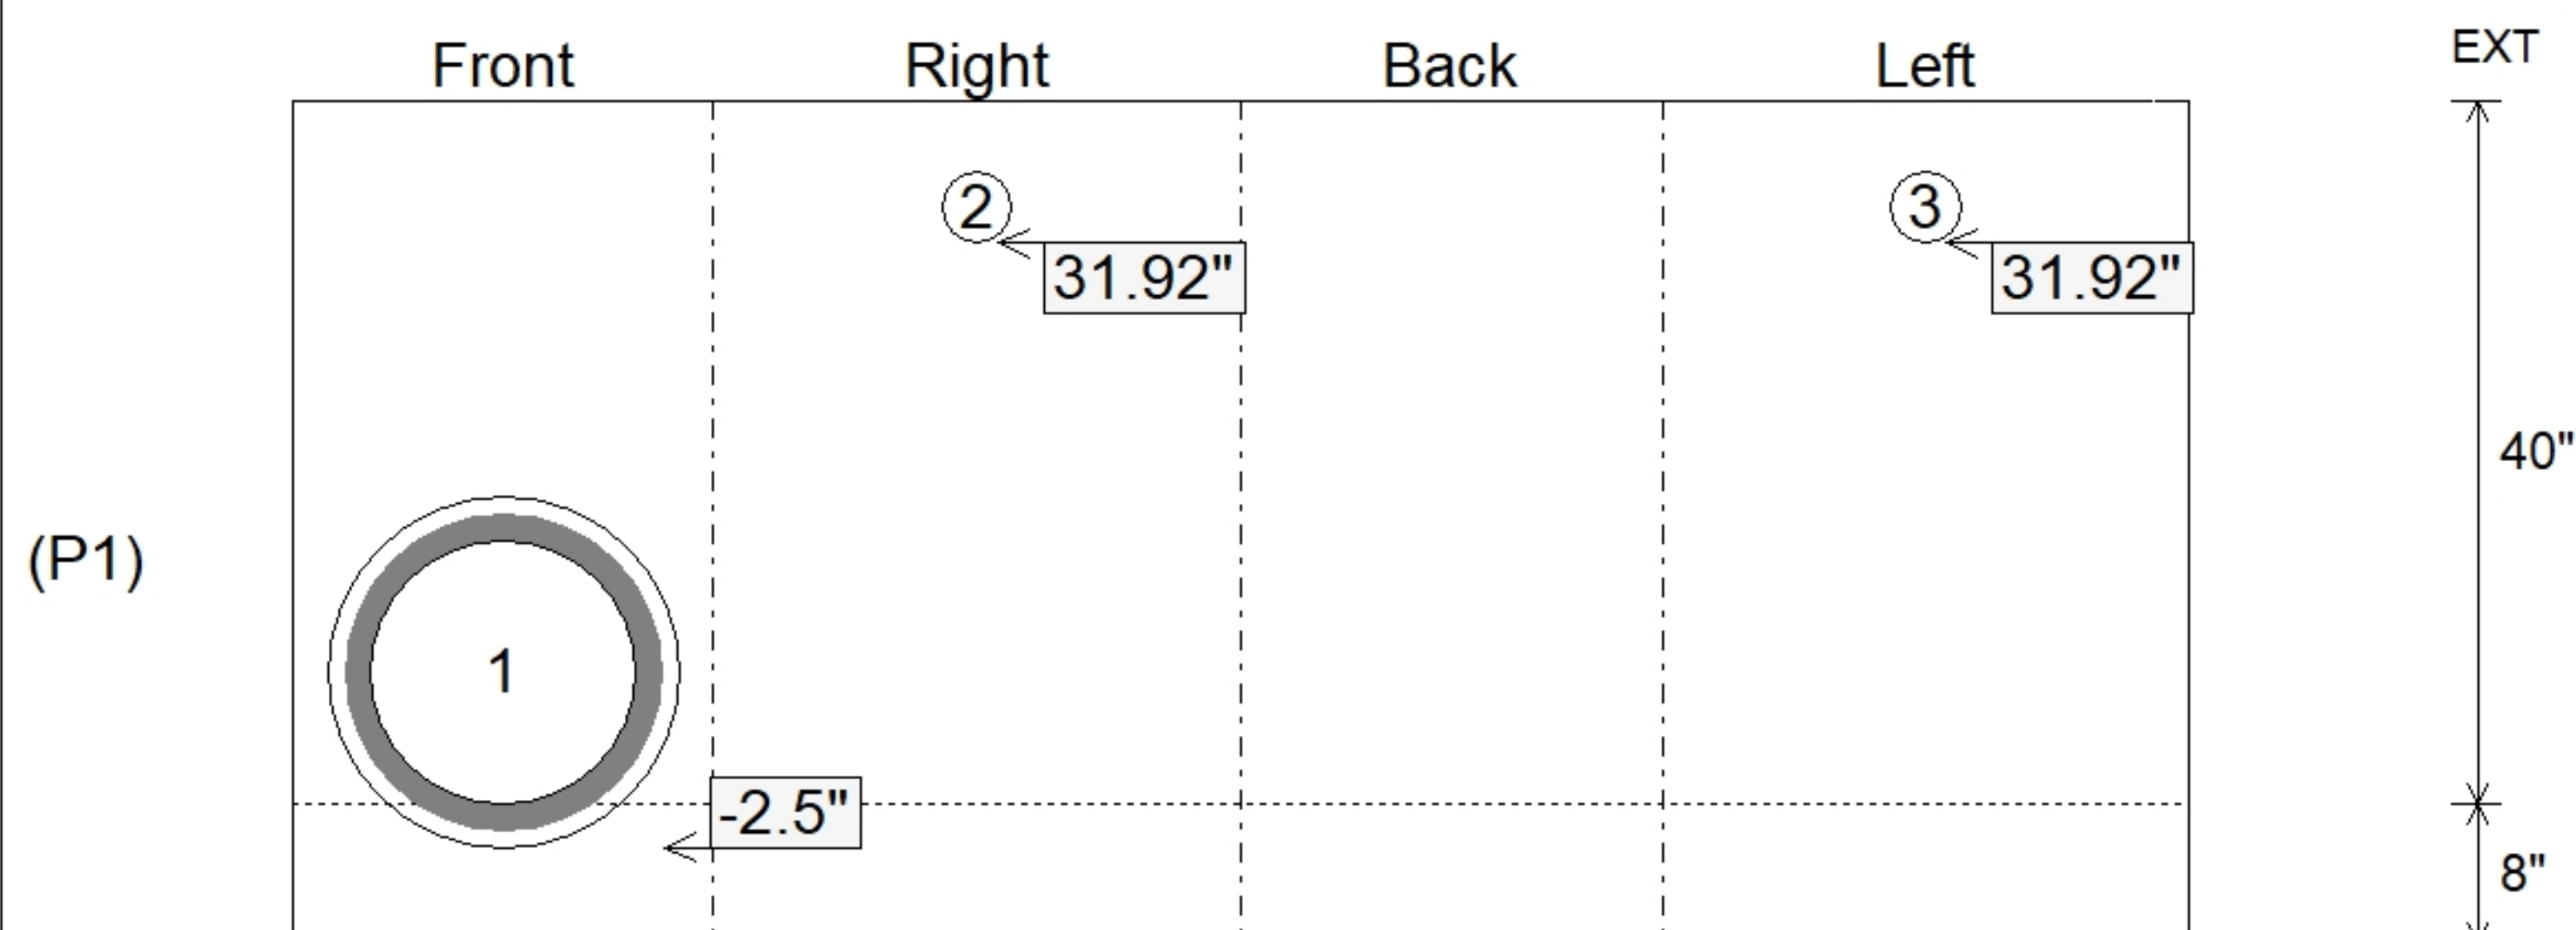

Submittal Drawing
7/10/2026 11:54:00 AM

SUBMITTAL
APPROVED BY:
