




Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt				Plant: 100 6/5/2026 11:57:56 AM		Tech: Jared - A PC: J. Jarvis				
Structure ID: 529										
P1 BX3636-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE T/F - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 25" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast) 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 24 2) Hole - 8					3400 lb 5270 lb 1235 lb 4446 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TY A / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-206 FRAME & COVER "STORM" SUPPLIED BY iCAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP 7. INVERT 2 OFFSET 14" FROM CENTER OF WALL			
Rim: 834.66' Rim to Invert: 5.09' Slack: 0.08" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	829.57'	340°	23.25"	18" ADS N-12	22"	Hole 24	24"	25.54"	-3"	6.25"
Invert 2	830.82'	90°	12"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	13"	-14"
Invert 3	830.82'	180°	26"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	13"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

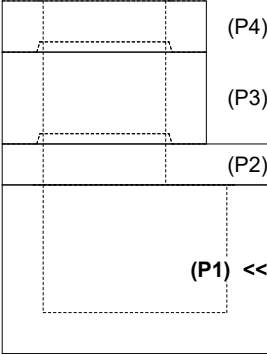

UPSIDE-DOWN VIEW (int. dimensions)

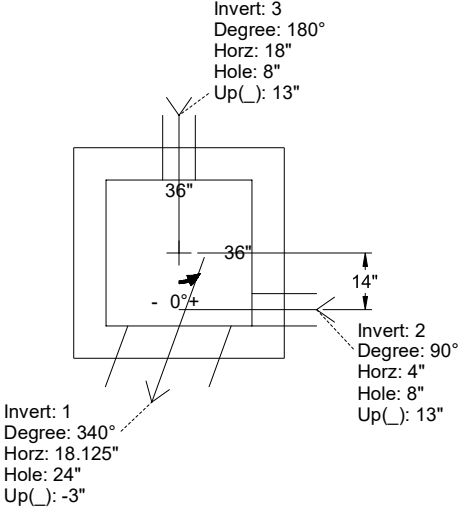

INSIDE WALL DIMENSIONS				
				

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 4446 lb Volume (Net): 1.14cu.yd
----------------------------------	-------------------------------	--	--	--
