

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

6/5/2026 9:04:28 AM

Tech: Jared - A

PC: J. Jarvis



Structure ID: 542

P3 BX024030-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE F/F



- P4) 15" x 27" - P.I.P. - BY OTHERS - 8"
P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
P2) 24" x 30" - BOX RISER 8inW F/G - 24"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 35"
1) CASTING - HOE KY-230-G F/G (GRADE)
2) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
3) Hole - 24
2) Hole - 4

Structure Total: 7128 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC DBI 13G / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: DOUBLE MAT #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. KY-230G FRAME & GRATE SUPPLIED BY ICAST - POURED IN PLACE BY OTHERS
5. WET STICK #5 BAR @ 12" C.C. (GRADE 60) OUT TOP OF FLAT LID AROUND 15" X 27" OPENING FOR FIELD POUR TIE-IN - MIN. 4" PENETRATION INTO FLAT LID
6. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
7. TOP SURFACE TO RECEIVE FLOATED FINISH

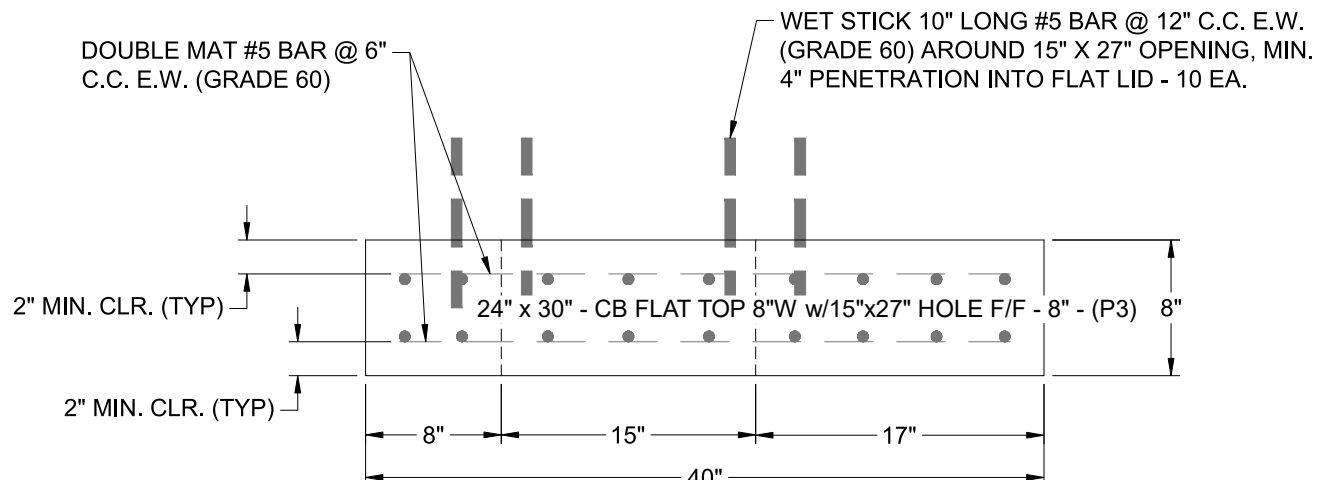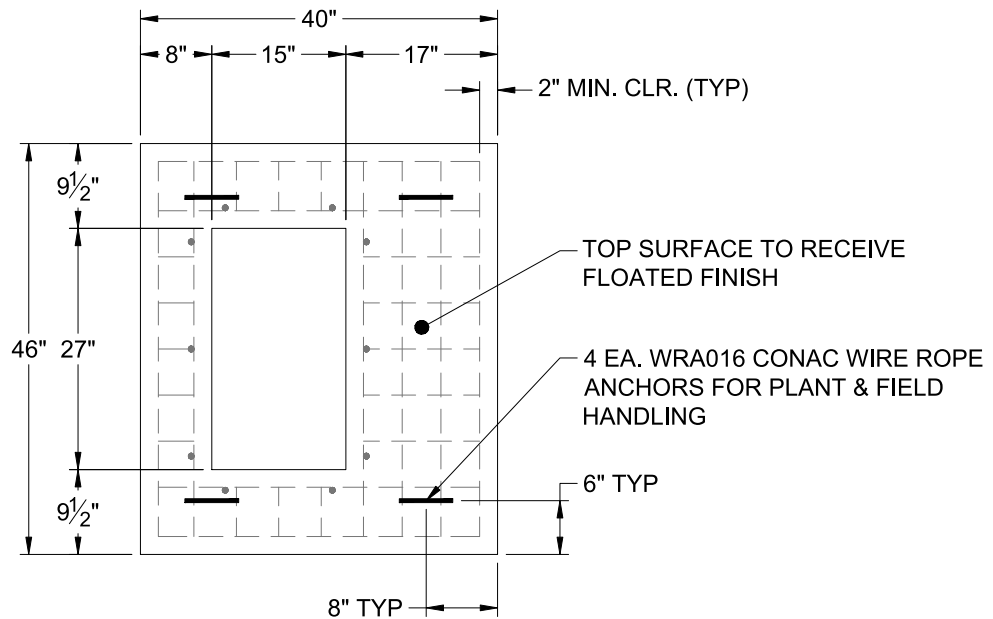

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb
Volume (Net): 0.25cu.yd
