

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

6/30/2026 2:47:16 PM

Tech: Jared - A

PC: J. Jarvis



Structure ID: 603

P2 MH048RS60

MH RISER



- P5) 24" - CASTING HEIGHT - 8"
P4) 48" - ECC CONE w/ 24" HOLE - 36"
P3) 48" - MH RISER - 36"
P2) 48" - MH RISER - 60"
P1) 48" - MH BASE Custom Ht - 70"
1) CASTING - HOE KY-510 F/C (KY TY.2)
3) 48" - Conseal CS-102 1.00"
3) Hole - 24
17) MH Step ML-10-TDS-NCR - 10"

- 0 lb
3000 lb
2515 lb
4192 lb
5629 lb
510 lb
0 lb
0 lb
0 lb
Structure Total: 15845 lb
- Structure Notes:
KYTC STATE PROJECT
1. HOE KY-510 F/C (KY TY2) PROVIDED BY ICAST.
2. PER KYTC MH A / ASTM C478 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60.)
- CONE (As .62)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 919.02' Rim to Invert: 17.32' Slack: 0.84" Sump: 3" Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

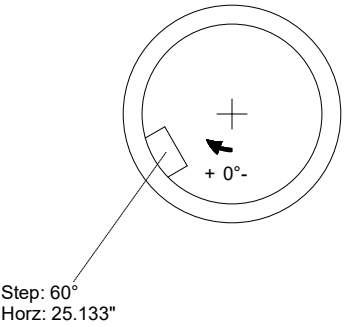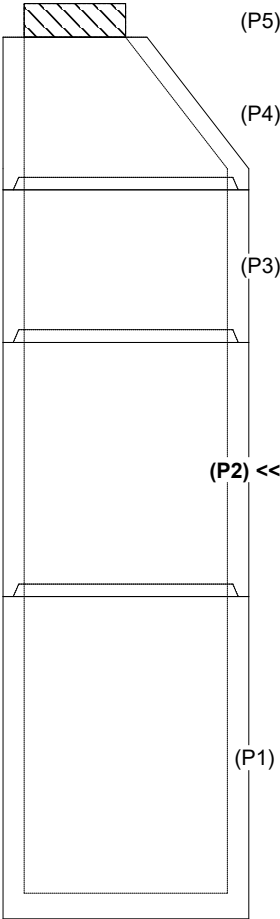

INSIDE WALL DIMENSIONS



Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 60"	Weight (Net): 4192 lb
Coating (Ext):	Seam Dn: Groove	Floor Height: 0"	Height (Ext): 60"	Volume (Net): 1.07cu.yd
