

Contractor: Eaton Asphalt

TECH: Jared - A


Plant: 100



Slack: 0.08"

13149 lb


Structure Total:	13148 lb
------------------	----------

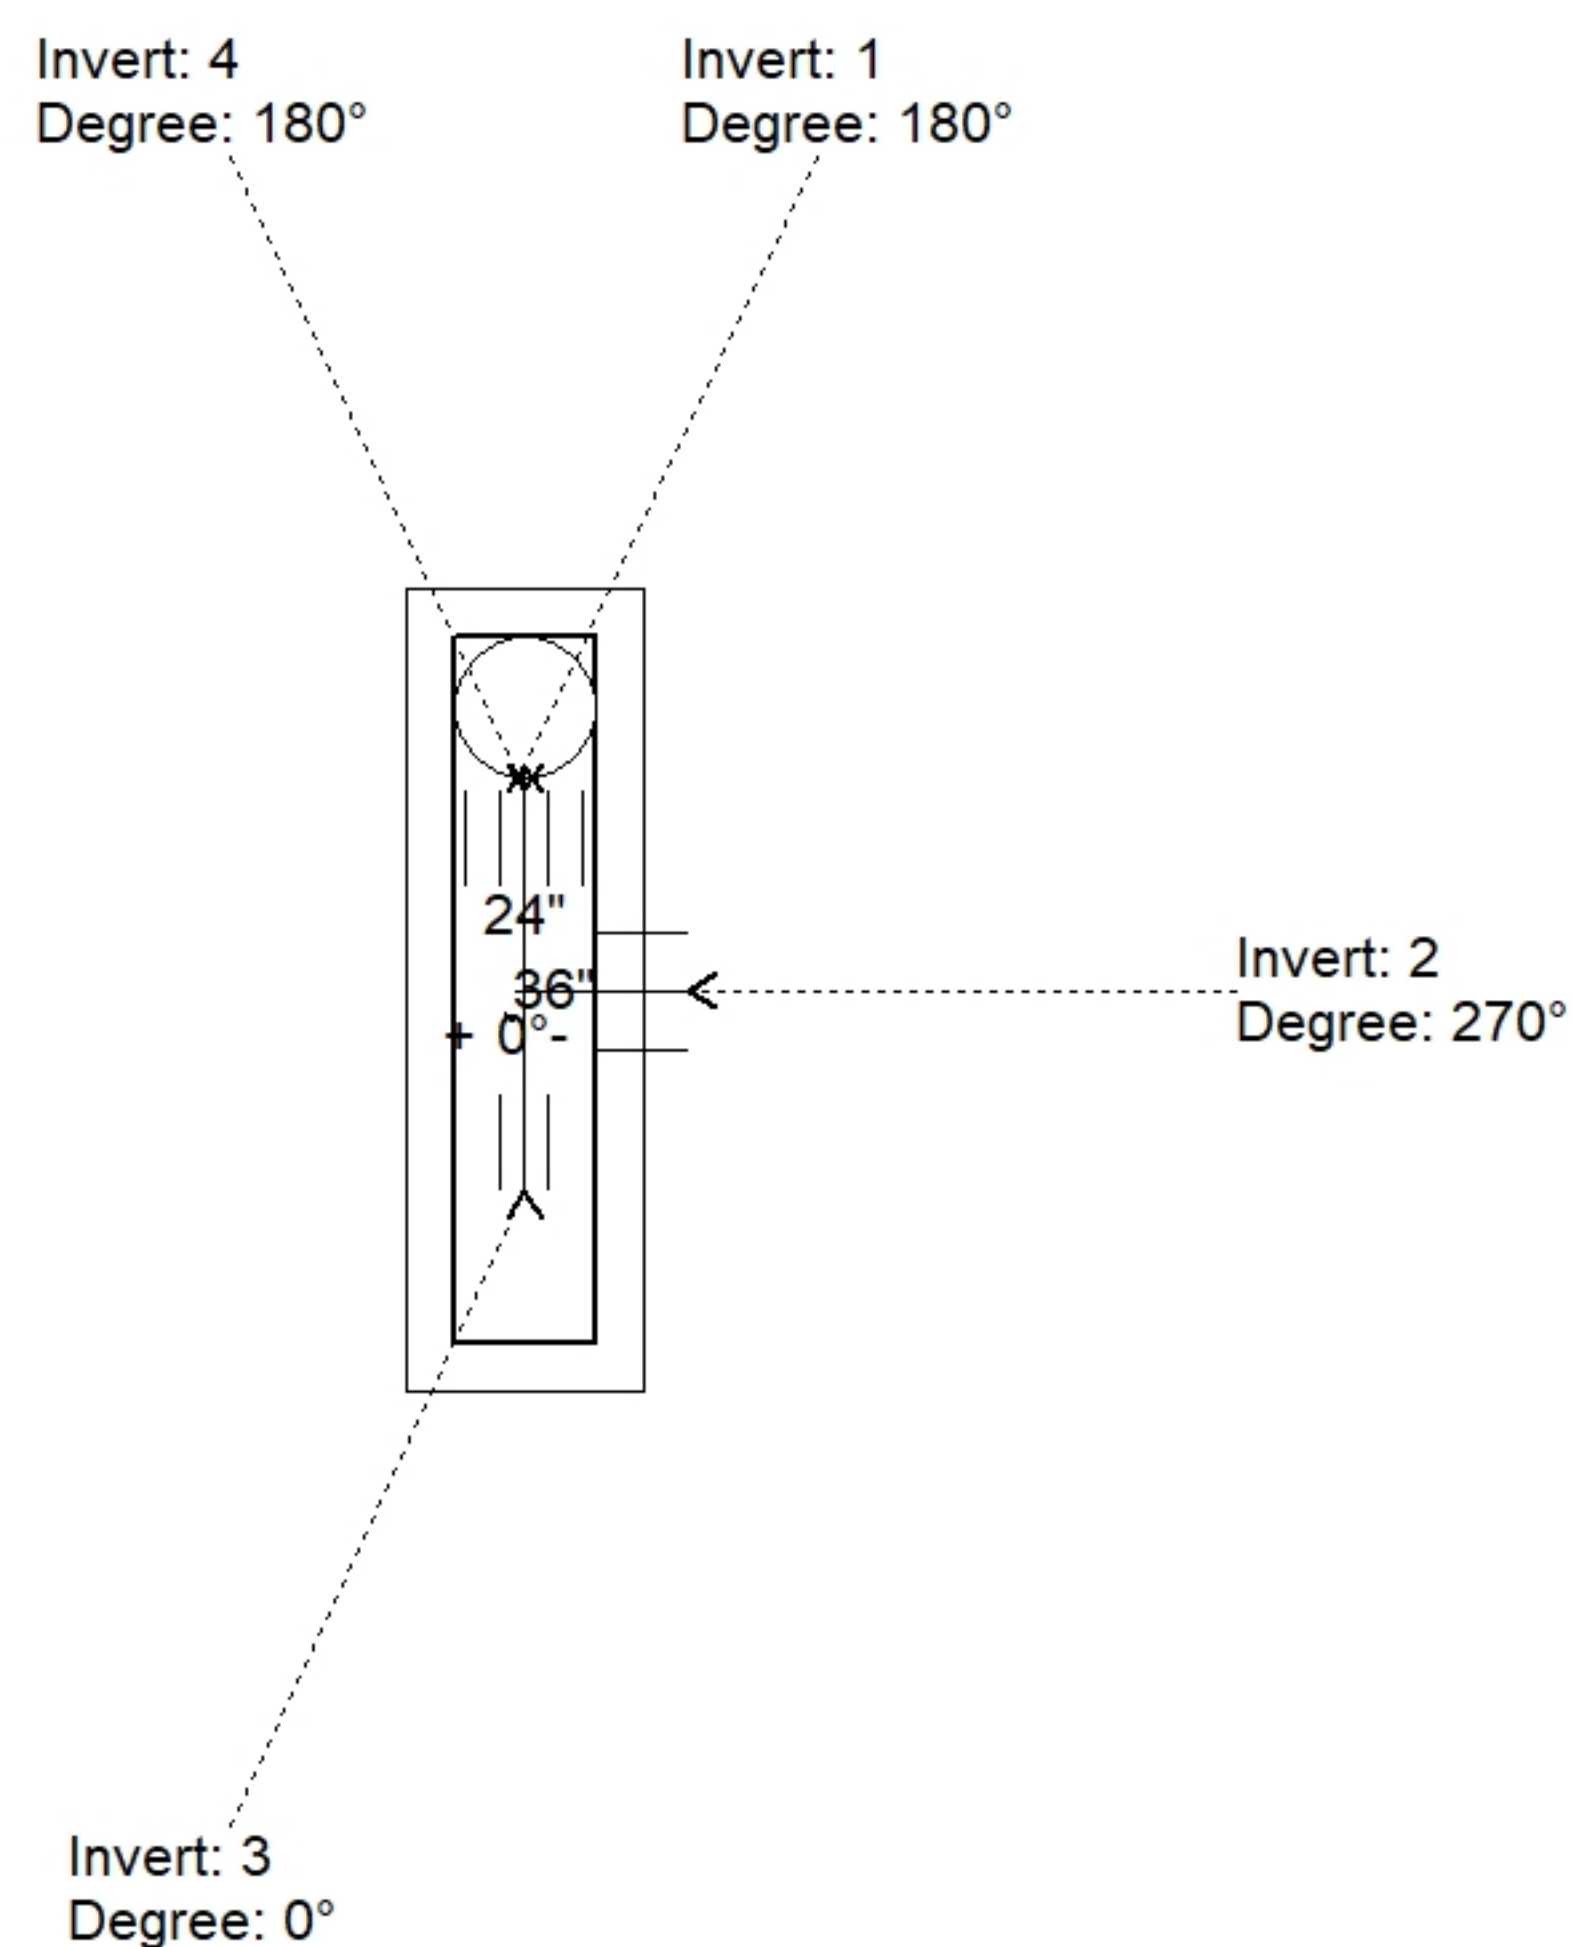

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	933.86'							
Reducer								
Invert 1	928.77'	180°	15" ADS N-12	18"	20"	Hole 20	-2.5"	P1
Invert 2	928.77'	270°	15" ADS N-12	18"	20"	Hole 20	-2.5"	P1
Invert 3	930.69'	0°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	21.04"	P1
Invert 4	930.69'	180°	4" HDPE (perf pipe)	4.8"	8"	Hole 8	21.04"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33" - (P1)

(P1)

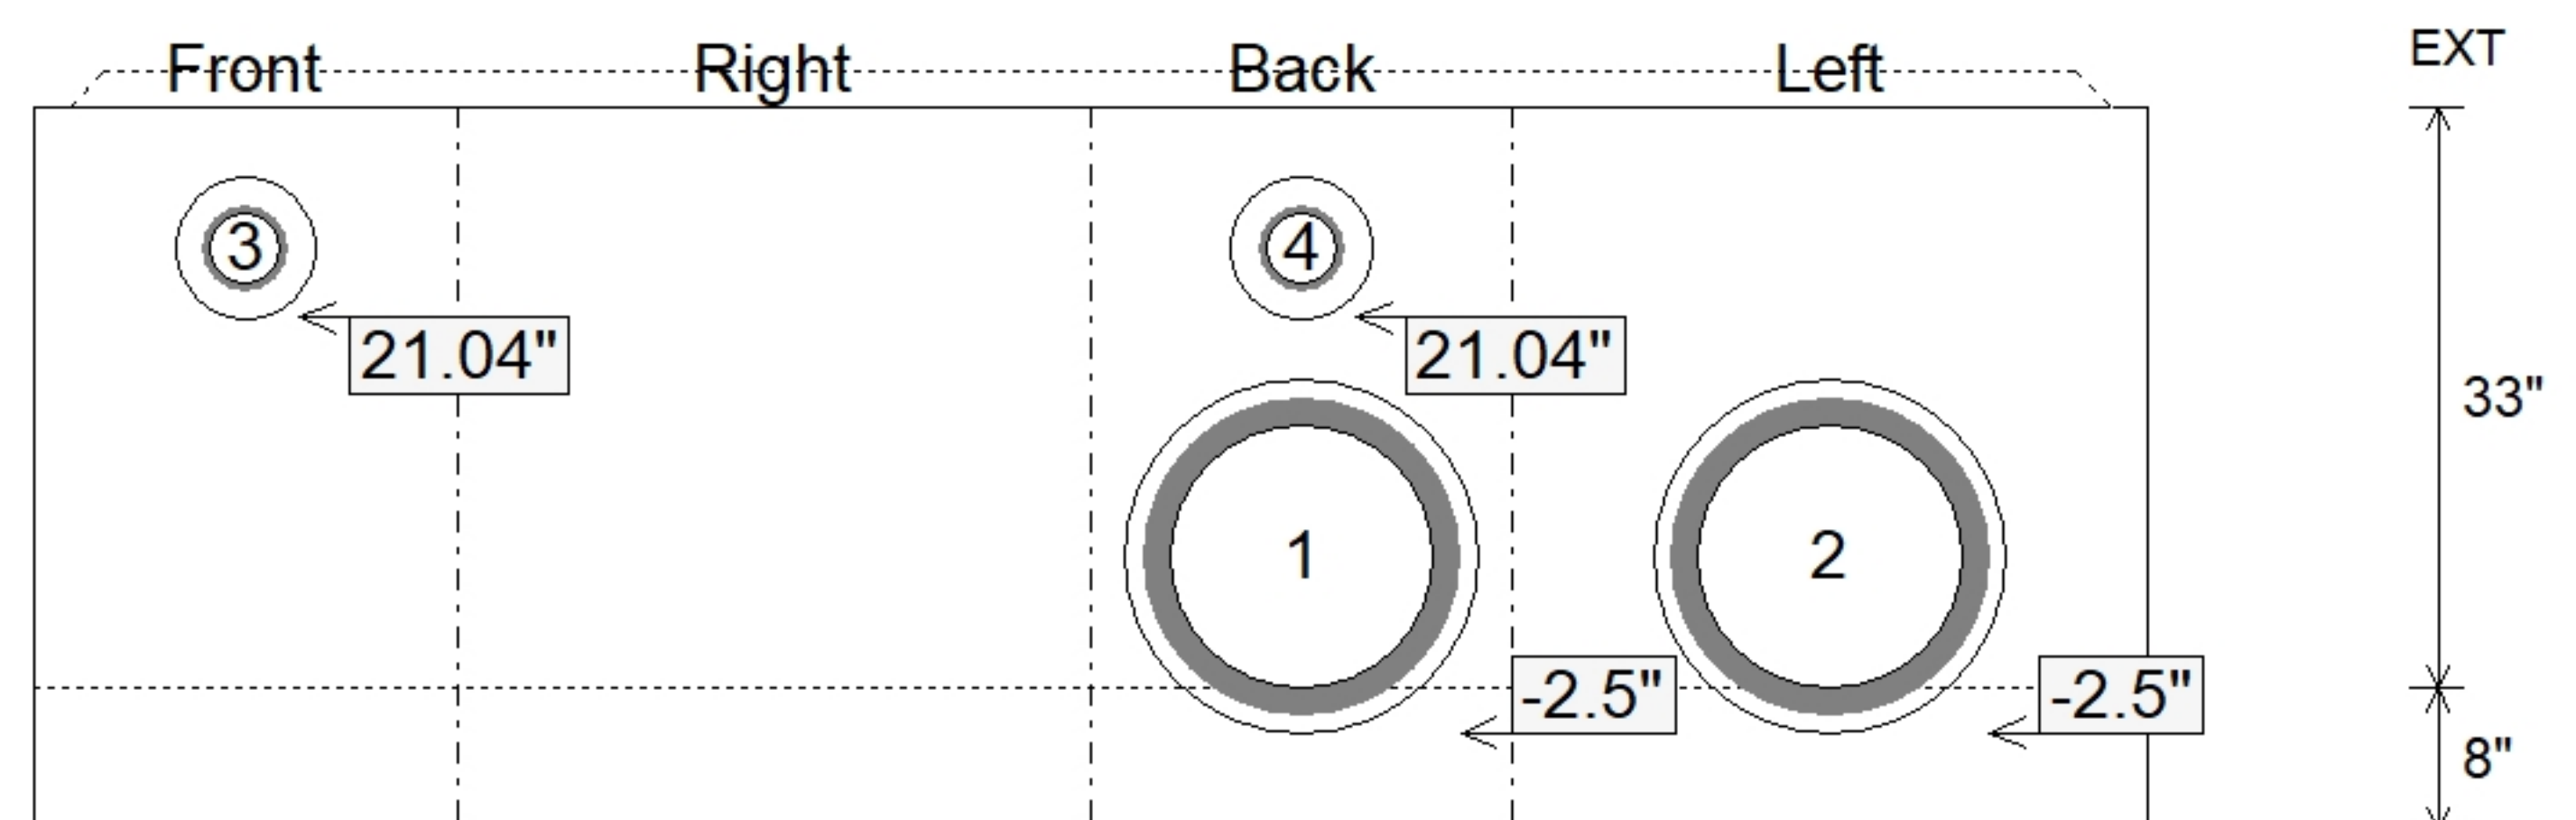

SUBMITTAL
APPROVED BY:
