




Structure ID: ICAST LI7 (4)


P1 HWSF24

24" - SLOPED & FLARED HEADWALL F/F


DIMENSIONS									
PIPE Ø	A	B	C	D	E	F	G	H	I
24"	3'-8"	4'-4"	2'-10"	1'-8"	5'-0"	4"	3"	2'-10"	6'-0"
									WEIGHT 4,956 LBS.

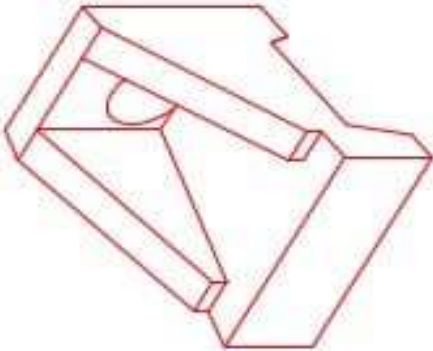


ISOMETRIC VIEW
24" HEADWALL

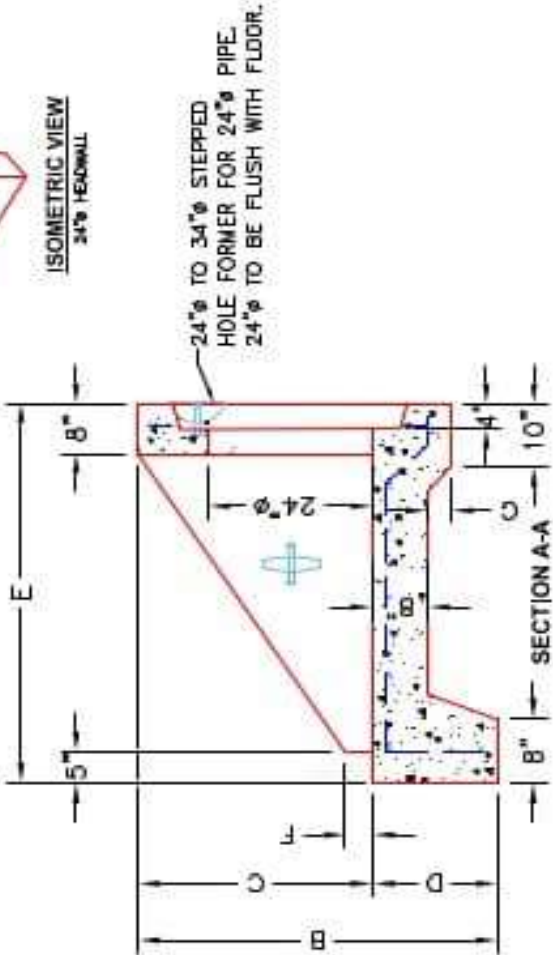

SECTION A-A

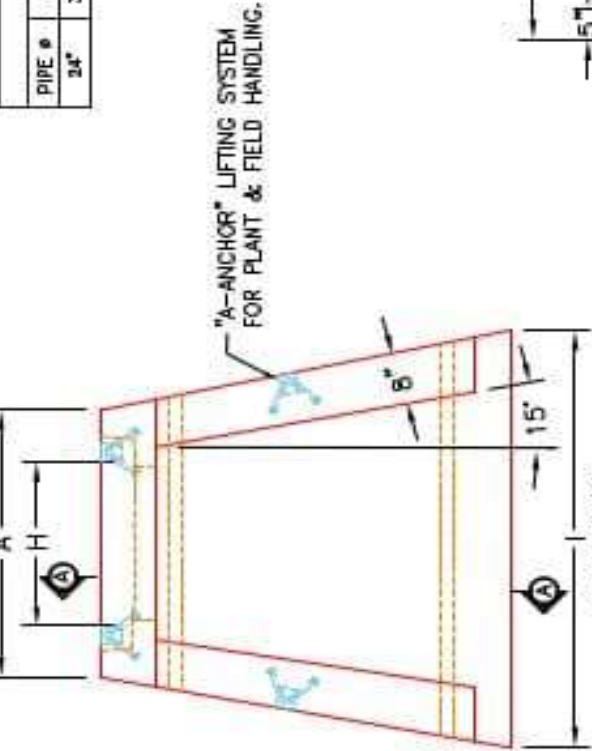


PLAN VIEW

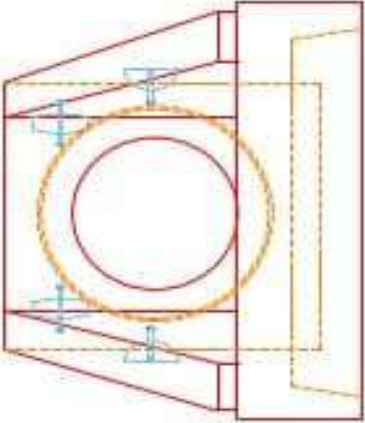

FRONT ELEVATION

- NOTES:
1. CONCRETE 4000 PSI @ 28 DAYS.
 2. REINFORCING #4 BAR @ 12" C/C E.W. - GRADE 60, (WITH 3" CONCRETE COVER MINIMUM)
 3. REINFORCING BARS TO BE TACK WELDED OR TIED.
 4. DRAWING TO BE USED IN CONJUNCTION WITH KYTC STD. DRAWING RCH-020-03 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
 5. CHAMFER ON ALL EXPOSED EDGES.

PRODUCTION WORK ORDER		PRODUCT I.D.: HWSF24		DESCRIPTION: KYTC 24" SLOPED & FLARED HEADWALL	
	QUALITY CONTROL CHECKLIST		PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: STOCK	
	☐ ALL DIMENSIONS CORRECT.		PLANT: BEAVER DAM, KY.	PROJECT: STOCK INVENTORY	
	☐ LIFTERS INSTALLED.		WEIGHT: 4,956 LBS.	STRUCTURE ID.: N/A	
	☐ STEPPED HF CORRECT SIZE.		TOP SECTION JOINT: N/A	QUOTE/SALES ORDER NO: N/A	
	☐ REINFORCING CORRECT.		BASE SECTION JOINT: N/A	CHECK: J.H. ROSS, PE	
	☐ DISSIPATOR BLOCK INSTALLED.		QC CHECK INITIALS:	DATE: REV. 4/22/24	
	☐ EDGES CHAMFERED.			DRAWING: N. RICHARDS	
	☐ ALL PATCHWORK ACCEPTABLE.			SCALE: NTS PG. 1 of 1	

