

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)  
Job Location: Independence, KY  
Contractor: Eaton Asphalt

Plant: 100  
6/10/2026 11:59:14 AM

Tech: Jared - A  
PC: J. Jarvis




Structure ID: ICAST LI7 (8)


P1 HWSF24

24" - SLOPED & FLARED HEADWALL F/F


| DIMENSIONS |       |       |        |       |       |    |    |        |            |
|------------|-------|-------|--------|-------|-------|----|----|--------|------------|
| PIPE Ø     | A     | B     | C      | D     | E     | F  | G  | H      | I          |
| 24"        | 3'-8" | 4'-4" | 2'-10" | 1'-8" | 5'-0" | 4" | 3" | 2'-10" | 6'-0"      |
|            |       |       |        |       |       |    |    |        | WEIGHT     |
|            |       |       |        |       |       |    |    |        | 4,956 LBS. |

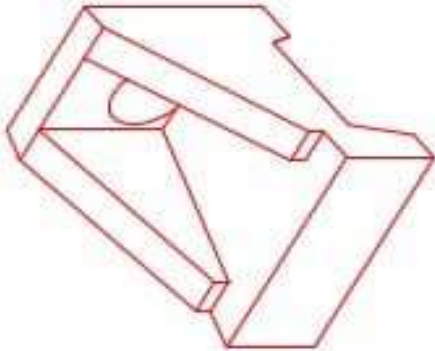


ISOMETRIC VIEW  
24" HEADWALL

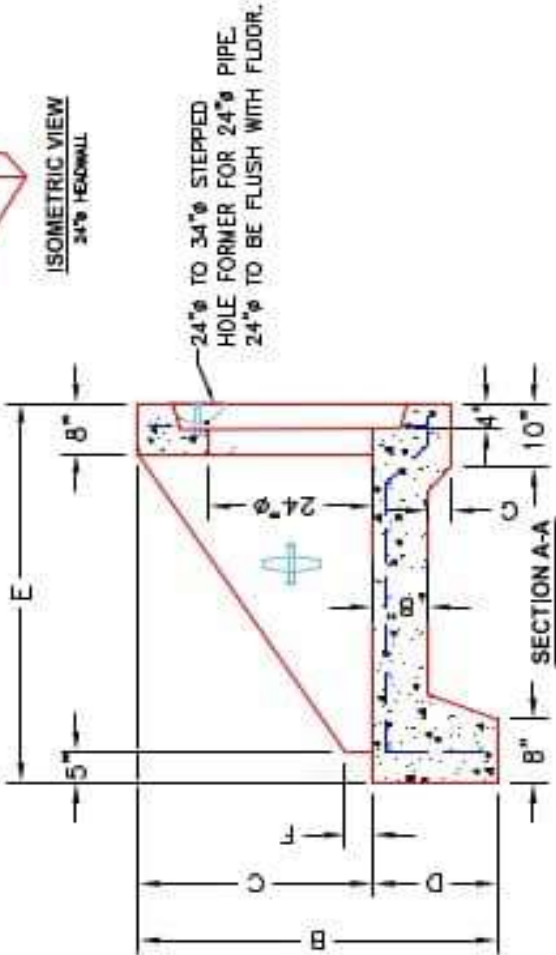

SECTION A-A

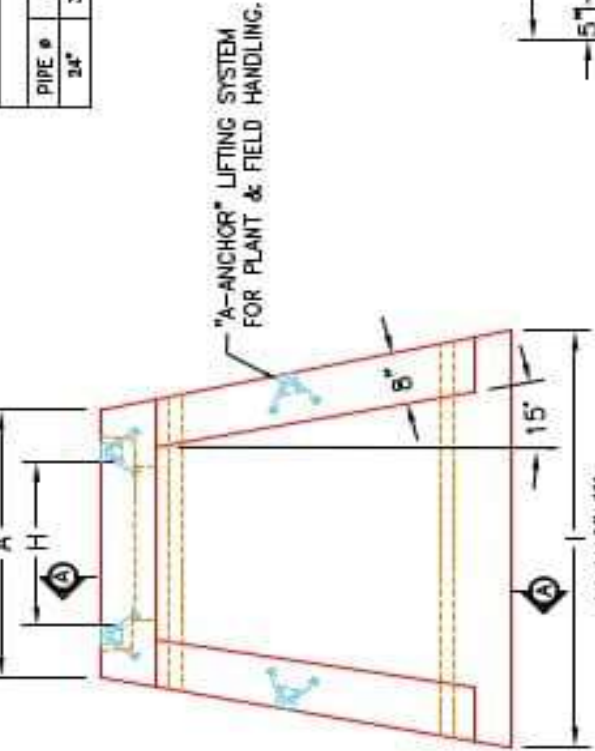


PLAN VIEW

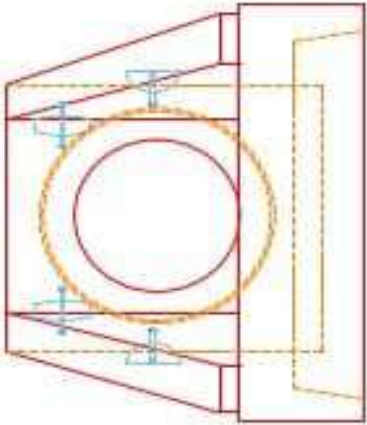

FRONT ELEVATION

- NOTES:
1. CONCRETE 4000 PSI @ 28 DAYS.
  2. REINFORCING #4 BAR @ 12" O.C. E.W. - GRADE 60, (WITH 3" CONCRETE COVER MINIMUM)
  3. REINFORCING BARS TO BE TACK WELDED OR TIED.
  4. DRAWING TO BE USED IN CONJUNCTION WITH KYTC STD. DRAWING RCH-020-03 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
  5. CHAMFER ON ALL EXPOSED EDGES.

| PRODUCTION WORK ORDER                                                                 |                                                      | PRODUCT I.D.: HWSF24 |                             | DESCRIPTION: KYTC 24" SLOPED & FLARED HEADWALL |  |
|---------------------------------------------------------------------------------------|------------------------------------------------------|----------------------|-----------------------------|------------------------------------------------|--|
|  | QUALITY CONTROL CHECKLIST                            |                      | PRODUCT VIEW: RIGHT SIDE UP | CUSTOMER: STOCK                                |  |
|                                                                                       | <input type="checkbox"/> ALL DIMENSIONS CORRECT.     |                      | PLANT: BEAVER DAM, KY.      | PROJECT: STOCK INVENTORY                       |  |
|                                                                                       | <input type="checkbox"/> LIFTERS INSTALLED.          |                      | WEIGHT: 4,956 LBS.          | STRUCTURE ID.: N/A                             |  |
|                                                                                       | <input type="checkbox"/> STEPPED HF CORRECT SIZE.    |                      | TOP SECTION JOINT: N/A      | QUOTE/SALES ORDER NO: N/A                      |  |
|                                                                                       | <input type="checkbox"/> REINFORCING CORRECT.        |                      | BASE SECTION JOINT: N/A     | CHECK: J.H. ROSS, PE                           |  |
|                                                                                       | <input type="checkbox"/> DISSIPATOR BLOCK INSTALLED. |                      | QC CHECK INITIALS:          | DRAWING: N. RICHARDS                           |  |
|                                                                                       | <input type="checkbox"/> EDGES CHAMFERED.            |                      |                             | DATE: REV. 4/22/24                             |  |
|                                                                                       | <input type="checkbox"/> ALL PATCHWORK ACCEPTABLE.   |                      |                             | SCALE: NTS                                     |  |
|                                                                                       |                                                      |                      |                             | PG. 1 of 1                                     |  |

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
