



Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:43:53 PM		Tech: Jared - A PC: C. Goff				
Structure ID: MH 1											
P1		MH060BA60		MH BASE							
P3) 24" - CASTING HEIGHT - 7" P2) 60" - MH FLAT TOP w/ 24" ECC Hole - 13" P1) 60" - MH BASE - 60" 1) CASTING - HOE MC-420 F/C Storm 1) 60" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 40 Structure Total: 10842 lb						0 lb 2869 lb 7633 lb 340 lb 0 lb 0 lb 0 lb ----- 10842 lb		Structure Notes: 1. HOE MC-420 F/C STORM PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 790'		Rim to Invert: 6.5'		Slack: 0.55"		Sump: 2.55"		Step Position: 125°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	783.5'	0°	0"	30" HDPE	35.1"	Hole 40	40"	43.784"	0"	0"	
Invert 2	783.5'	250°	157.08"	30" HDPE	35.1"	Hole 40	40"	43.784"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

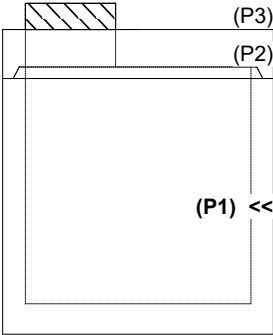

(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

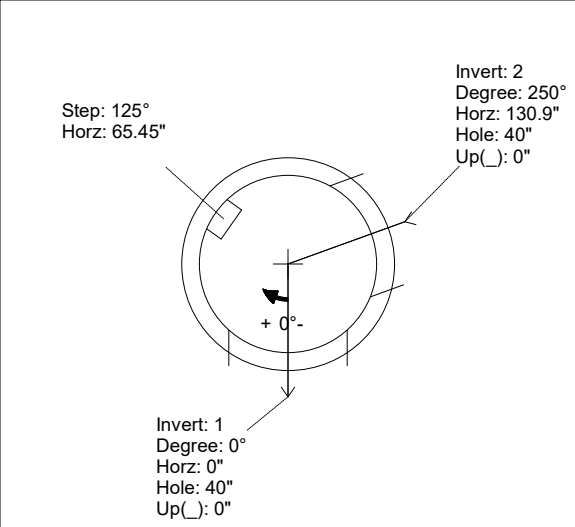


Step: 125°
Horz: 65.45"

Invert: 2
Degree: 250°
Horz: 130.9"
Hole: 40"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 40"
Up(): 0"

UPSIDE-DOWN VIEW (int. dimensions)

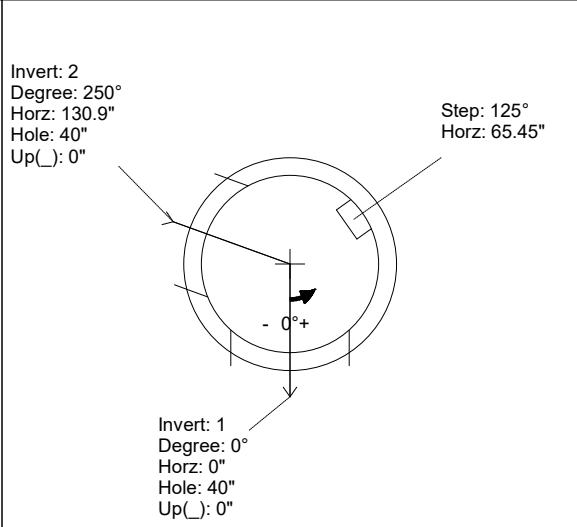


Step: 125°
Horz: 65.45"

Invert: 2
Degree: 250°
Horz: 130.9"
Hole: 40"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 40"
Up(): 0"

INSIDE WALL DIMENSIONS

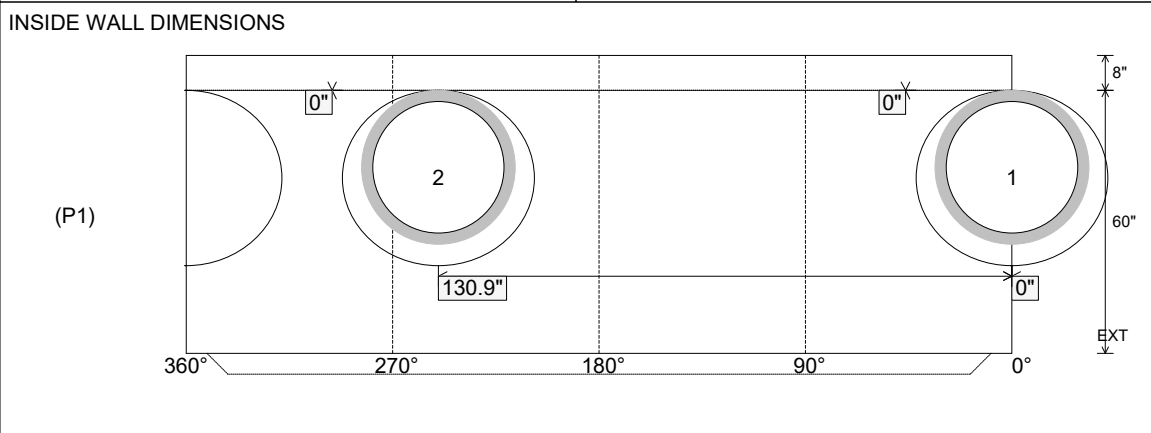

(P1)

0" X

2

130.9"

1

0"

360° 270° 180° 90° 0°

8"

60"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 7633 lb Volume (Net): 1.95cu.yd
----------------------------------	---------------------------------	--	--	--
