

Job Name: 25-3241P2 - Buck Hills Subdivision
Job Location: Lawrenceburg, KY 40342
Contractor: Edmonson Plumbing & Heating Supply

Plant: 100

7/24/2026 12:44:48 PM

Tech: Jared - A

PC: C. Goff



Structure ID: MH 1

P2 MH060LD13

MH FLAT TOP w/ 24" ECC Hole

- P3) 24" - CASTING HEIGHT - 7"
P2) 60" - MH FLAT TOP w/ 24" ECC Hole - 13"
P1) 60" - MH BASE - 60"
1) CASTING - HOE MC-420 F/C Storm
1) 60" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 40



Structure Total:

0 lb
2869 lb
7633 lb
340 lb
0 lb
0 lb
0 lb

10842 lb

Structure Notes:

1. HOE MC-420 F/C STORM PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

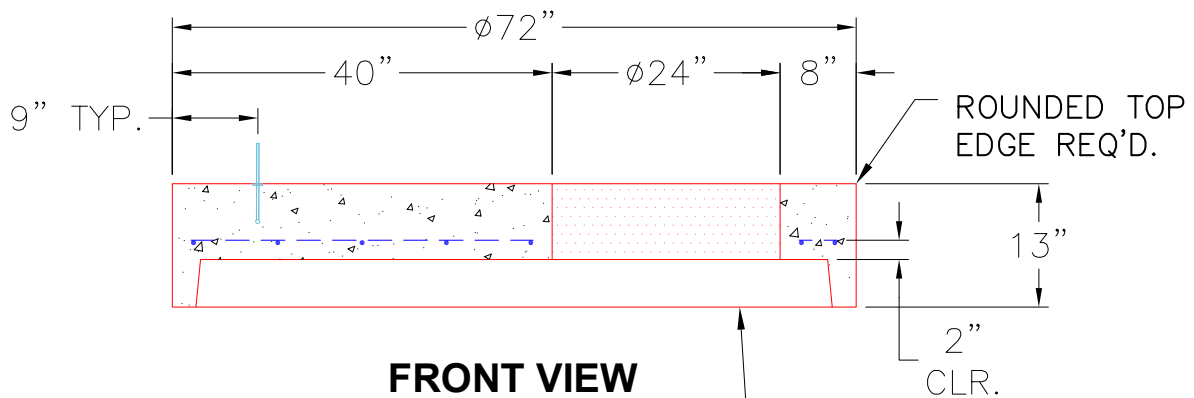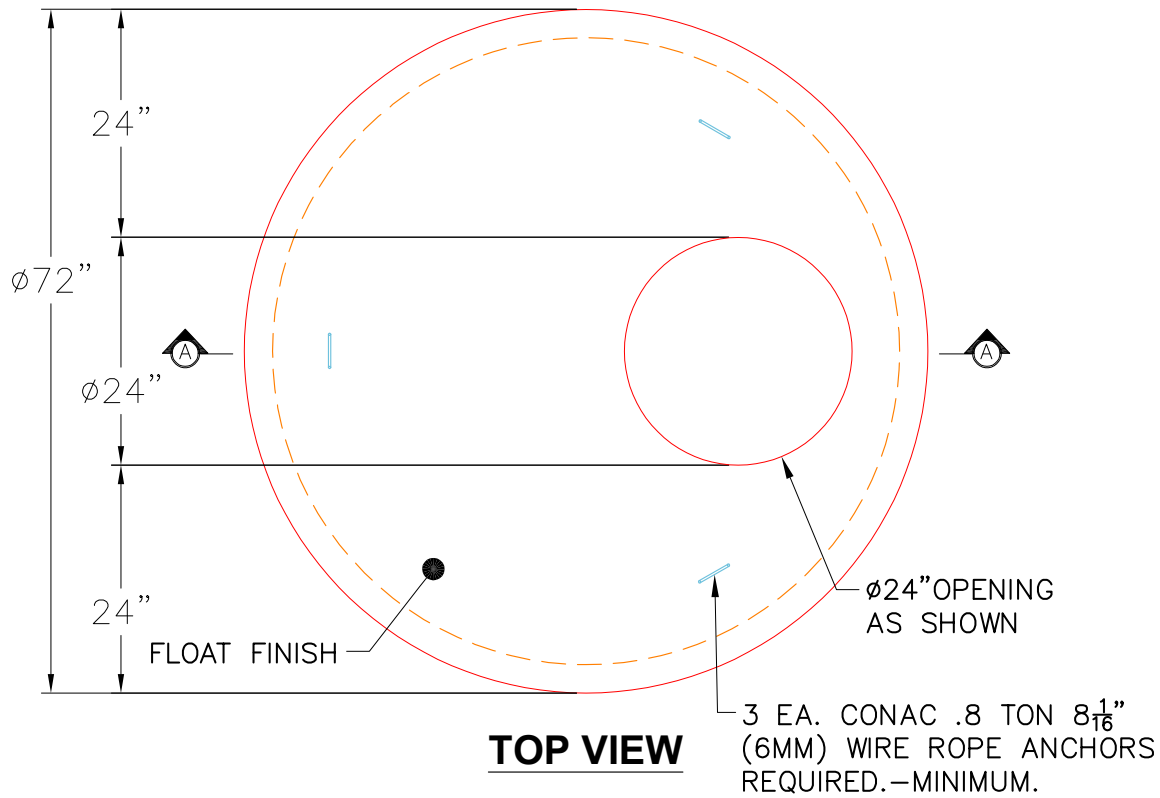

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2869 lb
Volume (Net): 0.73cu.yd
