

Job Name: 25-3326 Chappell's Dairy Road Sewer Extension
 Job Location: Somerset, KY
 Contractor: City of Somerset Wastewater

Plant: 100
 9/25/2025 4:27:51 PM

Tech: J. Horsley
 PC: J. Jarvis



Structure ID: MH-1

P2 MH048CN30

ECC CONE w/ 24" HOLE F/G



- P3) 24" - CASTING HEIGHT - 7"
- P2) 48" - ECC CONE w/ 24" HOLE F/G - 30"
- P1) 48" - MH BASE T/n - 30"
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) CASTING - HOE MC-350 F/C Sanitary
- 1) 48" - Conseal CS-102 1.00" (Double)
- 3) PSX - 12-08 NYLO
- 5) MH Step ML-10-TDS-NCR - 10"

0 lb
 2050 lb
 3282 lb
 0 lb
 1440 lb
 0 lb
 305 lb
 0 lb
 24 lb
 0 lb

 Structure Total: 7101 lb

Structure Notes:
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 4. CASTING BY ICAST (HOE MC-350 "SANITARY" F/C)

 REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

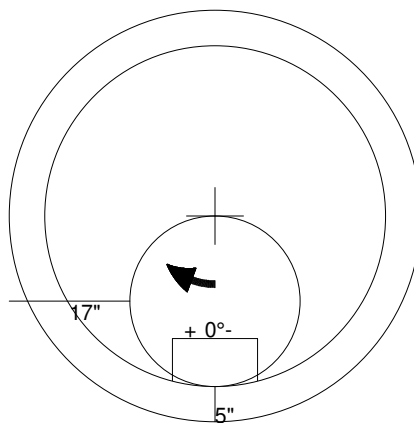

48" - ECC CONE w/ 24" HOLE F/G - 30" - (P2)

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 30"

Weight (Net): 2050 lb
 Volume (Net): 0.41cu.yd
