

Job Name: 25-3422 - 861485 Kroger L-756
 Job Location: Owensboro, KY
 Contractor: Contech Engineering Solutions

Plant: Beaver Dam
 10/15/2025 6:06:30 PM

Tech: J. Coppage
 PC: T. Sekula



Structure ID: 10-CS-8

P4 MH096LD17SP

MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G

- P5) 24" - CASTING HEIGHT - 4"
- P4) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17"
- P3) 96" - MH RISER T/G - 36"
- P2) 96" - MH RISER T/G - 96"
- P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 12"
- 1) CVSTENCILING
- 1) PSASSEMBLY
- 3) 96" - Conseal CS-102 1.00"
- 2) Hole - 48



0 lb
 10005 lb
 8599 lb
 21443 lb
 14124 lb
 0 lb
 0 lb
 0 lb
 0 lb

 Structure Total: 54171 lb

Structure Notes:
 (4" TALL CASTING PROVIDED BY OTHERS)

 ICAST TO INSTALL THE INTERNALS

 CONTECH'S LOGO AS WELL AS THE
 INLET AND OUTLET MUST BE
 STENCILED ONTO THE STRUCTURE

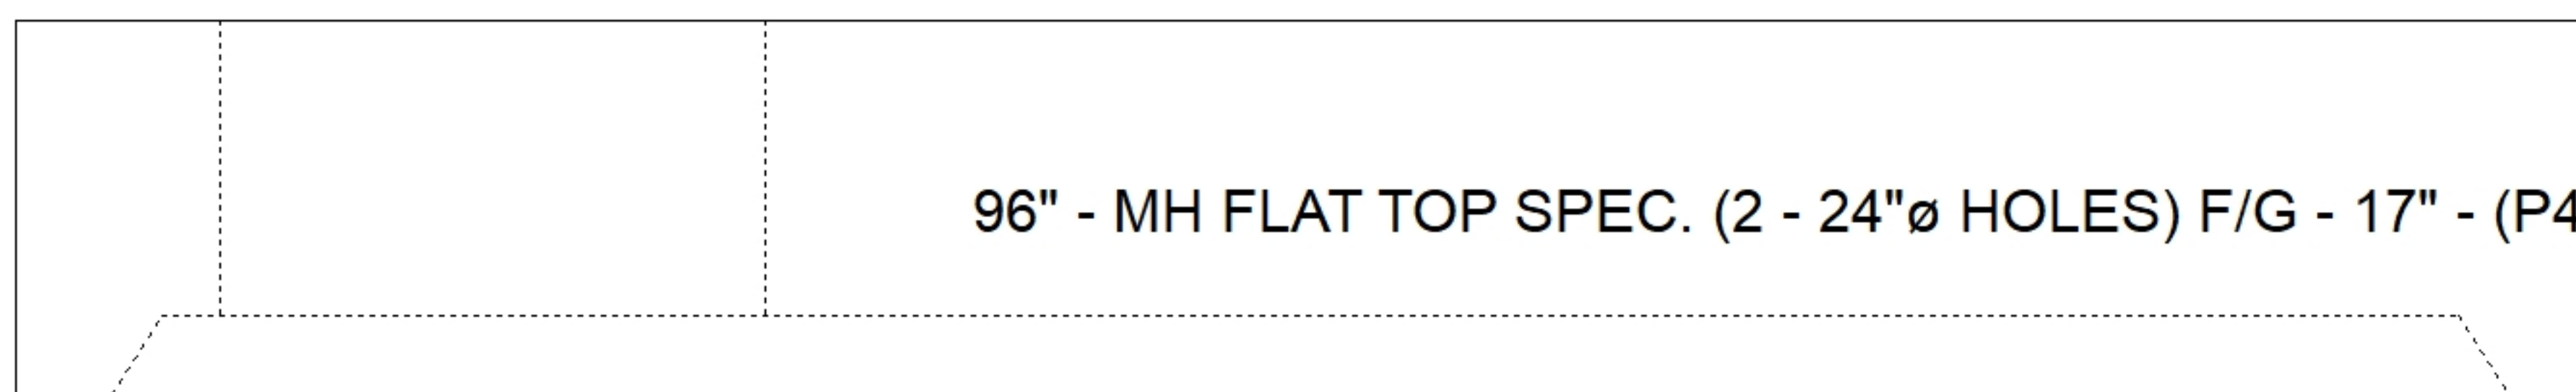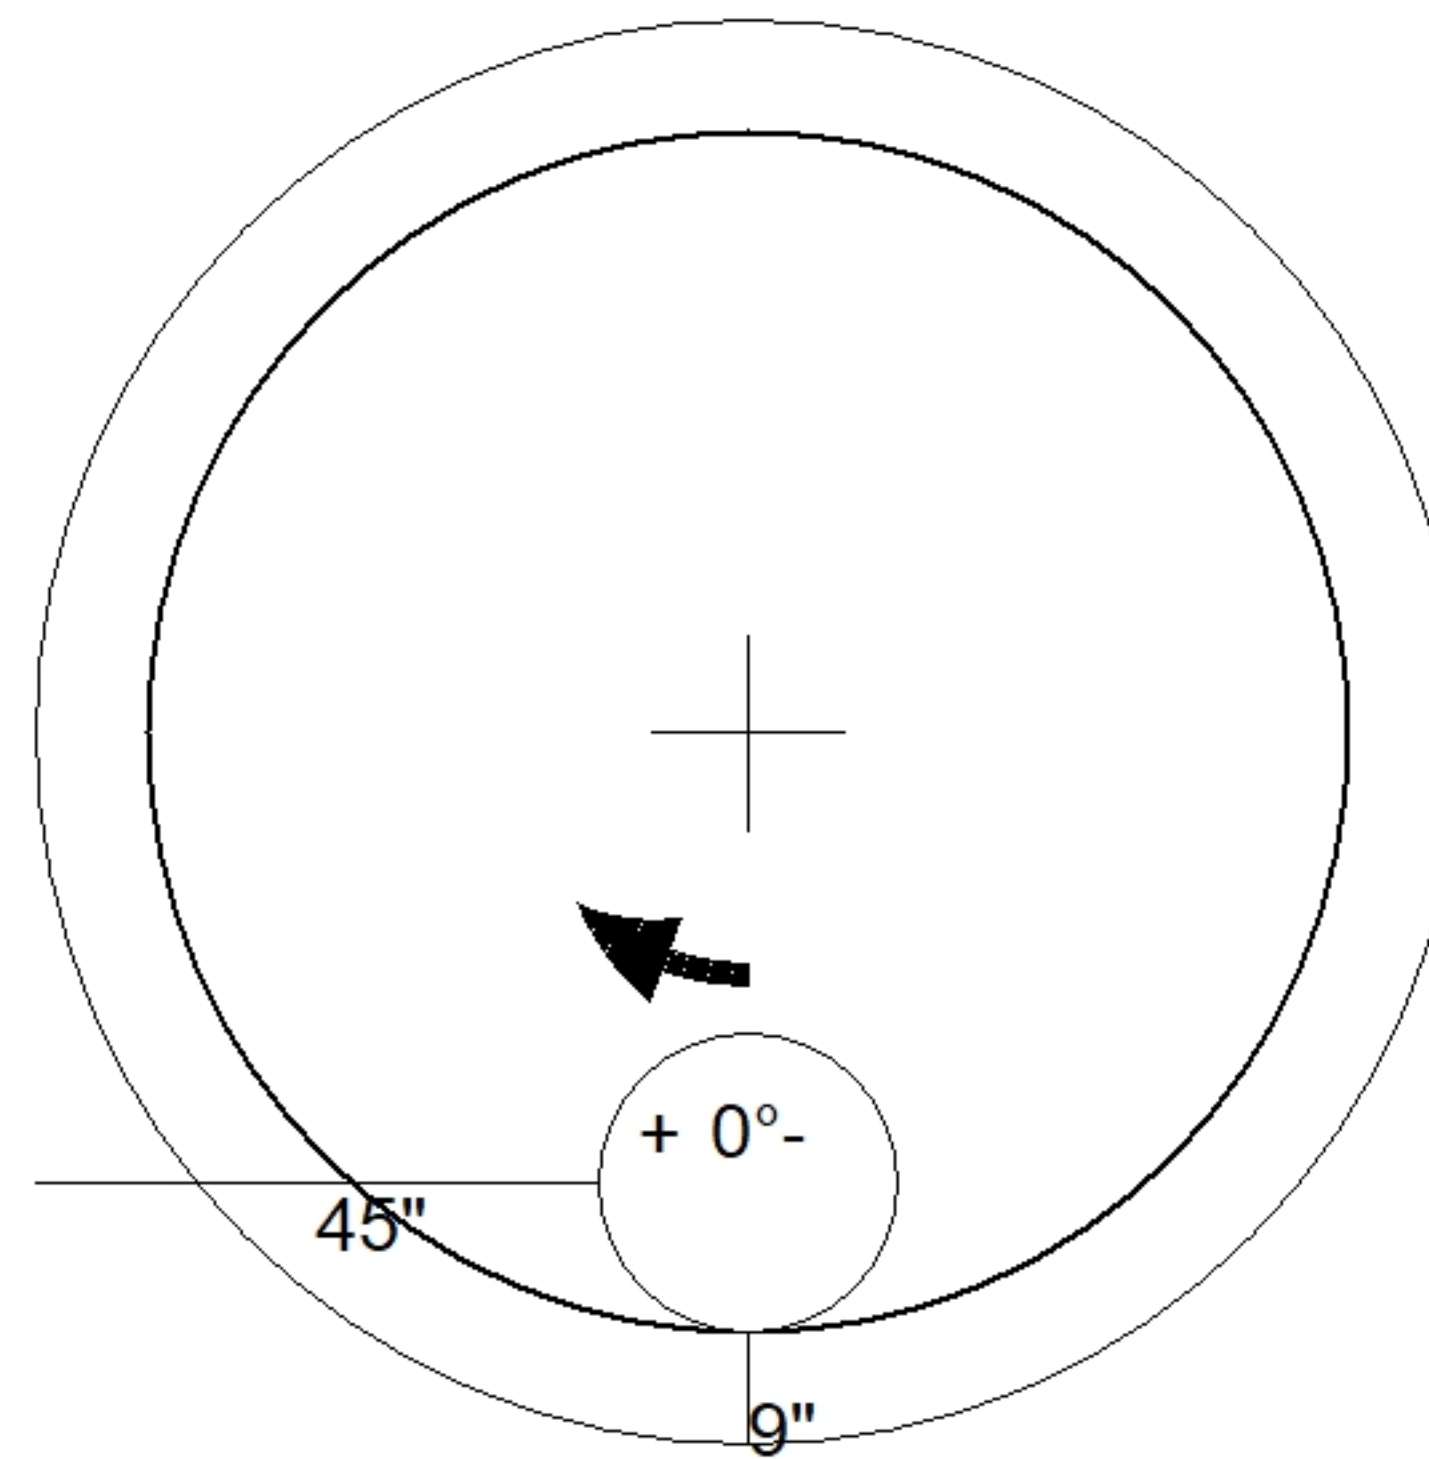

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: Groove

Wall Thickness: 9"

Height (Ext): 17"

Weight (Net): 10005 lb
 Volume (Net): 2.56cu.yd
