

Contractor: Louisville Paving and Construction

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 6.73'

Floor Height: 6"


Slack: 0.76"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

7) MH Step ML-10-TDS-NCR - 10"


0 lb

Structure Total: 6393 lb

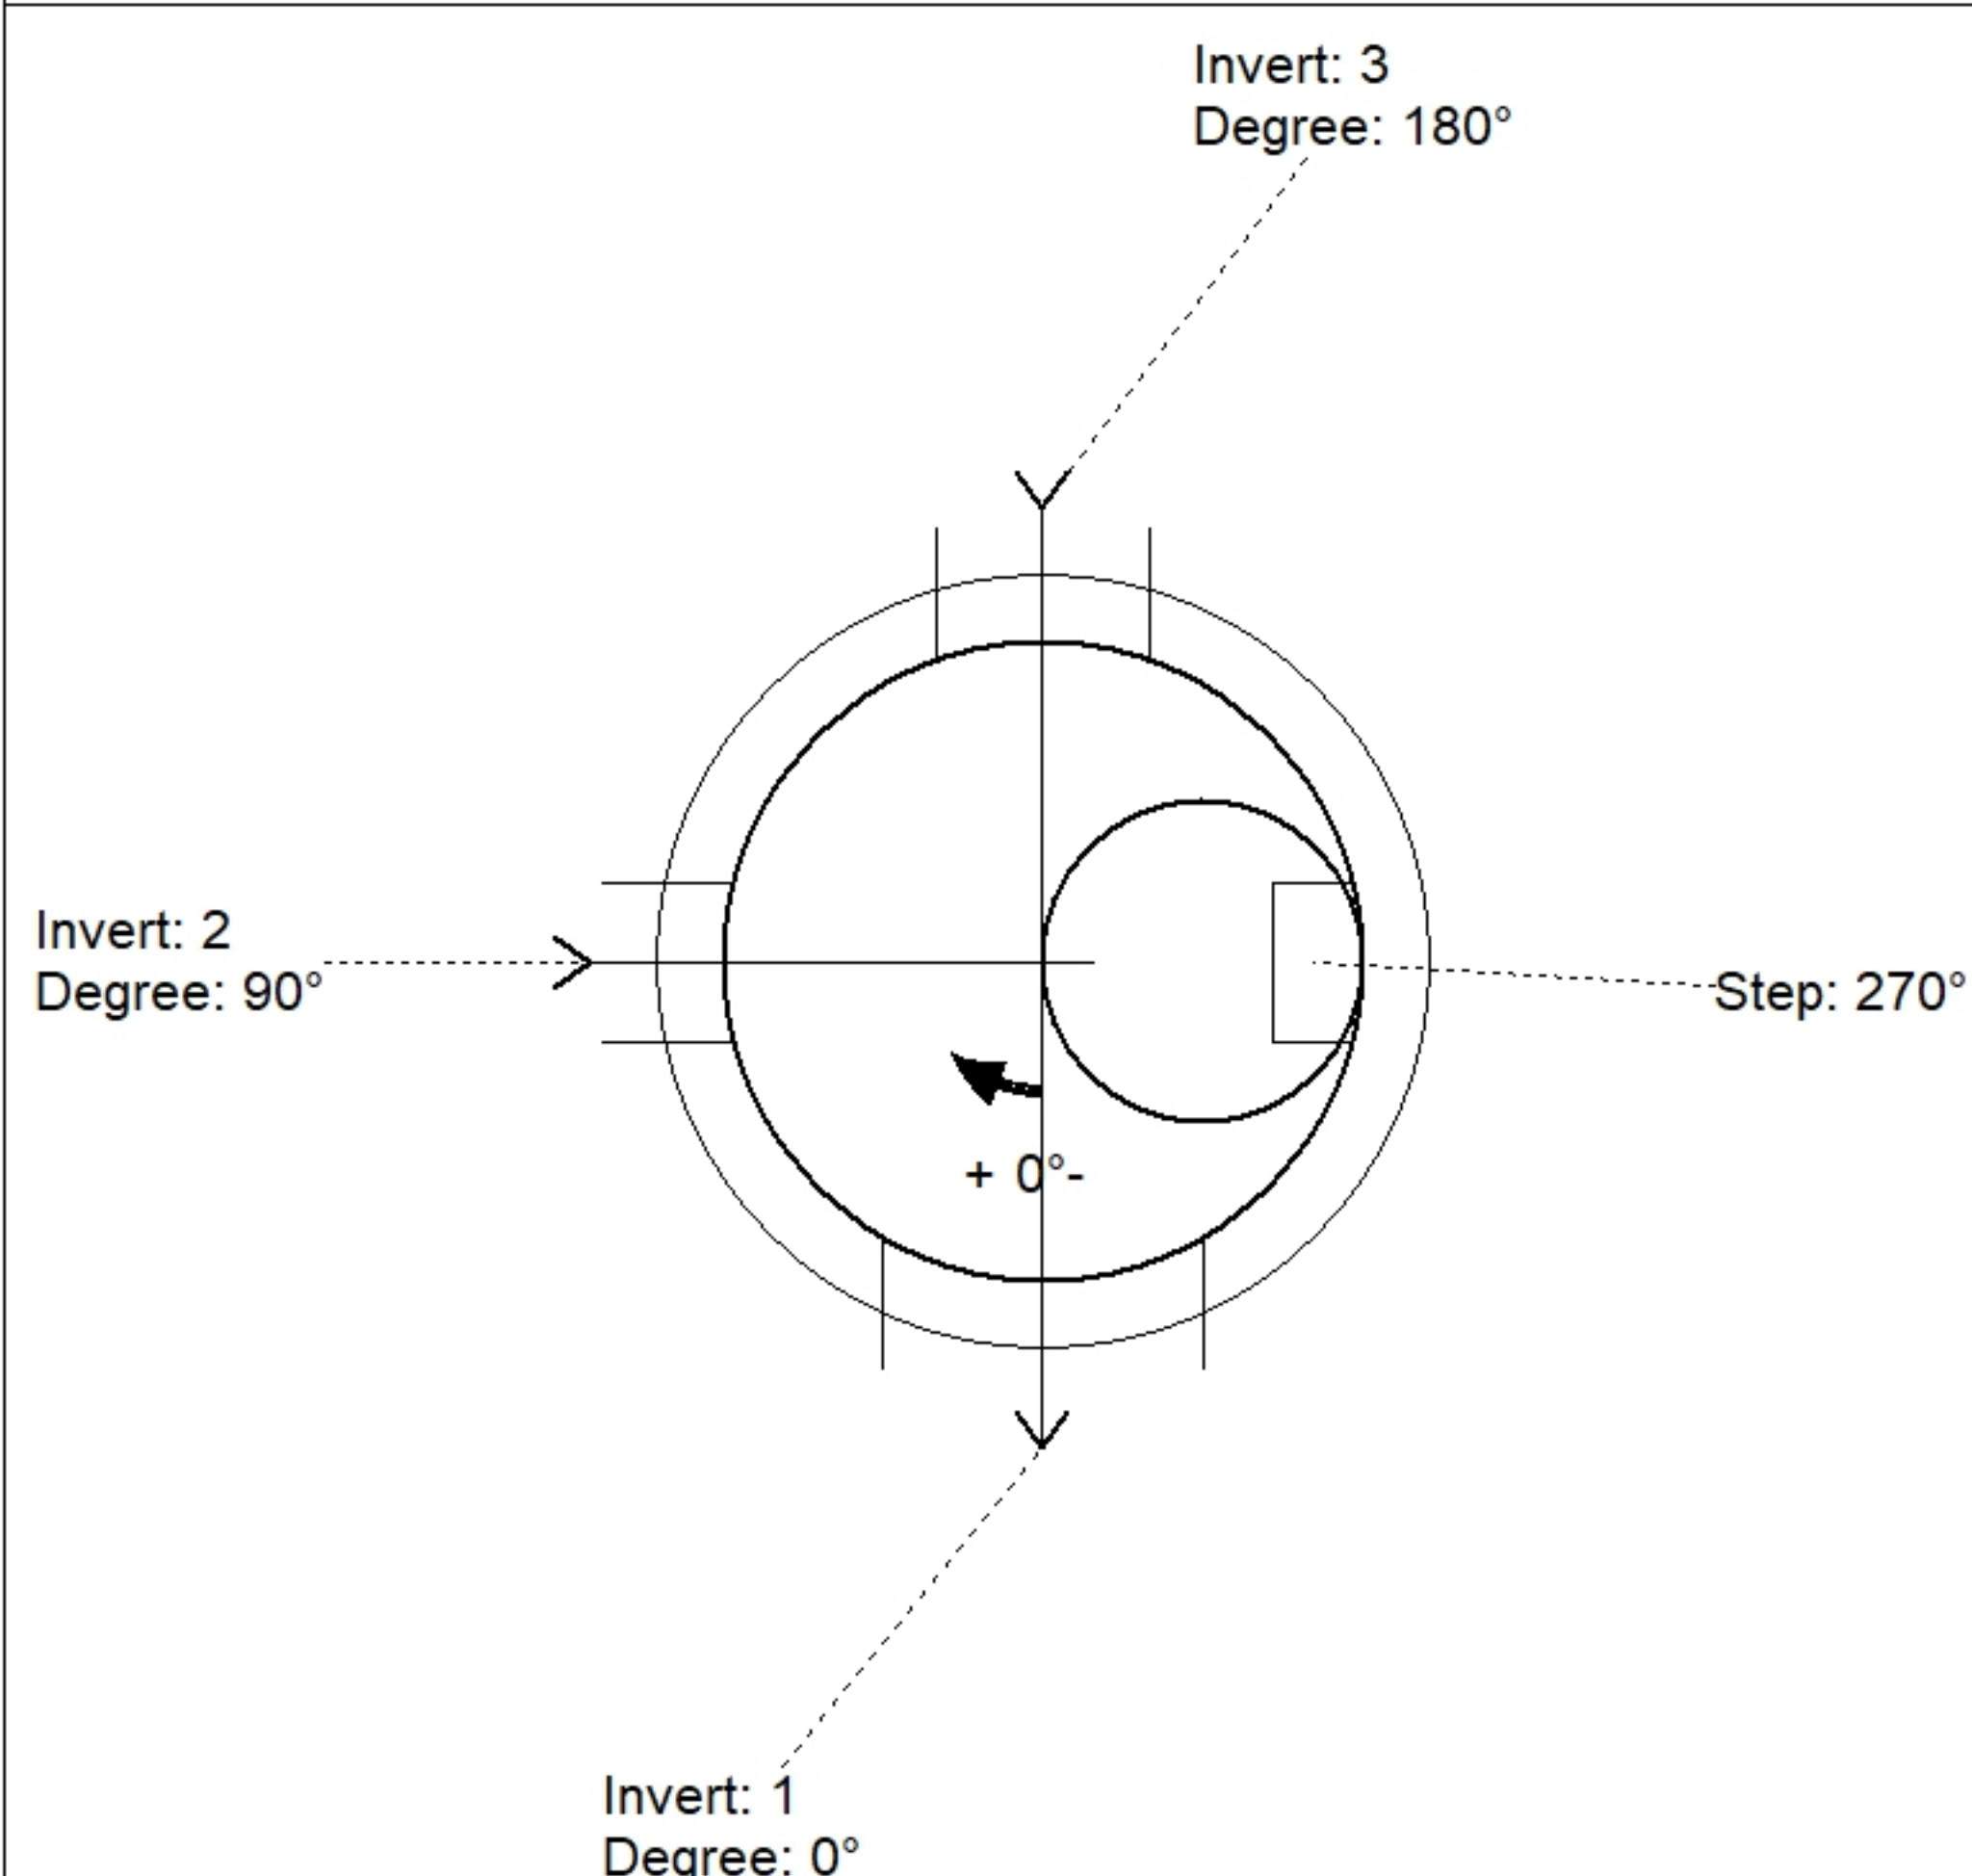

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	454.85'							
Reducer								
Invert 1	448.12'	0°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	448.54'	90°	8" HDPE	9.1"	12"	Hole 12	4.49"	P1
Invert 3	449.98'	180°	12" HDPE	14.5"	16"	Hole 16	21.07"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

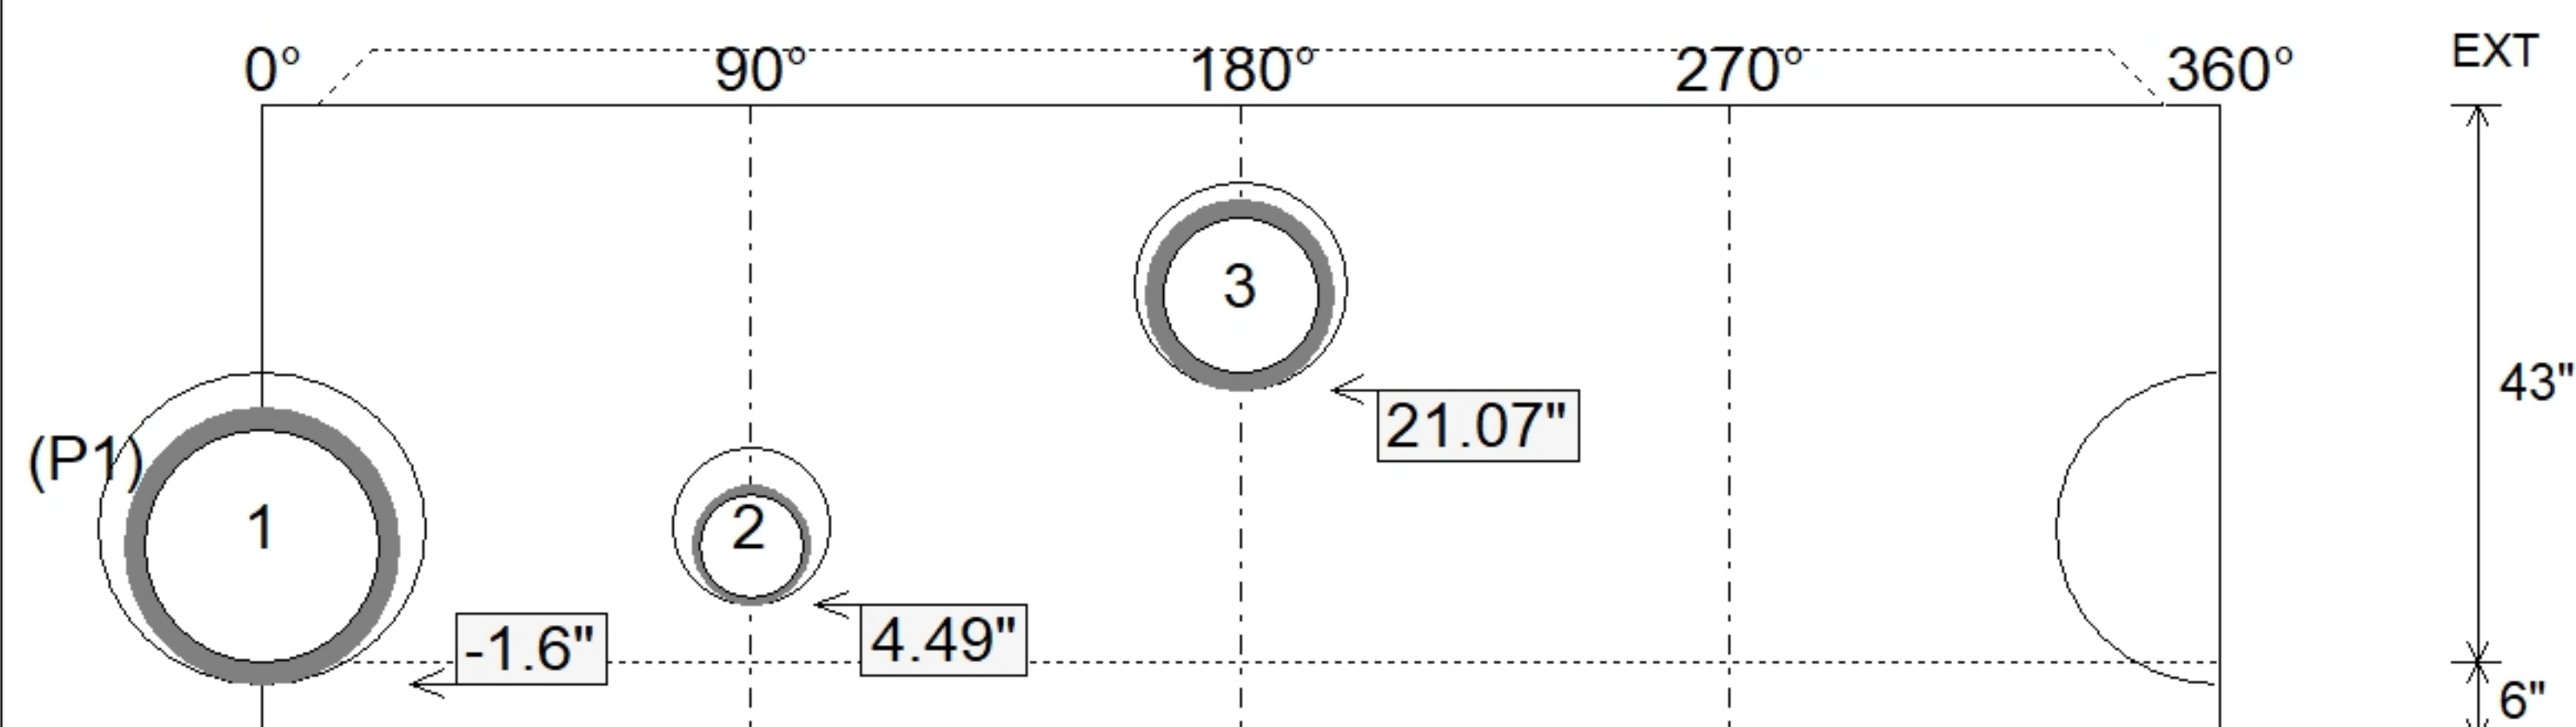

Submittal Drawing
5/6/2026 8:50:33 AM

SUBMITTAL
APPROVED BY:
