

Contractor: Louisville Paving and Construction

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 5.17'

Floor Height: 6"


Slack: 0.04"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


5) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 5030 lb

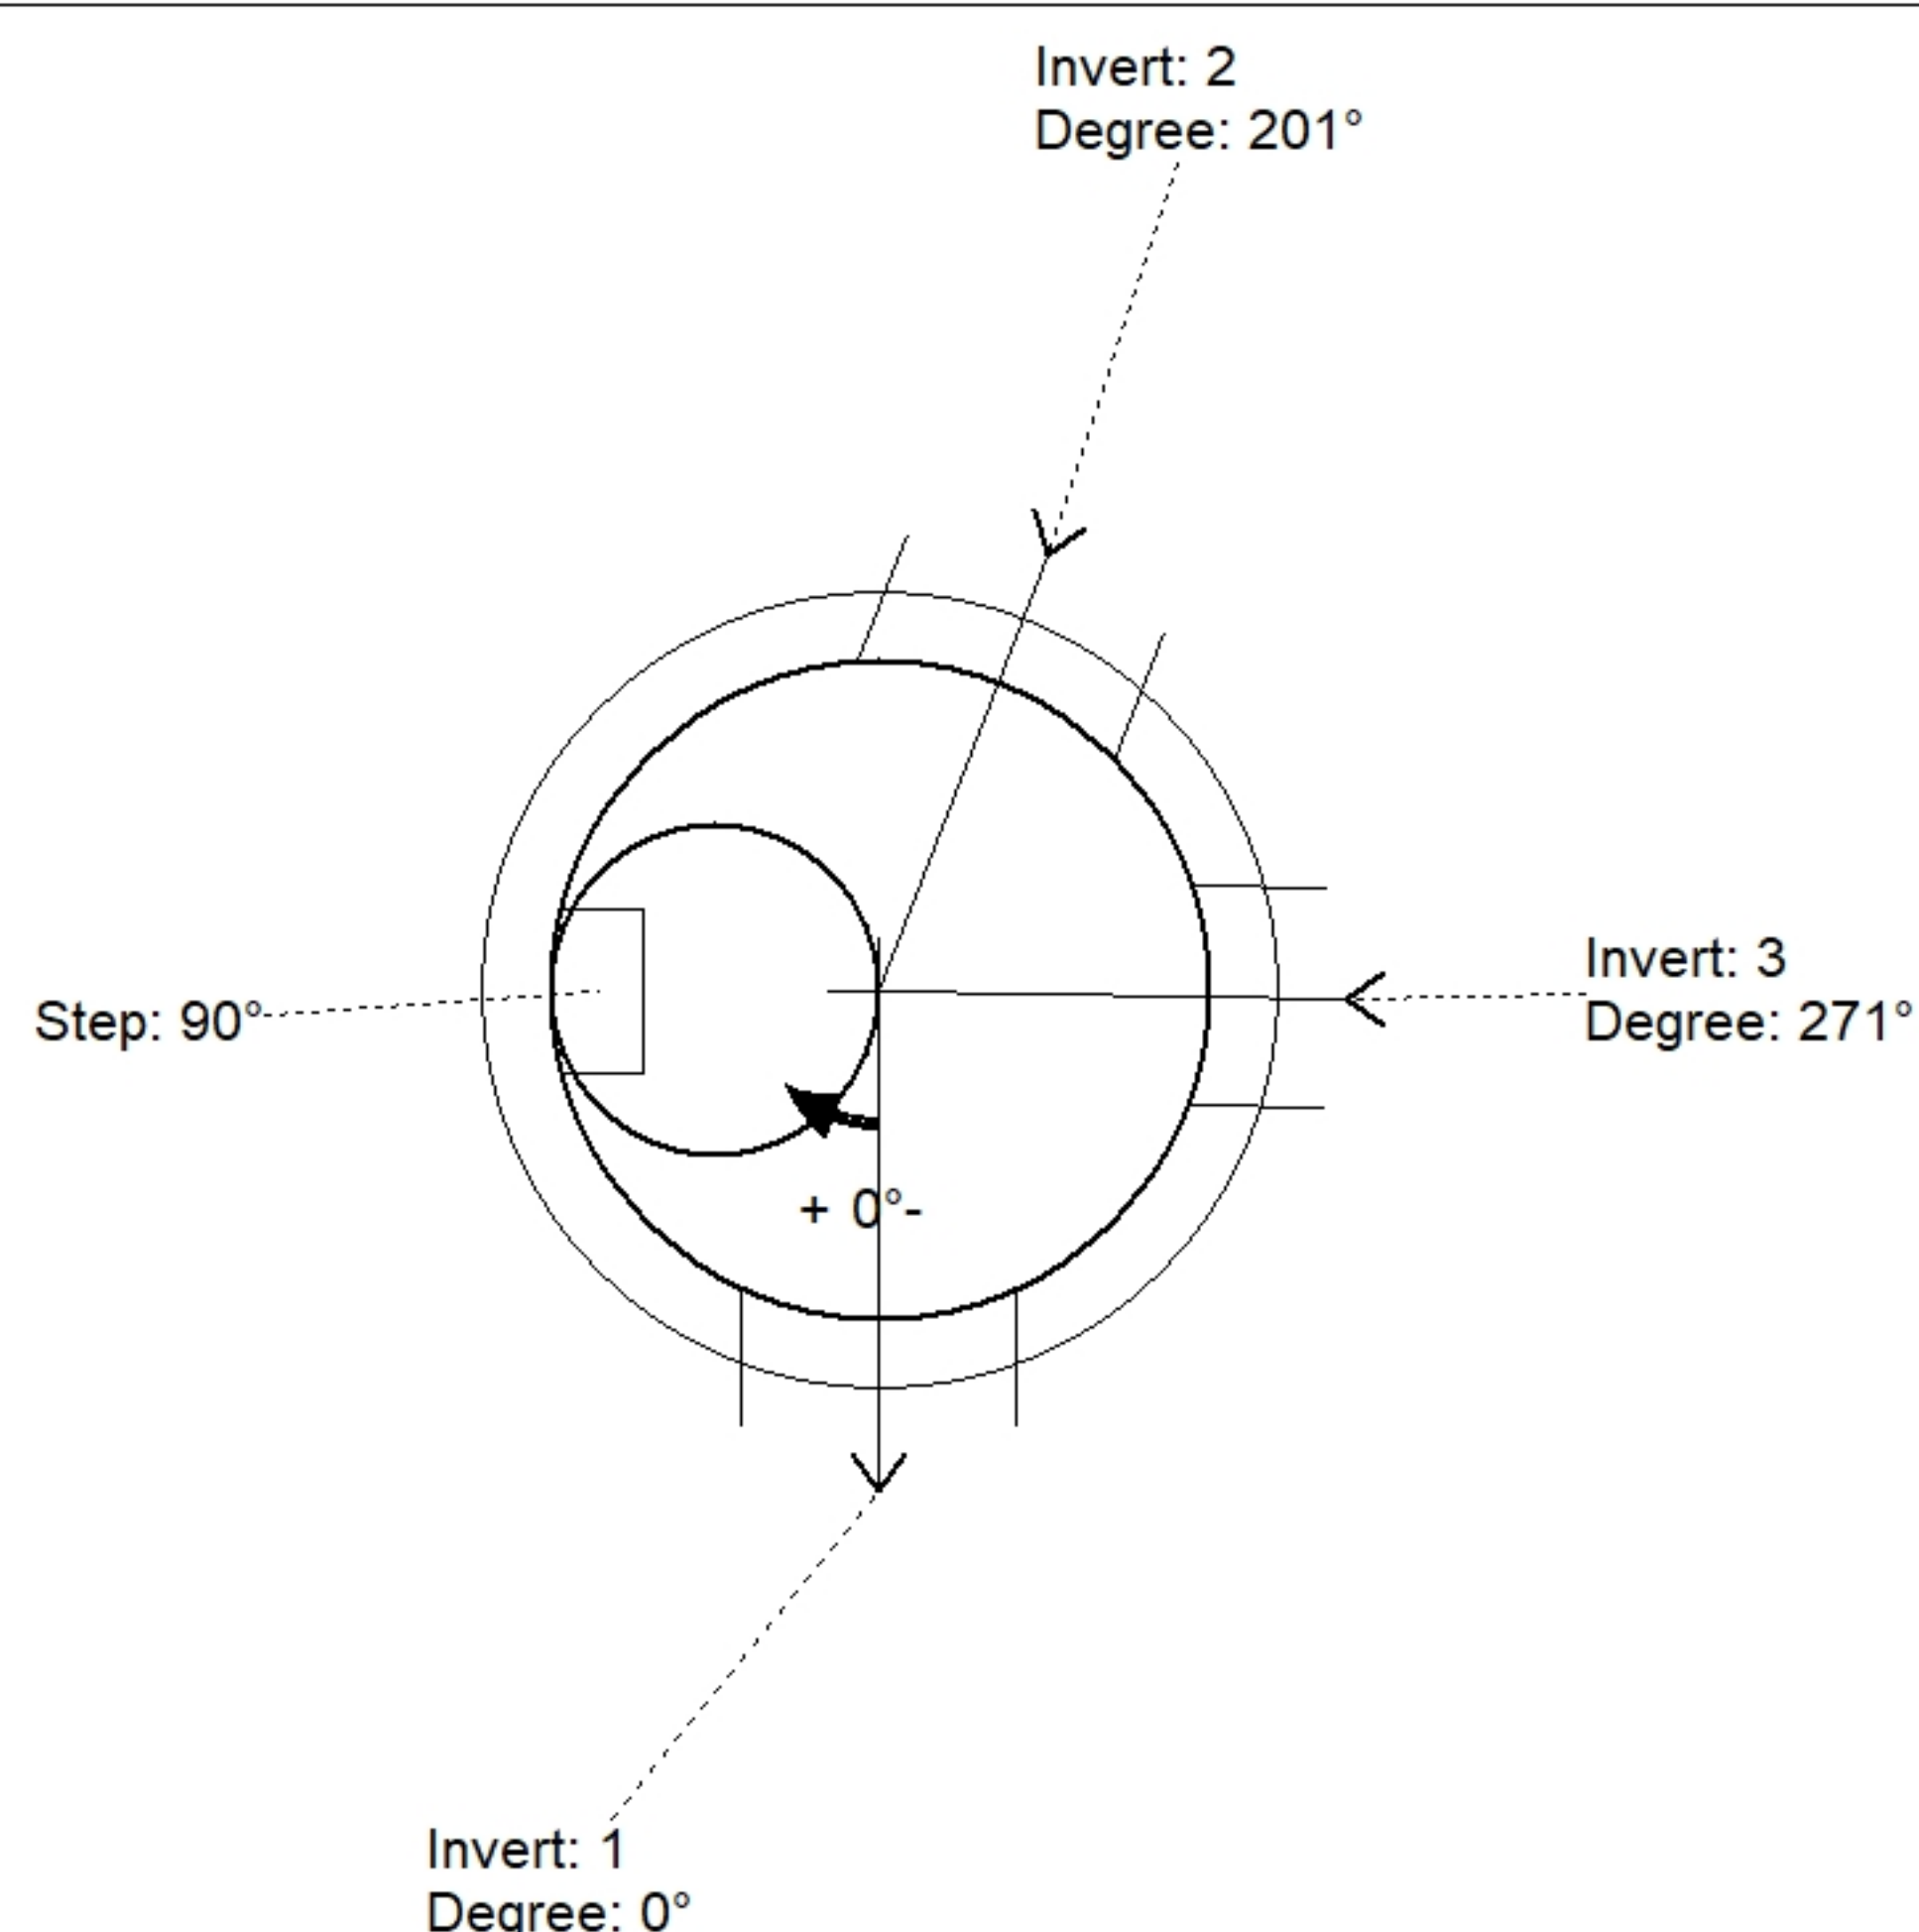

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	454.86'							
Reducer								
Invert 1	449.69'	0°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	449.69'	201°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 3	449.69'	271°	12" HDPE	14.5"	16"	Hole 16	-1.25"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

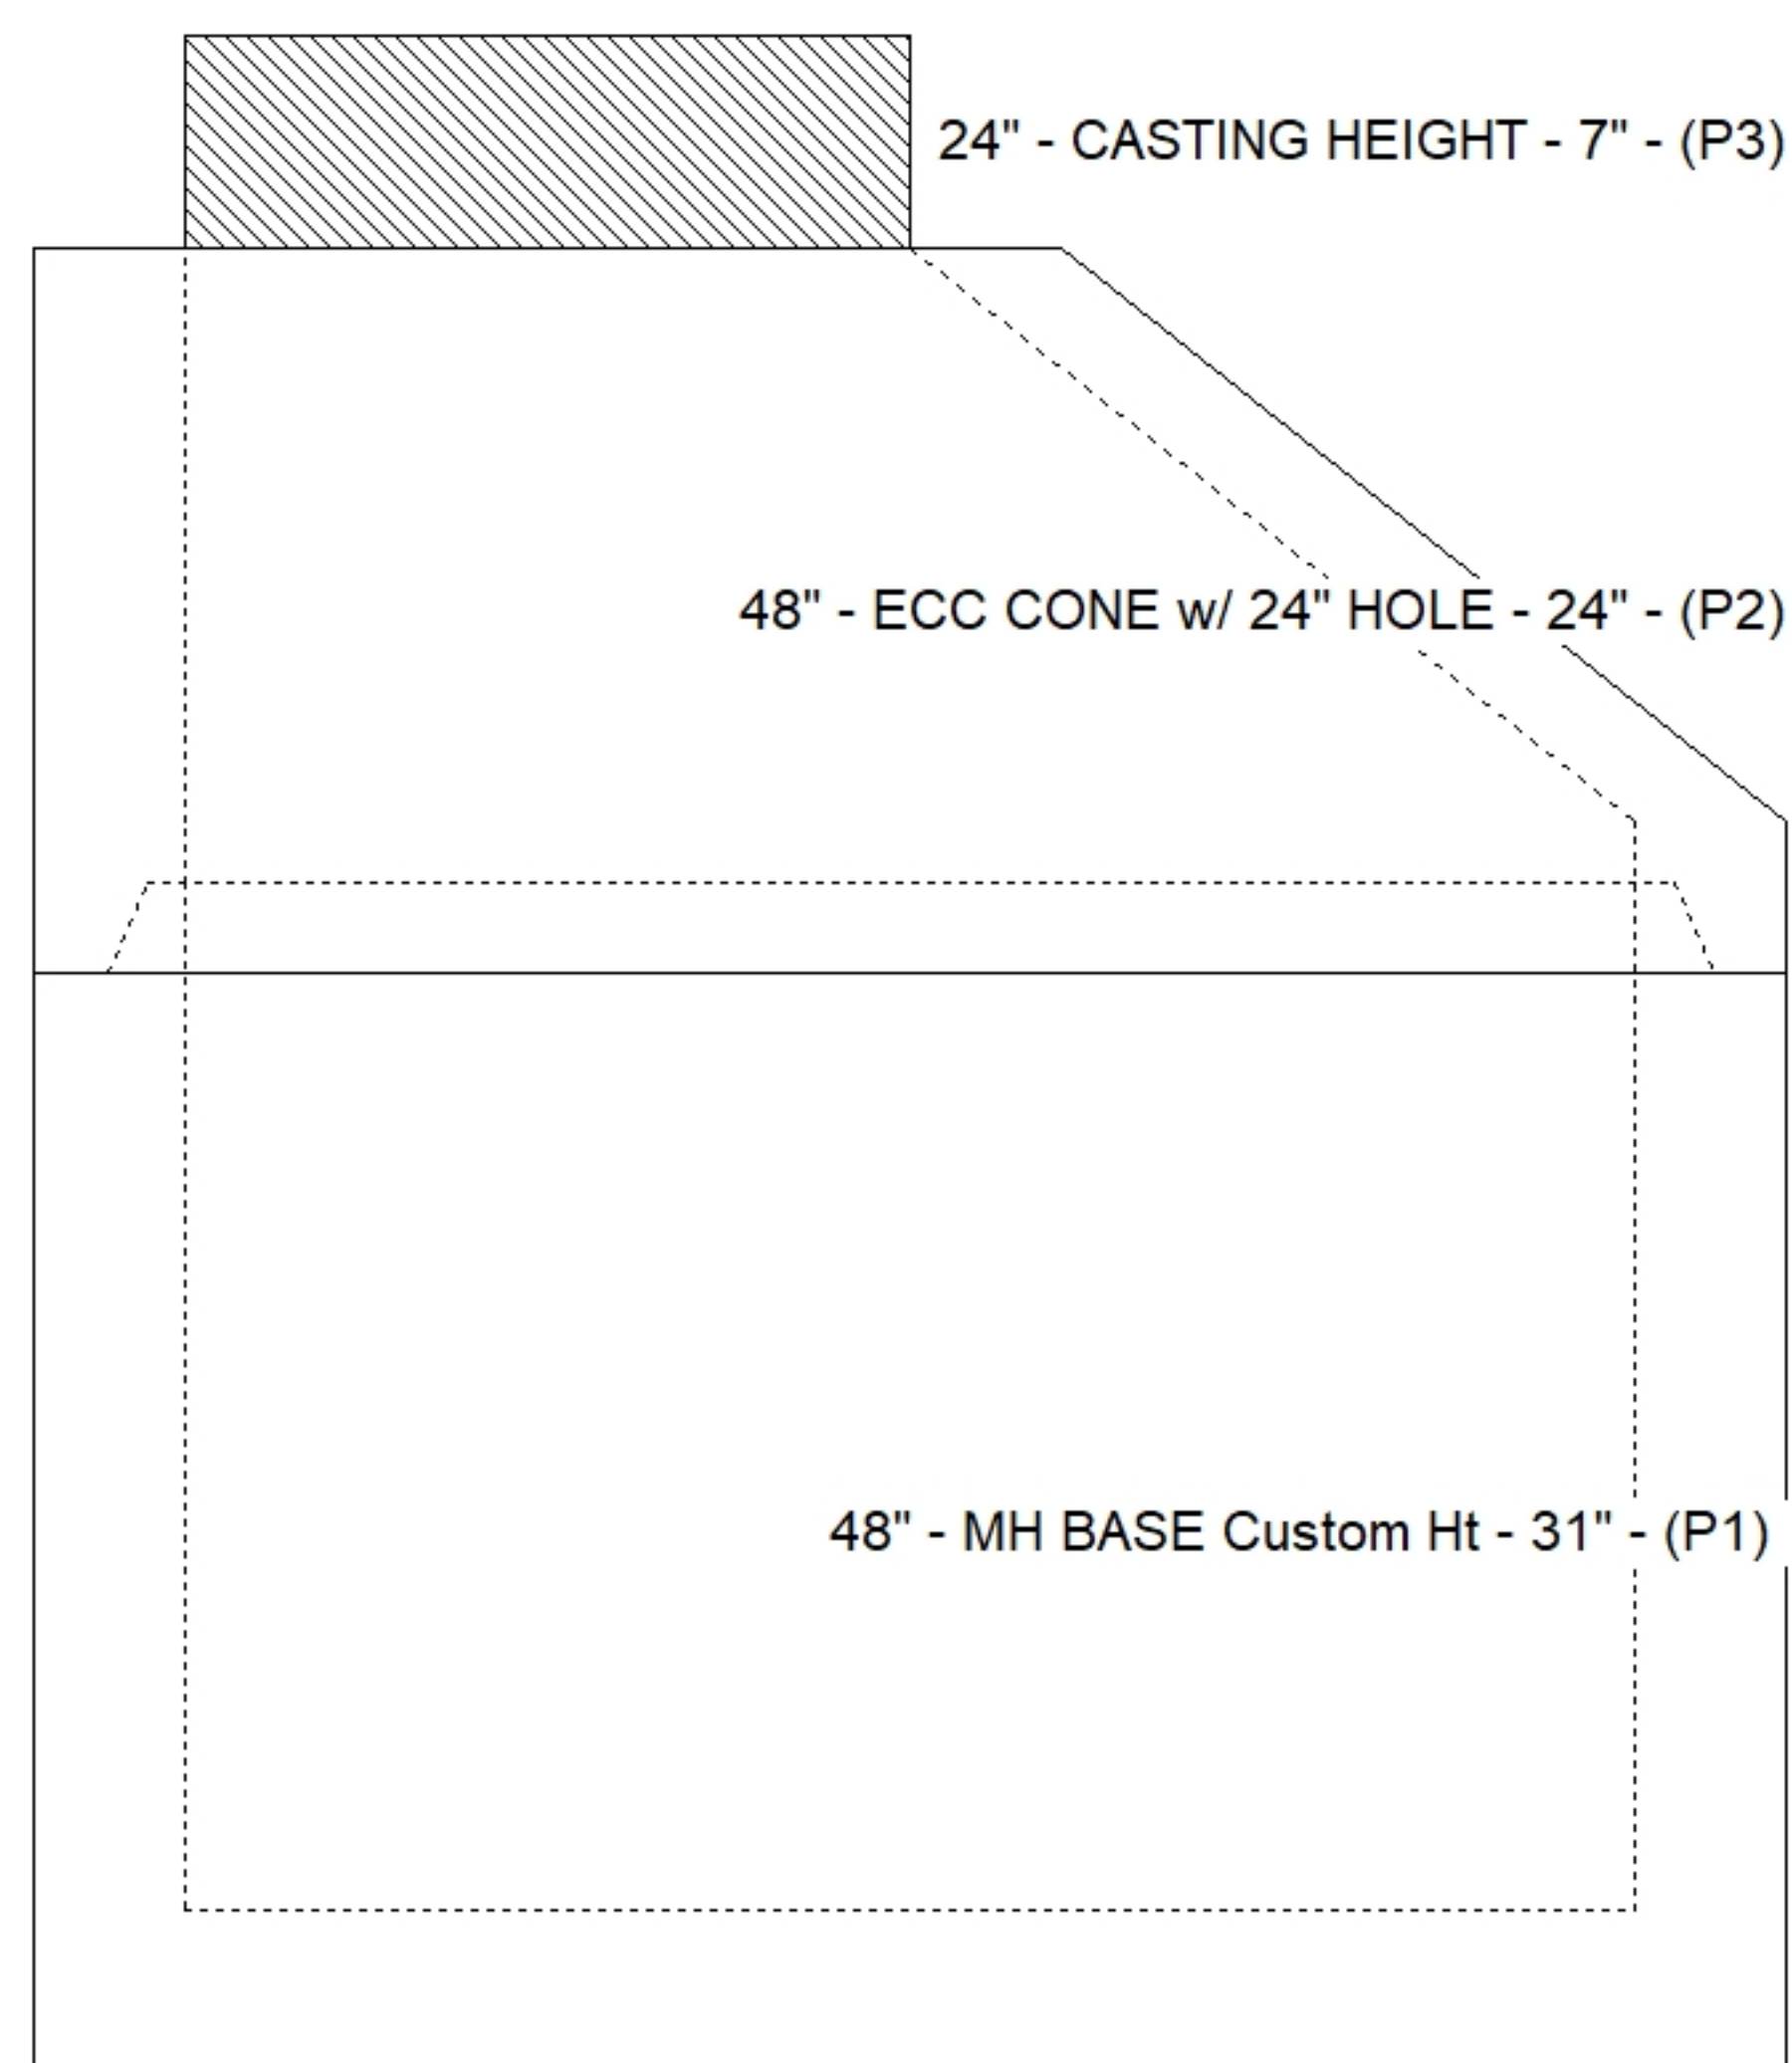

Default - Interior Dimensions

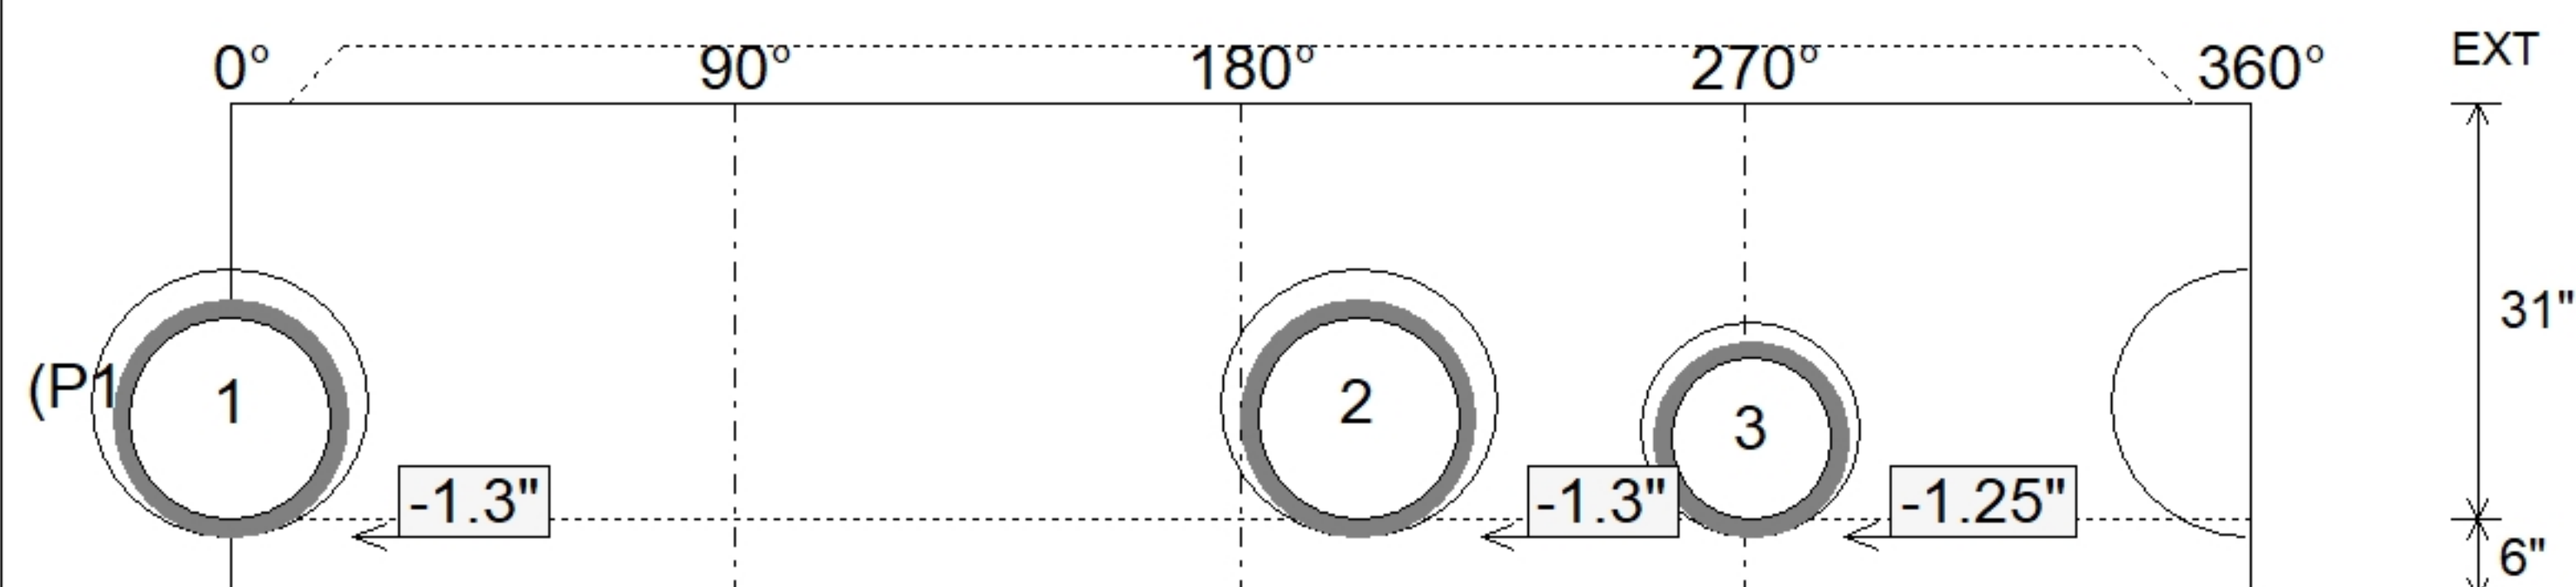

Submittal Drawing
5/6/2026 8:50:39 AM

SUBMITTAL
APPROVED BY:
