

Job Name: 25-3555 - Gates Ford New Truck Service Shop
Job Location: Richmond, KY 40475
Contractor: Lagco Inc.

PC: T. Lewis
 TECH: Jared - F
 Plant: 100



Structure ID: **CB 4-2**
 Spec: Storm
 Type: BX 8inW, 8inF
 Size: 24" x 36"

Rim: 893.84'
 Invert: 889.78'
 Rim to Invert: 4.06'

Sump: 0"
 Floor (Top): 889.78'
 Floor Height: 8"

Floor (Bot): 889.113'
 Overall Height: 4.667'
 Slack: 0.72"

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. NO STORM INVERT
5. NO STEPS
6. HOE-525-LV FRAME, L-VANE GRATE, & CURB HOOD SUPPLIED BY ICAST



STRUCTURE SUMMARY:

- P2) 24" x 36" - CASTING HEIGHT - 6"
 P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 42"
 1) CASTING - HOE 525 LV SET (F/G/H)
 1) 24" x 36" - Conseal CS-102 1.00"
 2) Hole - 20


0 lb
 5260 lb
 442 lb
 0 lb
 0 lb

Structure Total: 5702 lb

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	893.84'							
Reducer								
Invert 1	889.78'	90°	15" HDPE	17.6"	20"	Hole 20	-1.25"	P1
Invert 2	889.78'	0°	15" HDPE	17.6"	20"	Hole 20	-1.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

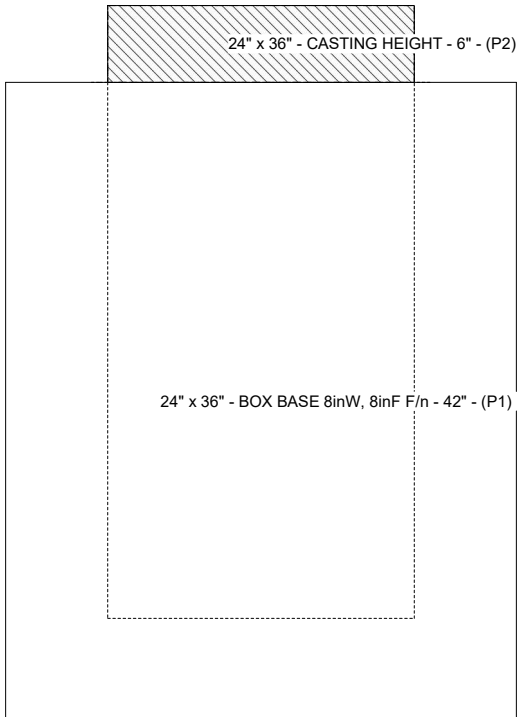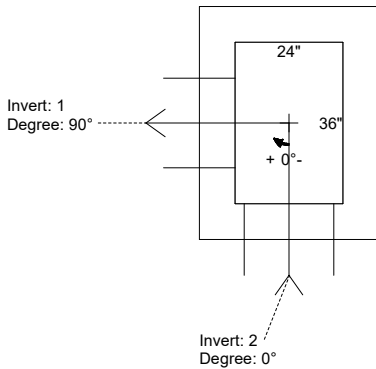

Cast (Int. Dim.) - Interior Dimensions

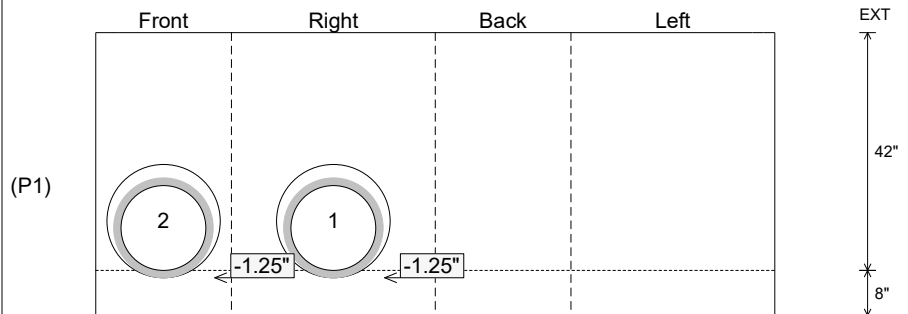

Submittal Drawing
 4/24/2026 9:58:24 AM

SUBMITTAL
 APPROVED BY:
