
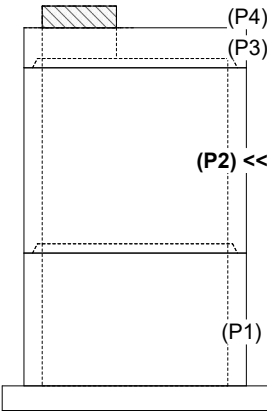



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting					Plant: 100 6/7/2026 1:25:24 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: MH A13											
P2		MH060RS60S		MH RISER w/COATING T/G							
P4) 24" - CASTING HEIGHT - 7" P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P2) 60" - MH RISER w/COATING T/G - 60" P1) 60" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 43" 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 060" MAC WRAP 1) SPECIAL EXTERNAL COATING - Carboline 300M 1) SECONDARY POUR - Extended Flange 2) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1040 8) MH Step ML-10-TDS-NCR - 10" 225.5 SqFt) Carboline Bitumastic 300M [EXT]					0 lb 2869 lb 6264 lb 7456 lb 2692 lb 0 lb 0 lb 0 lb 0 lb 0 lb 2 lb 0 lb 0 lb ----- 19282 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. STEPS AT 245 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS				
Rim: 899.98' Rim to Invert: 10.095' Slack: 0.355" Sump: 2.215" Step Position: 245°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

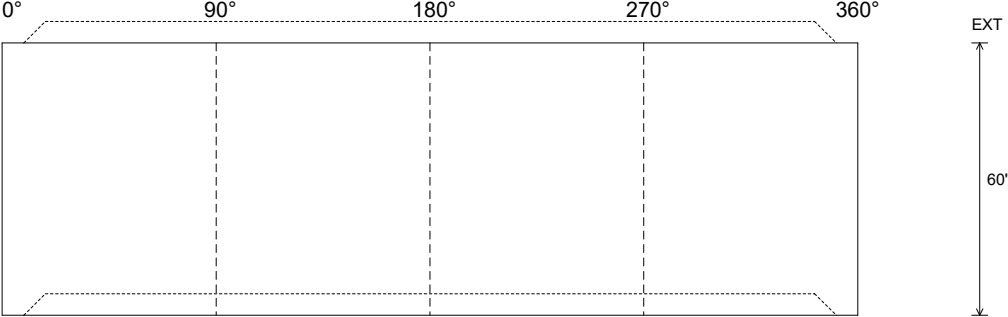

RIGHT-SIDE UP VIEW (int. dimensions)


INSIDE WALL DIMENSIONS


Coating (Int): Coating (Ext): Carboline Bitumastic 300M	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 6264 lb Volume (Net): 1.6cu.yd
--	------------------------------------	--	--	---

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A13

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
