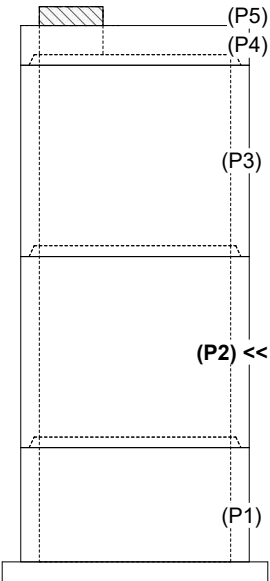
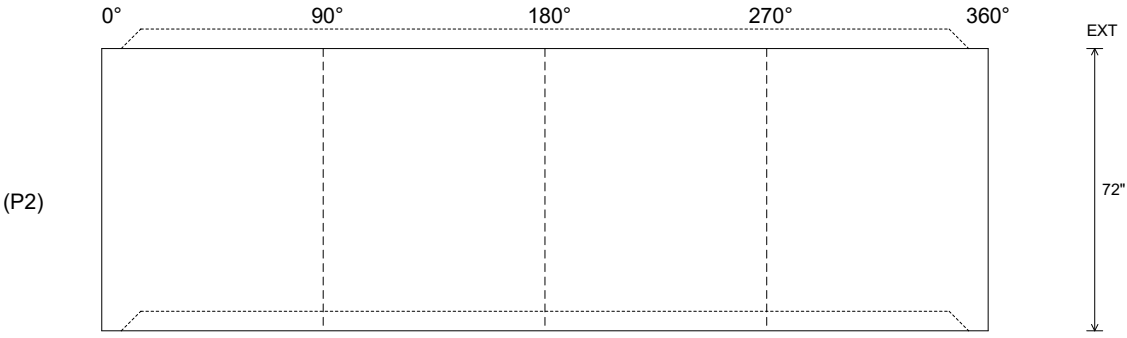


Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting					Plant: 100 6/7/2026 1:25:19 PM		Tech: J. Horsley PC: C. Goff					
Structure ID: MH A9												
P2		MH072RS72S										
P5) 24" - CASTING HEIGHT - 7" P4) 72" - MH FLAT TOP SPECIAL F/G - 15" P3) 72" - MH RISER SPECIAL w/COATING T/G - 72" P2) 72" - MH RISER w/COATING T/G - 72" P1) 72" - MH BASE w/FLANGE (08F/07EF) w/Coating T/n - 43" 1) SPECIAL EXTERNAL COATING - Carboline 300M 1) 72" - MH INVERT CHANNEL - FULL HEIGHT 3) JOINT WRAP - 12" WD x 072" MAC WRAP 1) SECONDARY POUR - Extended Flange 3) 72" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 1040 2) Kor-N-Seal2 - S206-28 15) MH Step ML-10-TDS-NCR - 10" 436.79 SqFt) Carboline Bitumastic 300M [EXT]					0 lb 5254 lb 10126 lb 10496 lb 10101 lb 5422 lb 0 lb 0 lb 0 lb 0 lb 2 lb 13 lb 0 lb 0 lb ----- 0 lb		<u>Structure Notes:</u> 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CARBOLINE 300M EXTERIOR COATING REQUIRED 5. STEPS AT 90 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY OTHERS					
Rim: 906'					Rim to Invert: 17.315'		Slack: 0.995"		Sump: 2.215"		Step Position: 90°	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)												
												
INSIDE WALL DIMENSIONS												
												
Coating (Int): Coating (Ext): Carboline Bitumastic 300M			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 7" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 10496 lb Volume (Net): 2.68cu.yd			

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer
Ph 2

Structure:

MH A9

Note:

This Structure Is To Receive An
External Coating of Carboline 300M
(Supplied By iCast)
