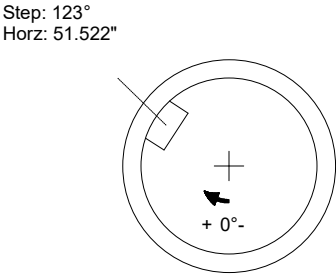



Job Name: 25-3579 - Lebanon Rd Clarks Run Trunk Sewer Ph 2 Job Location: Danville, KY Contractor: Hubert Excavating & Contracting					Plant: 100 8/21/2026 1:12:56 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: MH H1											
P2		MH048RS36S		MH RISER w/COATING T/G							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/Coating F/G - 36" P2) 48" - MH RISER w/COATING T/G - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/Coating T/n - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) SPECIAL EXTERNAL COATING 2) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 8) MH Step ML-10-TDS-NCR - 10" 134.51 SqFt) Carboline Bitumastic 300M [EXT]					0 lb 2251 lb 2515 lb 4765 lb 1440 lb 0 lb 0 lb 0 lb 12 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE WT-375 SAN. F/C). 4. ALL PIECES TO HAVE EXTERIOR COATING (CARBOLINE BITUMASTIC 300M). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total:					10983 lb						
Rim: 910.47' Rim to Invert: 9.01' Slack: 1.12" Sump: 2" Step Position: 123°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext): Carboline Bitumastic 300M			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd		

Job Number:

25-3579

Job Name:

Lebanon Rd Clarks Run Trunk Sewer Ph 2

Structure:

MH H1

Note:

This structure is to receive an external coating of carbolite 300M (supplied by ICAST)
