

Job Name: 25-3664-Hallmark Communities
Job Location: Nicholasville, KY
Contractor: The Allen Company, Inc.

Plant: 100
9/9/2026 2:28:06 PM

Tech: Jared - A
PC: Erica Bradley



Structure ID: CI10

P2 BX242408-VF

BOX RISER 8inW, Variable Ht

P3) 24" x 24" - CASTING HEIGHT - 5"
P2) 24" x 24" - BOX RISER 8inW, Variable Ht - 19"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 60"
1) CASTING - HOE KY-465 SET (CBI TY F)
2) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 24
1) Hole - 20

0 lb
1633 lb
5777 lb
465 lb
0 lb
0 lb
0 lb



Structure Total: 7875 lb

Structure Notes: .
1. HOE KY-465 SET (CBI TY F) PROVIDED BY OTHERS.
2. KYTC CBI TYPE F / ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. NO STEPS.
6. REINFORCING PER ASTM A615 (GRADE 60).
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Rim: 1013' Rim to Invert: 7' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

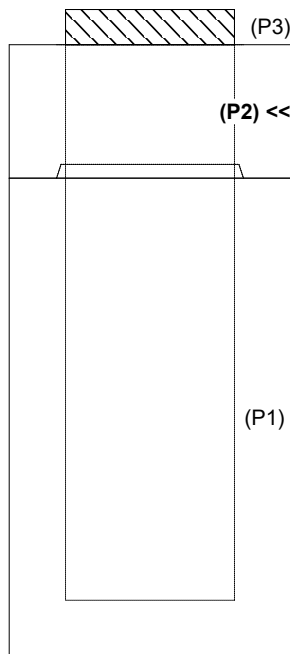

INSIDE WALL DIMENSIONS



Coating (Int):	Seam Up: Flat	Wall Thickness: 8"	Height (Int): 19"	Weight (Net): 1633 lb
Coating (Ext):	Seam Dn: Groove	Floor Height: 0"	Height (Ext): 19"	Volume (Net): 0.42cu.yd
