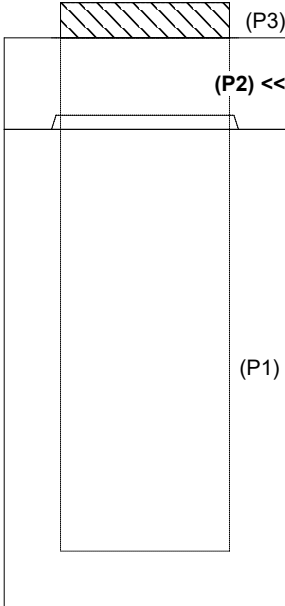




Job Name: 25-3664-Hallmark Communities Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: 100 9/9/2026 2:28:12 PM		Tech: Jared - A PC: Erica Bradley				
Structure ID: CI5											
P2		BX242408-VF		BOX RISER 8inW, Variable Ht							
P3) 24" x 24" - CASTING HEIGHT - 5" P2) 24" x 24" - BOX RISER 8inW, Variable Ht - 13" P1) 24" x 24" - BOX BASE 8inW, 8inF - 60" 1) CASTING - HOE KY-465 SET (CBI TY F) 2) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 12						0 lb 1117 lb 5920 lb 465 lb 0 lb 0 lb 0 lb ----- Structure Total: 7502 lb		Structure Notes: . 1. HOE KY-465 SET (CBI TY F) PROVIDED BY OTHERS. 2. KYTC CBI TYPE F / ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. NO STEPS. 6. REINFORCING PER ASTM A615 (GRADE 60). - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1020.64'		Rim to Invert: 6.5'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 13" Height (Ext): 13"		Weight (Net): 1117 lb Volume (Net): 0.28cu.yd	
