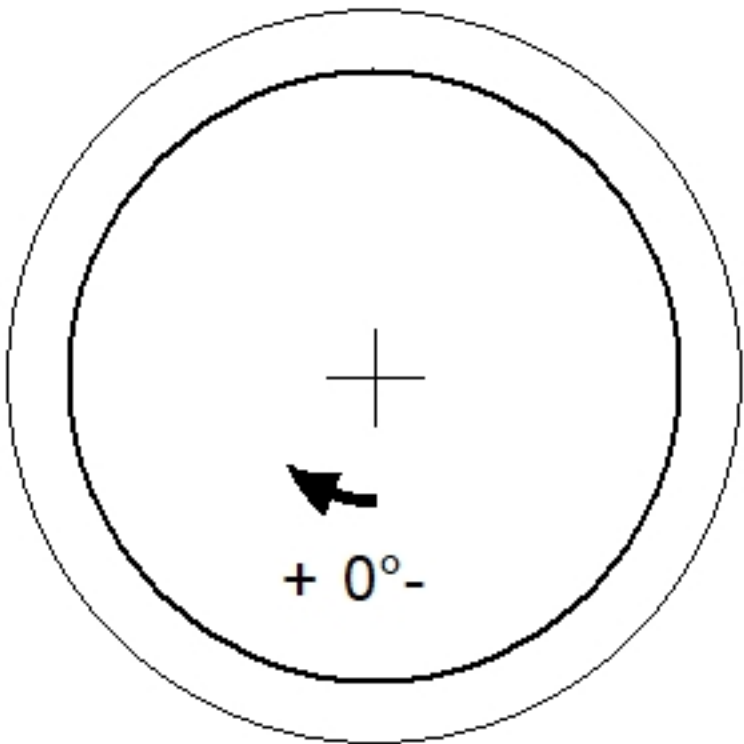


Job Name: 25-4212 - Greentree Lane Sewer Job Location: Mt. Washington, KY Contractor: Citgo Waterworks					Plant: 100 7/2/2026 12:01:54 PM		Tech: J. Horsley - F PC: C. Goff						
Structure ID: B1 REV.B													
P1		P.I.P. BY OTHERS - BTM SLAB											
P5) 24" - CASTING HEIGHT - 4.75" P4) 48" - ECC CONE w/ 24" HOLE NO STEP - 24" P3) 60" - MH Transition Slab 48" Hole - 13" P2) 60" - MH RISER Custom Ht - 50" P1) 60" - P.I.P. BY OTHERS - BTM SLAB - 0" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) SPECIAL EXTERNAL COATING - CARBOLINE 300M 2) 60" - DBL 1"x14.5' Butyl (2x) 1) 48" - DBL 1"x14.5' Butyl (2x) 1) PSX - 16M NYLO 2) DOGHOUSE - 16"x22" 154.16 SqFt) Carboline Bitumastic 300M [EXT]						0 lb 1550 lb 1928 lb 4737 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 8 lb 0 lb 0 lb ----- 8223 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY OTHERS. 5. CARBOLINE 300M >>EXTERIOR COATING ONLY<< 6. INVERTS 2 & 3 OFFSET 11" FROM CENTER REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - TRANSITION SLAB (As .31) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18)					
Rim: 670.82' Rim to Invert: 7.15' Slack: 0.05" Sump: 6" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
(P5) (P4) (P3) (P2) (P1) << RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)													

INSIDE WALL DIMENSIONS

(P1)

0°

90°

180°

270°

360°

EXT
X0"
