




THIS DRAWING IS INTENDED TO BE PRINTED IN COLOR.

36" X 36" AL HATCH
SUPPLIED BY OTHERS,
CAST-IN CENTERED

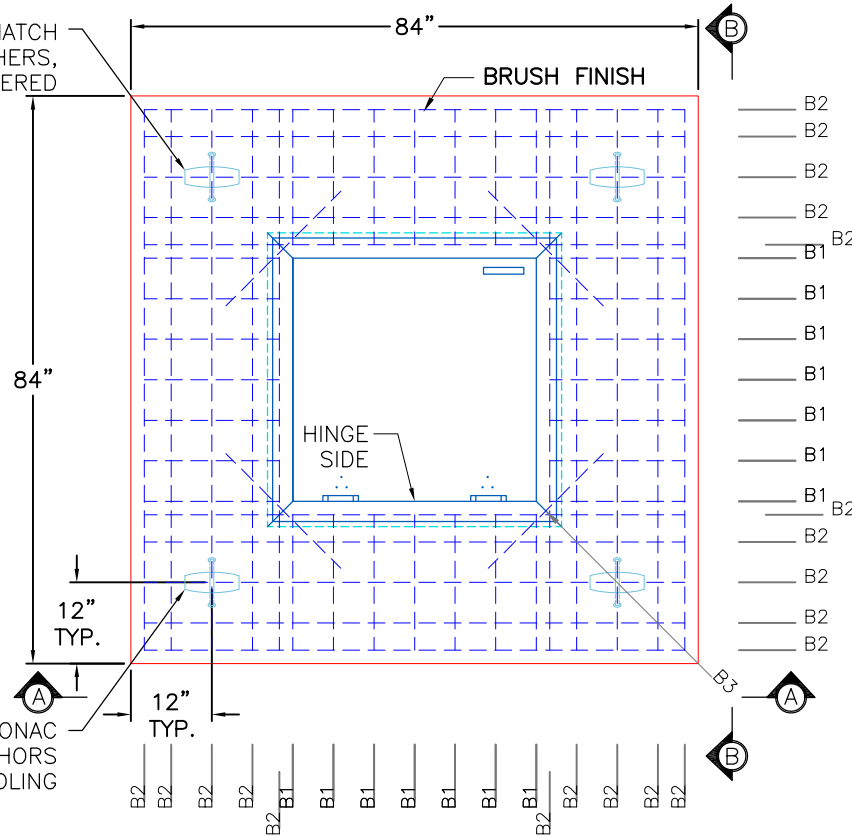

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C.E.W. PER ASTM A615. (GRADE 60).
4. WEIGHT = 3,967 LBS
5. DOUBLE ROLL CS-102 JOINT SEALANT.
6. 36" X 36" AL HATCH SUPPLIED BY OTHERS, CAST-IN CENTERED.

REBAR TAKEOFF SUMMARY

BAR | SIZE | LENGTH | QTY

B1	#5	20 in (1'-8")	28 pcs
B2	#5	80 in (6'-8")	16 pcs
B3	#5	24 in (2'-0")	4 pcs

Total Pieces: 52 Pcs

Total Footage: 188.00 LF

Total Weight: 196.09 lbs (0.098 Tons)

TYP SPA = #5 BARS AT 6" C.C.E.W.

PRODUCTION WORK ORDER



QUALITY CONTROL CHECKLIST

- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ HATCH CORRECT LOCATION.
- ☐ REINFORCING CORRECT.
- ☐ SURFACE QUALITY ACCEPTABLE.
- ☐ EDGES CHAMFERED.
- ☐ ALL PATCHWORK ACCEPTABLE.

PRODUCT I.D.: BX072072-08LD06-S

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 3,967 LBS

TOP SECTION JOINT: N/A

BASE SECTION JOINT: FLAT

QC CHECK INITIALS:

DESCRIPTION: 84" X 84" X 8" THICK VAULT TOP SLAB

CUSTOMER: CUMBERLAND VALLEY CONSTRUCTORS

PROJECT: RESERVOIR REHABILITATION

STRUCTURE: TYNE VALLEY CHECK VALVE

ORDER NO: 25-4238

PC: A. CHAMBERS

DRAWING: S. FELLETER

DATE: 09/11/26

SCALE: NTS

PG. 1 of 1
