




THIS DRAWING IS INTENDED TO BE PRINTED IN COLOR.

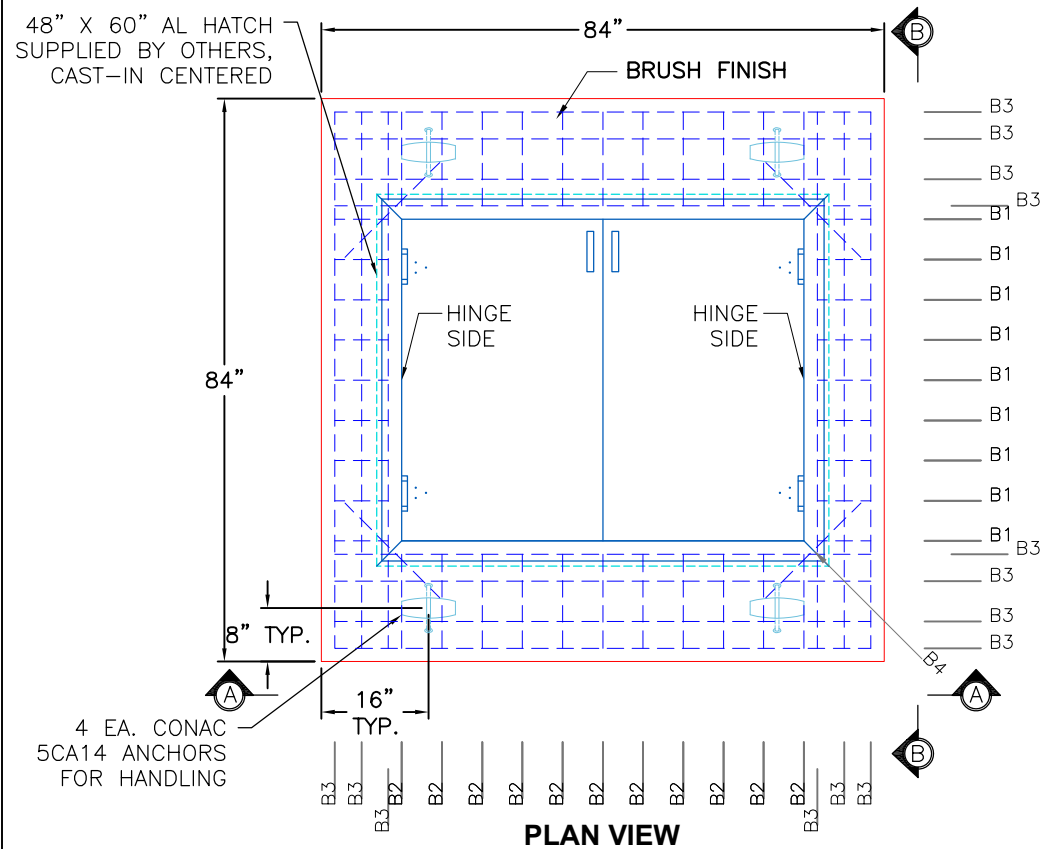

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C.E.W. PER ASTM A615. (GRADE 60).
4. WEIGHT = 2,903 LBS
5. DOUBLE ROLL CS-102 JOINT SEALANT.
6. 48" X 60" AL HATCH SUPPLIED BY OTHERS, CAST-IN CENTERED.

REBAR TAKEOFF SUMMARY

BAR	SIZE	LENGTH	QTY
B1	#5	8 in (0'-8")	18 pcs
B2	#5	14 in (1'-2")	22 pcs
B3	#5	8 in (6'-8")	14 pcs
B4	#5	20 in (1'-8")	4 pcs

Total Pieces: 54 Pcs
Total Footage: 137.67 LF
Total Weight: 143.59 lbs (0.072 Tons)
TYP SPA = #5 BARS AT 6" C.C.E.W.

PRODUCTION WORK ORDER



QUALITY CONTROL CHECKLIST

- | | |
|--------------------------|-----------------------------|
| ☐ | ALL DIMENSIONS CORRECT. |
| ☐ | LIFTERS INSTALLED. |
| ☐ | HATCH CORRECT LOCATION. |
| ☐ | REINFORCING CORRECT. |
| ☐ | SURFACE QUALITY ACCEPTABLE. |
| ☐ | EDGES CHAMFERED. |
| ☐ | ALL PATCHWORK ACCEPTABLE. |

PRODUCT I.D.: BX072072-08LD06-S

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 2,903 LBS.

TOP SECTION JOINT: N/A

BASE SECTION JOINT: FLAT

QC CHECK INITIALS:

DESCRIPTION: 84" X 84" X 8" THICK VAULT TOP SLAB

CUSTOMER:	CUMBERLAND VALLEY CONSTRUCTORS
-----------	--------------------------------

PROJECT:	RESERVOIR REHABILITATION
----------	--------------------------

STRUCTURE: VAULT 6 (MILLS RD. VAULT)

ORDER NO: 25-4238

PC: A. CHAMBERS

DATE: 09/11/26

DRAWING: S. FELLETER

SCAIF: NTS

PG. 1 of 1
