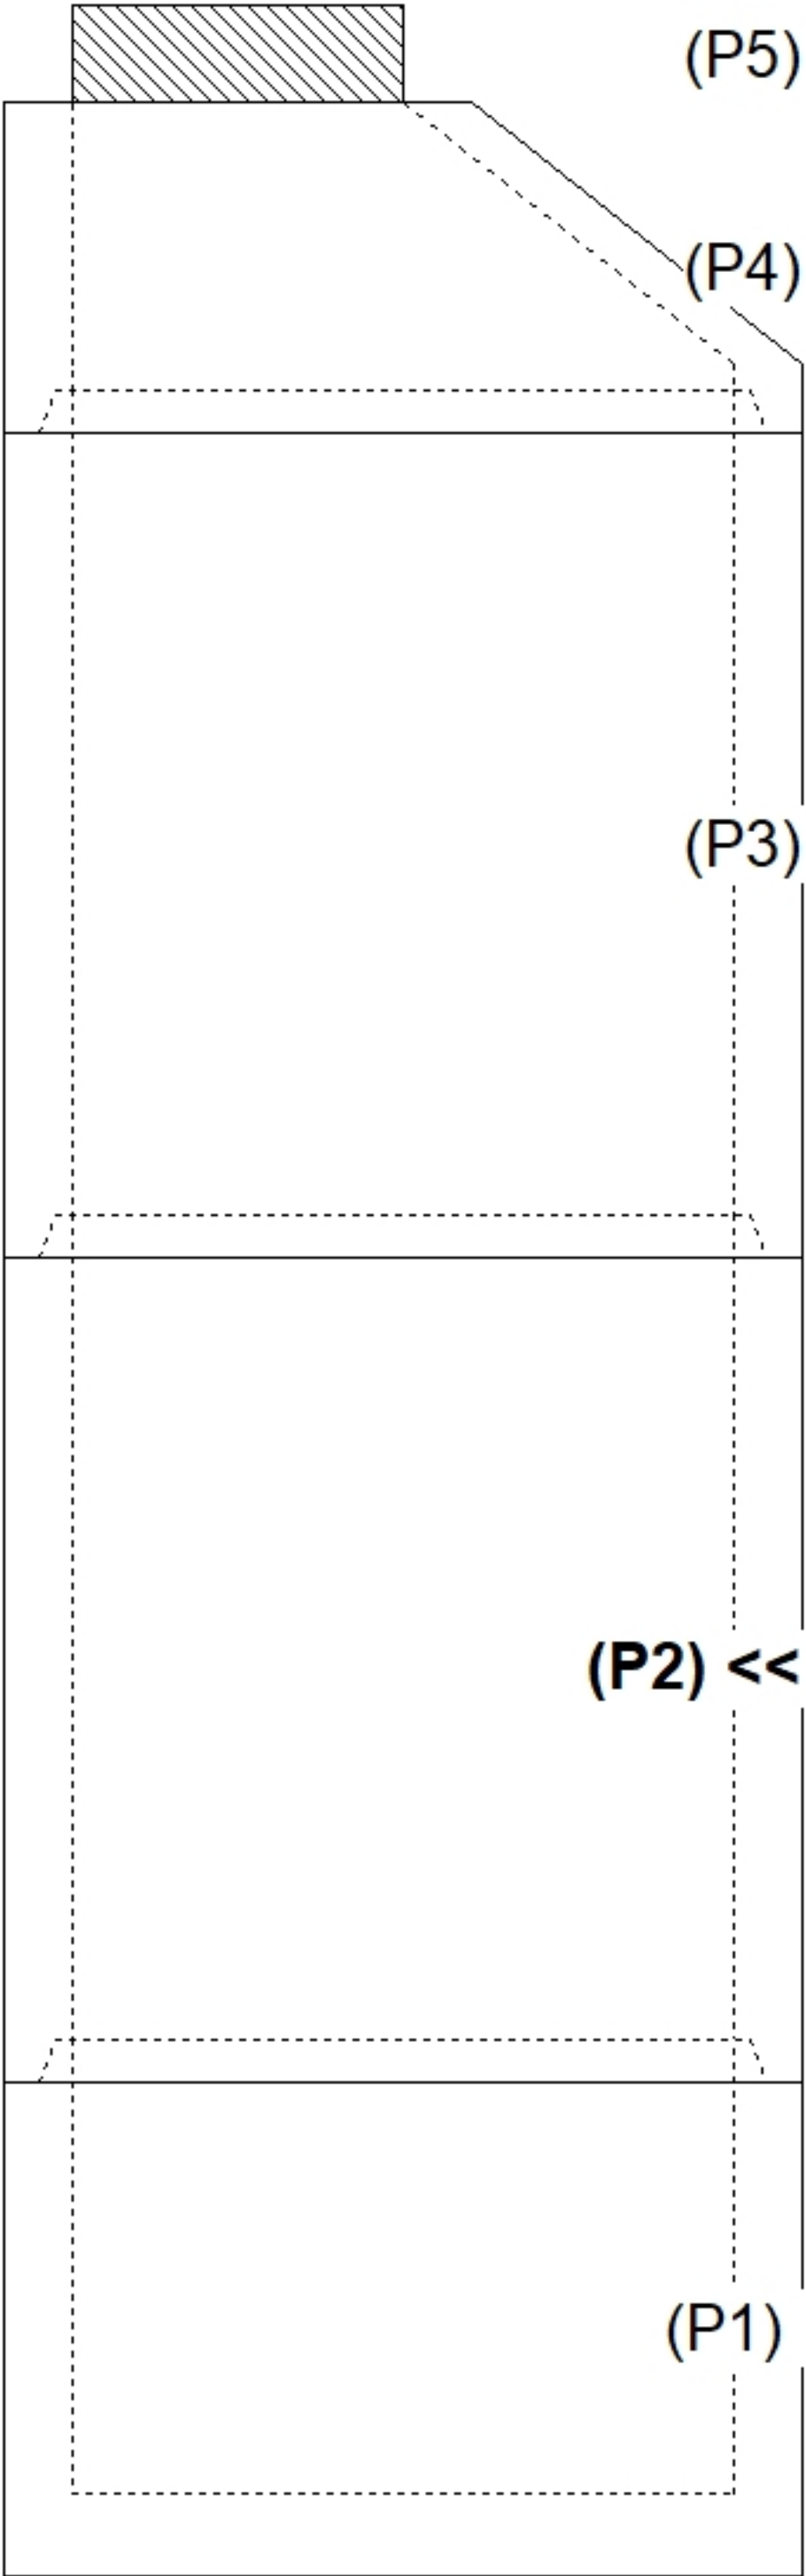
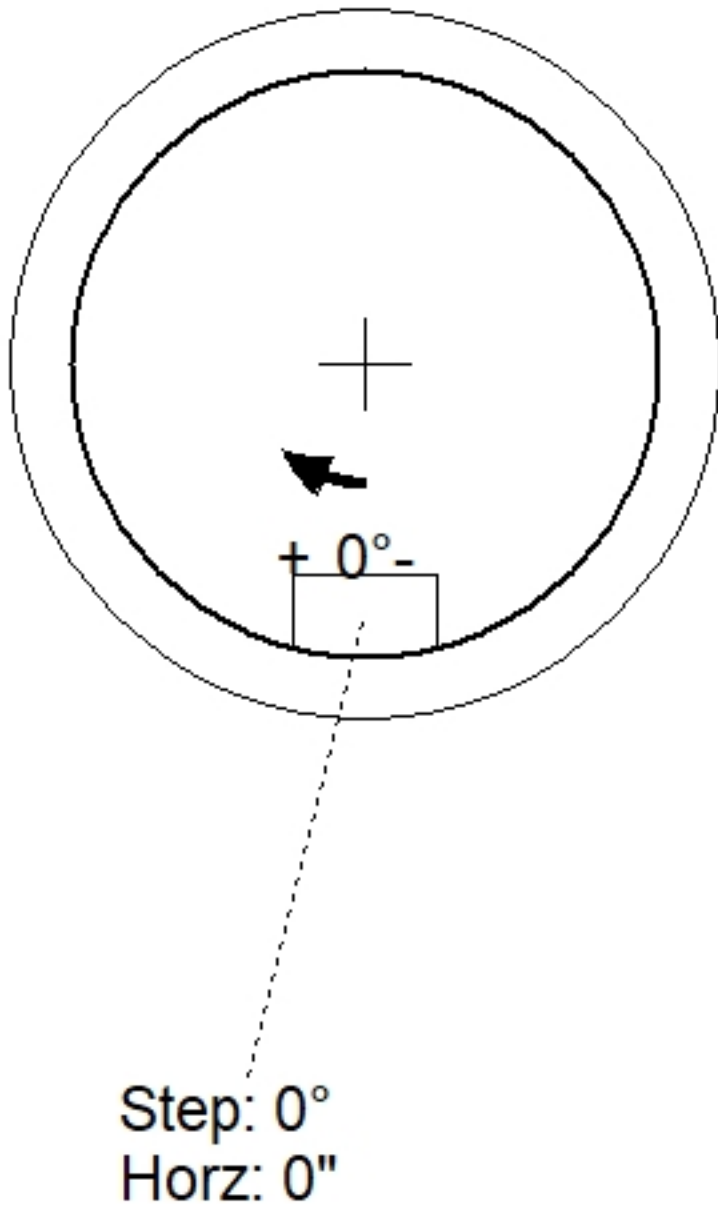
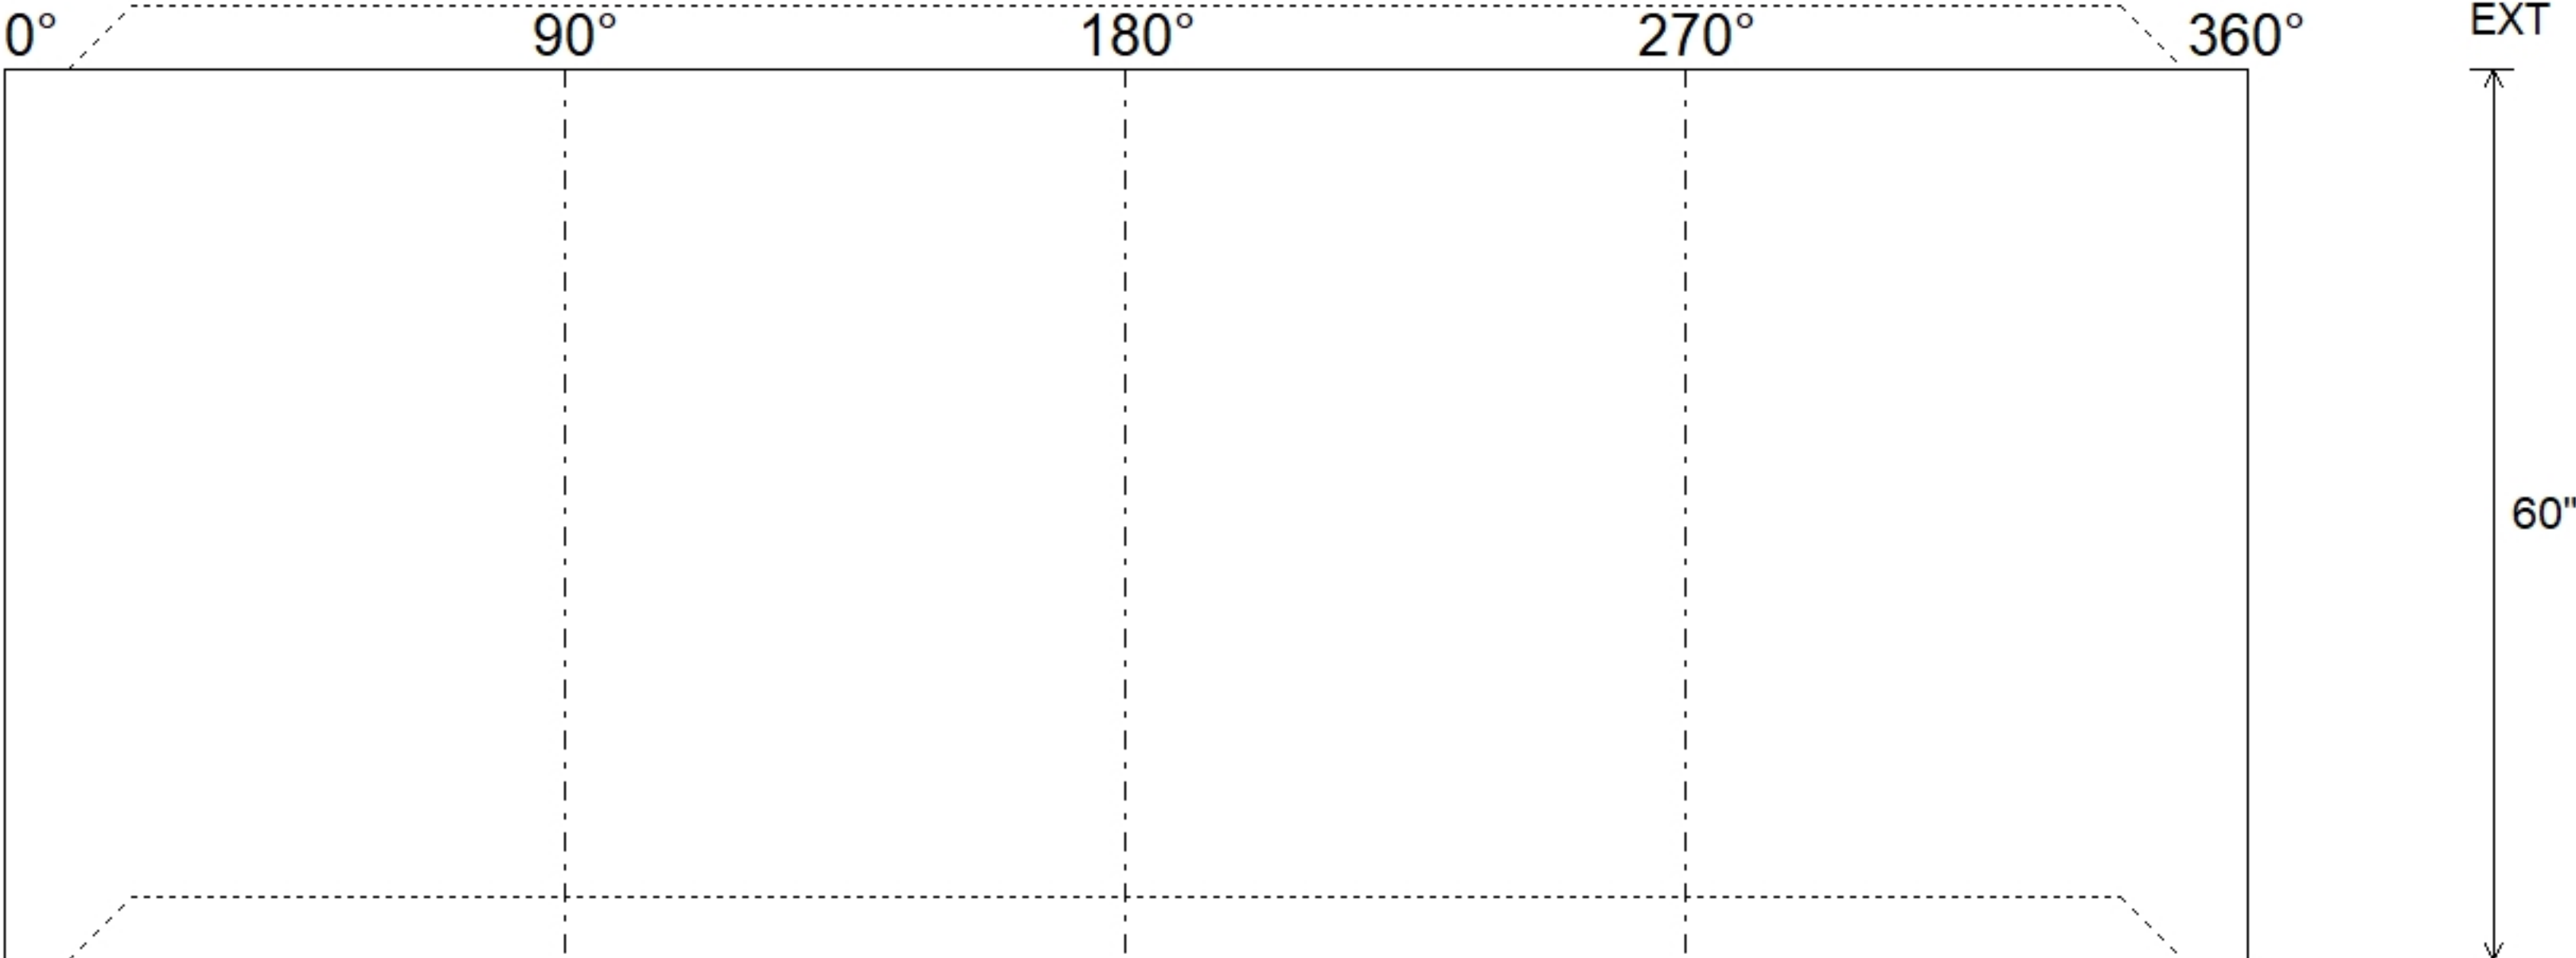


Job Name: 25-4288 - Project Wave Job Location: Franklin, KY 42134 Contractor: Cumberland Pipeline LLC					Plant: 100 9/2/2026 8:41:39 AM		Tech: PC: Erica Bradley						
Structure ID: A12													
P2		MH048RS60X		MH RISER w/XYPEX T/G									
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P3) 48" - MH RISER w/XYPEX T/G - 60" P2) 48" - MH RISER w/XYPEX T/G - 60" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 14) MH Step ML-10-TDS-NCR - 10"						0 lb 1738 lb 4192 lb 4192 lb 3330 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 15158 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST					
Rim: 727.7'		Rim to Invert: 15.11'		Slack: 2.32"		Sump: 2"		Step Position: 0°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
				INSIDE WALL DIMENSIONS									
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 60" Height (Ext): 60"		Weight (Net): 4192 lb Volume (Net): 1.07cu.yd			
