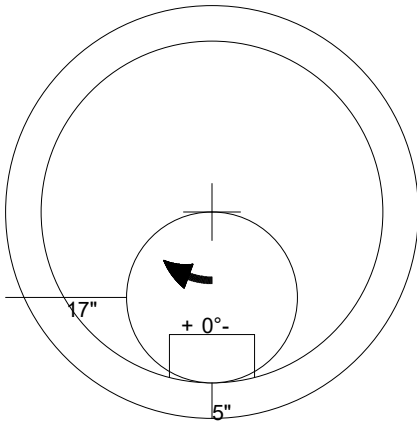



Job Name: 25-4288 - Project Wave		Plant: 100	Tech: Jared - A	
Job Location: Franklin, KY 42134		7/10/2026 8:15:51 AM	PC: Erica Bradley	
Contractor: Cumberland Pipeline LLC				
Structure ID: A14				
P4 MH048CN30X		ECC XYPEX CONE w/ 24" HOLE		
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P3) 48" - MH RISER w/XYPEX - 60" P2) 48" - MH RISER w/XYPEX - 60" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 12-06 NYLO 15) MH Step ML-10-TDS-NCR - 10"		0 lb 1981 lb 4192 lb 4192 lb 2863 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 8 lb 0 lb ----- 14941 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
				
48" - ECC XYPEX CONE w/ 24" HOLE - 30" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 1981 lb Volume (Net): 0.51cu.yd
